

Job Name: 25-1511 Halfhill Estates Ph.3
Job Location: Nicholasville, KY
Contractor: Perdue Environmental Contracting Co., Inc.

PC: J. Jarvis
 TECH: J. Horsley
 Plant: Beaver Dam



Structure ID: **CBI 1903**
 Spec: KYTC
 Type: CBI TYPE A (10')
 Size: 36" x 36"

Rim: 878.83'
 Invert: 870.96'
 Rim to Invert: 7.87'

Sump: 0"
 Floor (Top): 870.96'
 Floor Height: 8"


Floor (Bot): 870.293'
 Overall Height: 8.5'
 Slack: 0.44"

Structure Notes:


- ** KYTC STATE PROJECT **
- PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
 - CONCRETE = 4,000 PI AT 28 DAYS.
 - NO INVERT CHANNEL.
 - CASTING BY ICAST (HOE KY-206 KY TY.1 F/C) CAST INTO TOP SLAB.
- REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:


P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10"	3398 lb
P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18"	5270 lb
P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE T/F - 8"	1235 lb
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58"	7204 lb
1) CASTING - HOE KY-206 F/C (KY TY1)	206 lb
1) 36" x 36" - Conseal CS-102 1.00"	0 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 38	0 lb
1) Hole - 30	0 lb
Structure Total:	17313 lb

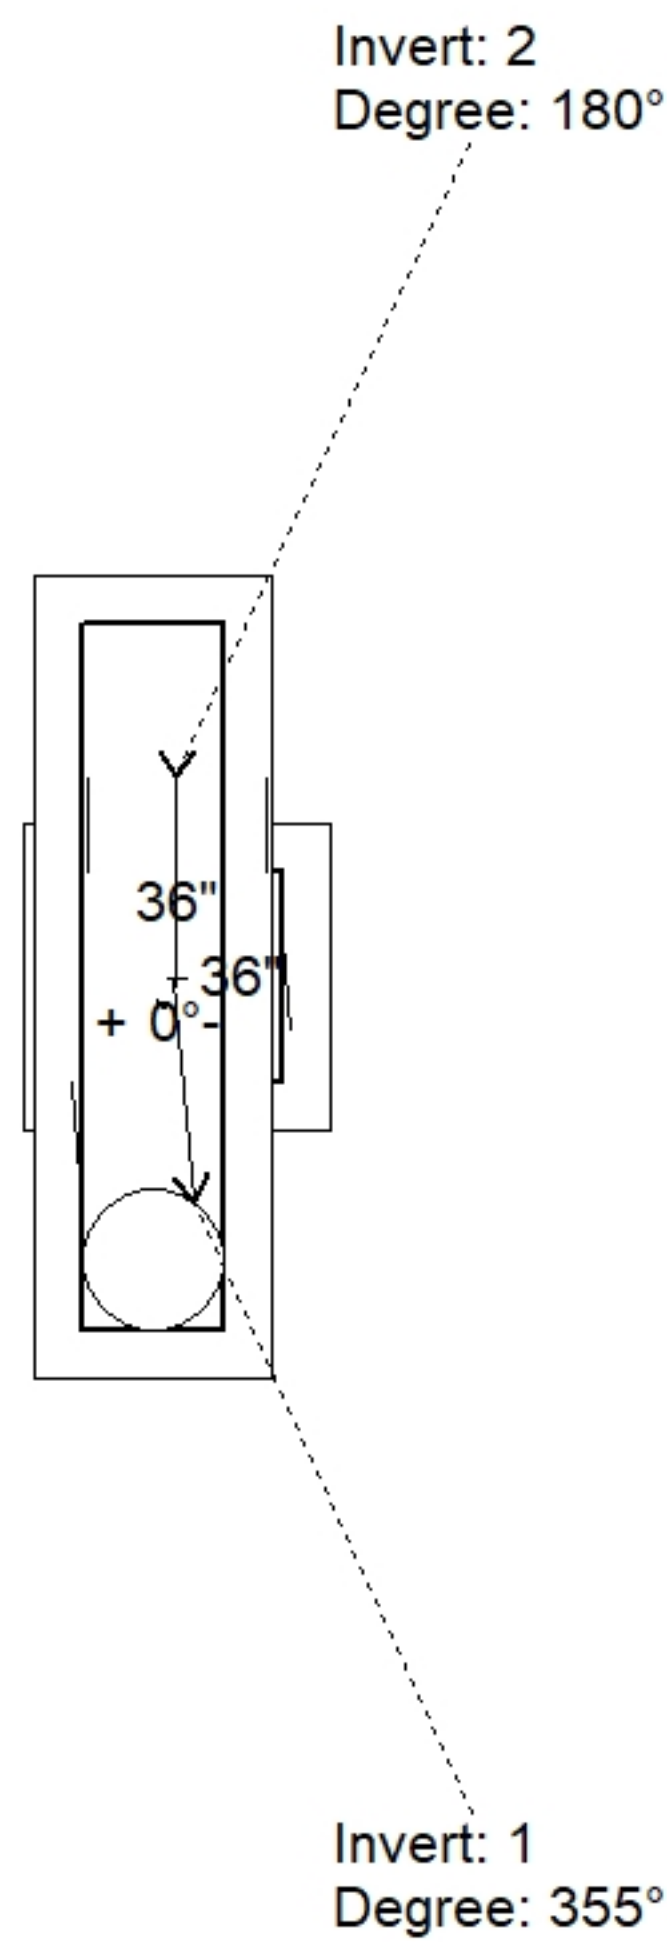

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	878.83'							
Reducer	875.793'							
Invert 1	870.96'	355°	30" HDPE	35.1"	38"	Hole 38	-4"	P1
Invert 2	871.46'	180°	24" HDPE	27.8"	30"	Hole 30	3"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

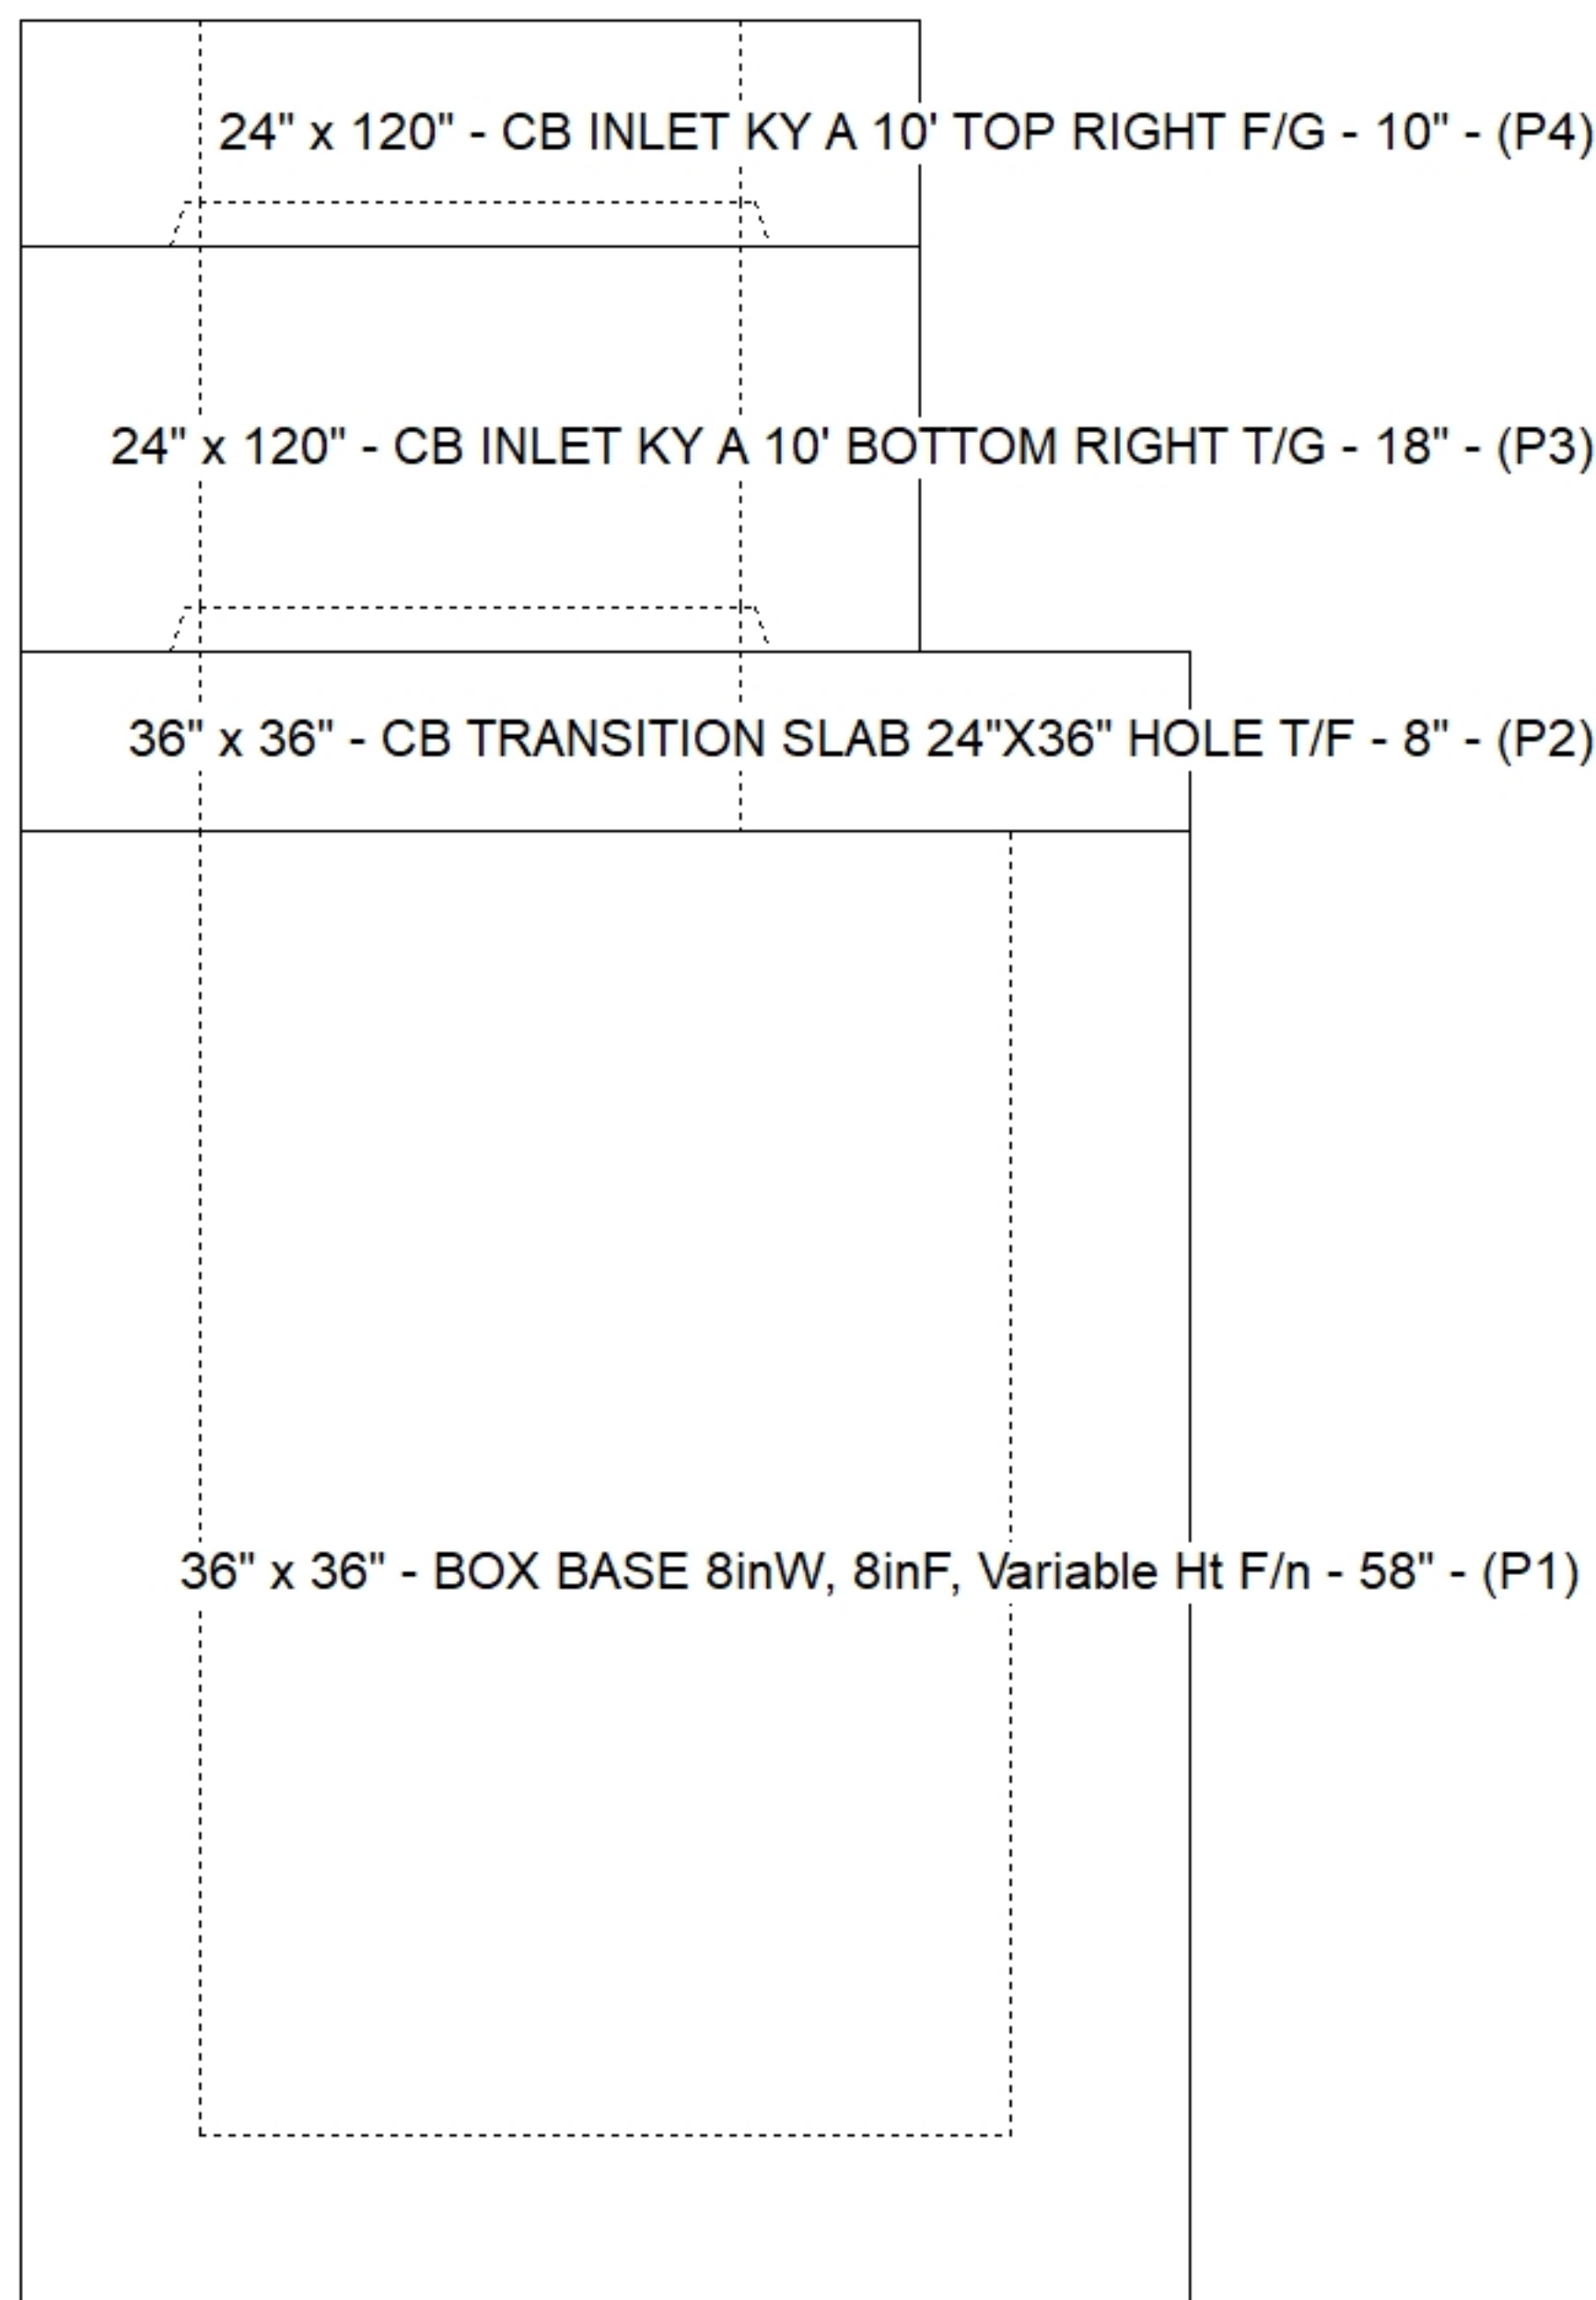

Cast (Int. Dim.) - Interior Dimensions

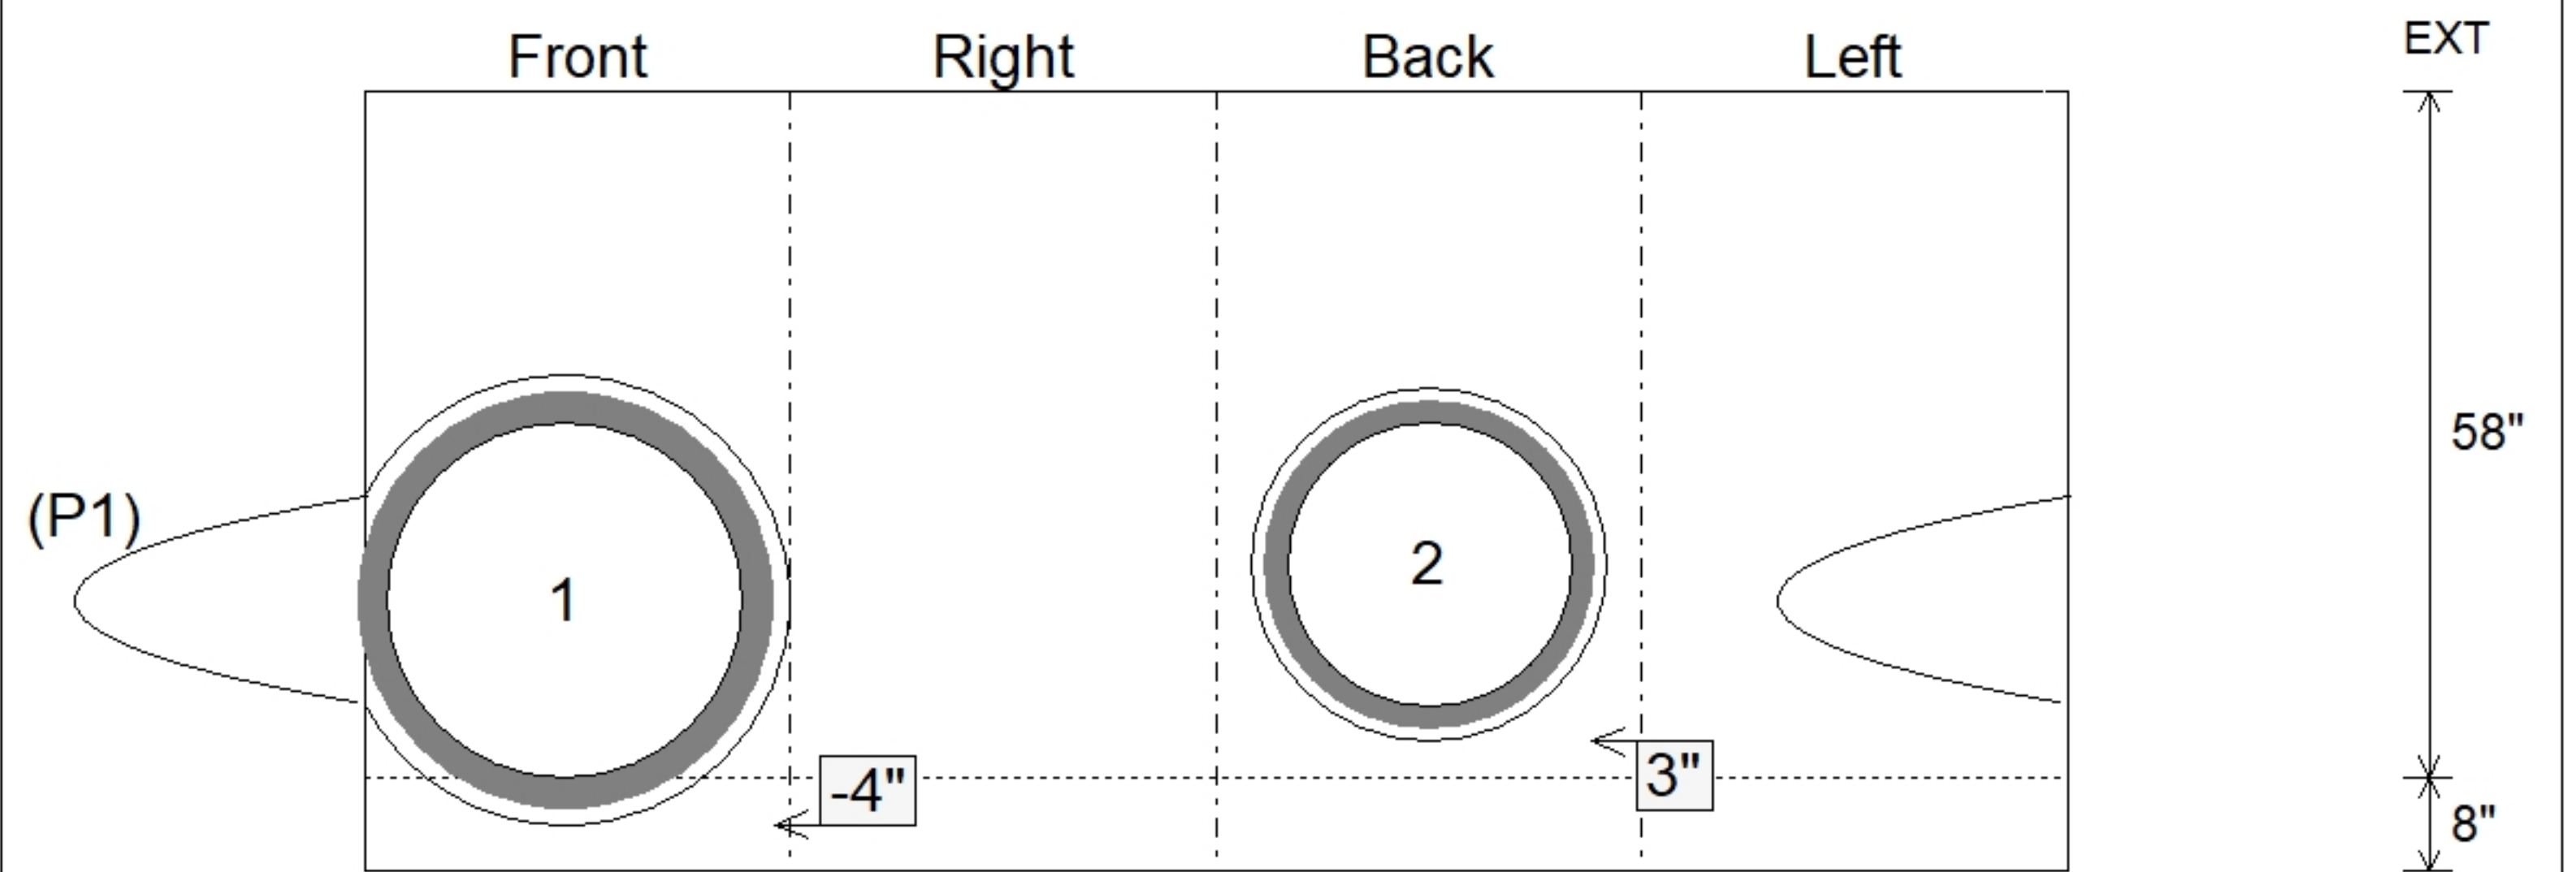

Submittal Drawing
 12/16/2025 4:34:45 PM

SUBMITTAL
 APPROVED BY:
