

**Job Name: 25-1684 KYTC Jefferson Co. Call 200 (251007)**

**Job Location: I-264 Louisville, Ky.**

**Contractor: Cleary Construction, Inc.**

PC: J. Jarvis

TECH: N. Richards

Plant: Beaver Dam, Ky.



Structure ID: 5136+37 RT CBBI-MOD B1

Spec: KYTC

Type: MBI TYPE 9

Size: 24" x 36"

Rim: 558.86'

Invert: 553.76'

Rim to Invert: 5.1'

Sump: 0"

Floor (Top): 553.76'

Floor Height: 8"

Floor (Bot): 553.093'

Overall Height: 5.417'


Slack: 4.2"

**Structure Notes:**


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

**STRUCTURE SUMMARY:**


P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH F/F - 17"	4000 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40"	5052 lb
1) 24" x 36" - Con Seal CS-102 1.00"	0 lb
1) Hole - 22	0 lb
1) Hole - 18	0 lb
<b>Structure Total:</b>	<b>9052 lb</b>

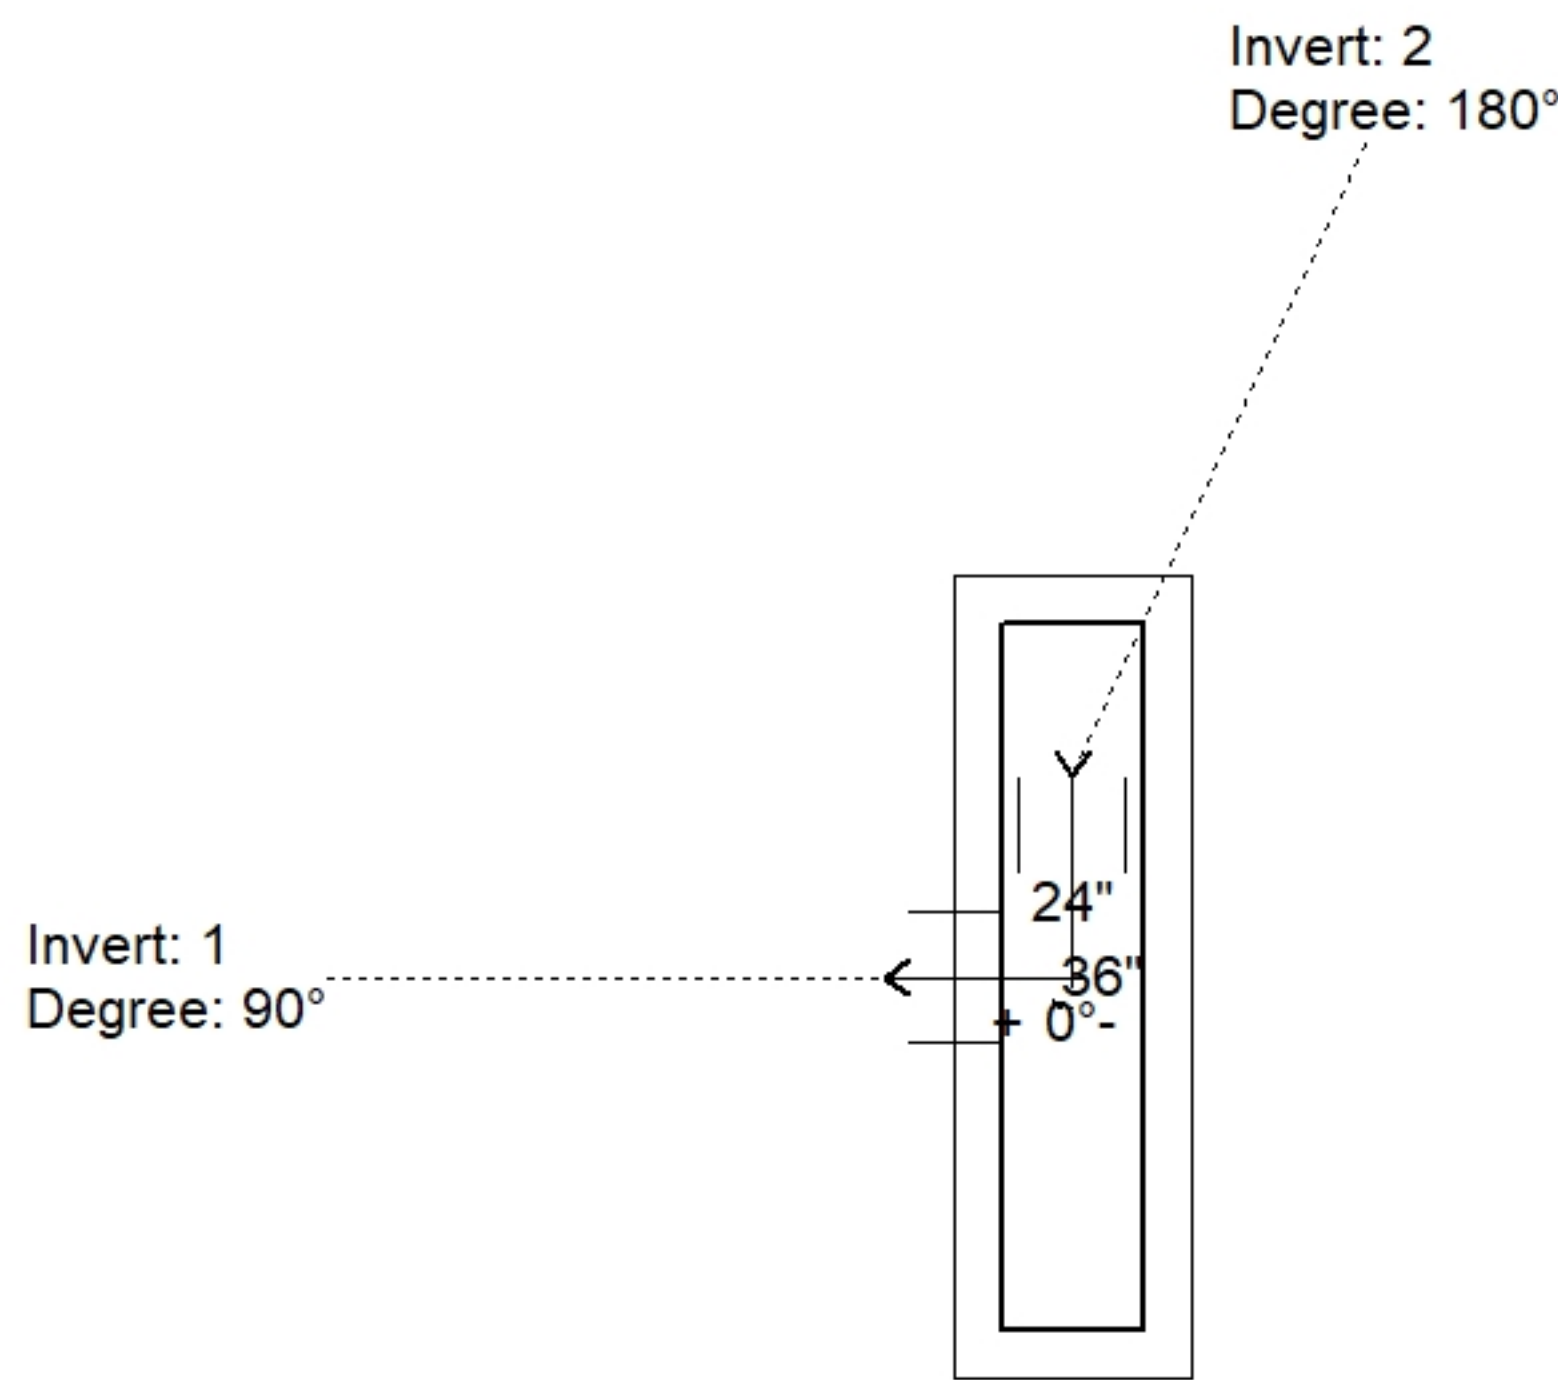

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (L)	Ref
Rim	558.86'							
Reducer								
Invert 1	553.76'	90°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	553.76'	180°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

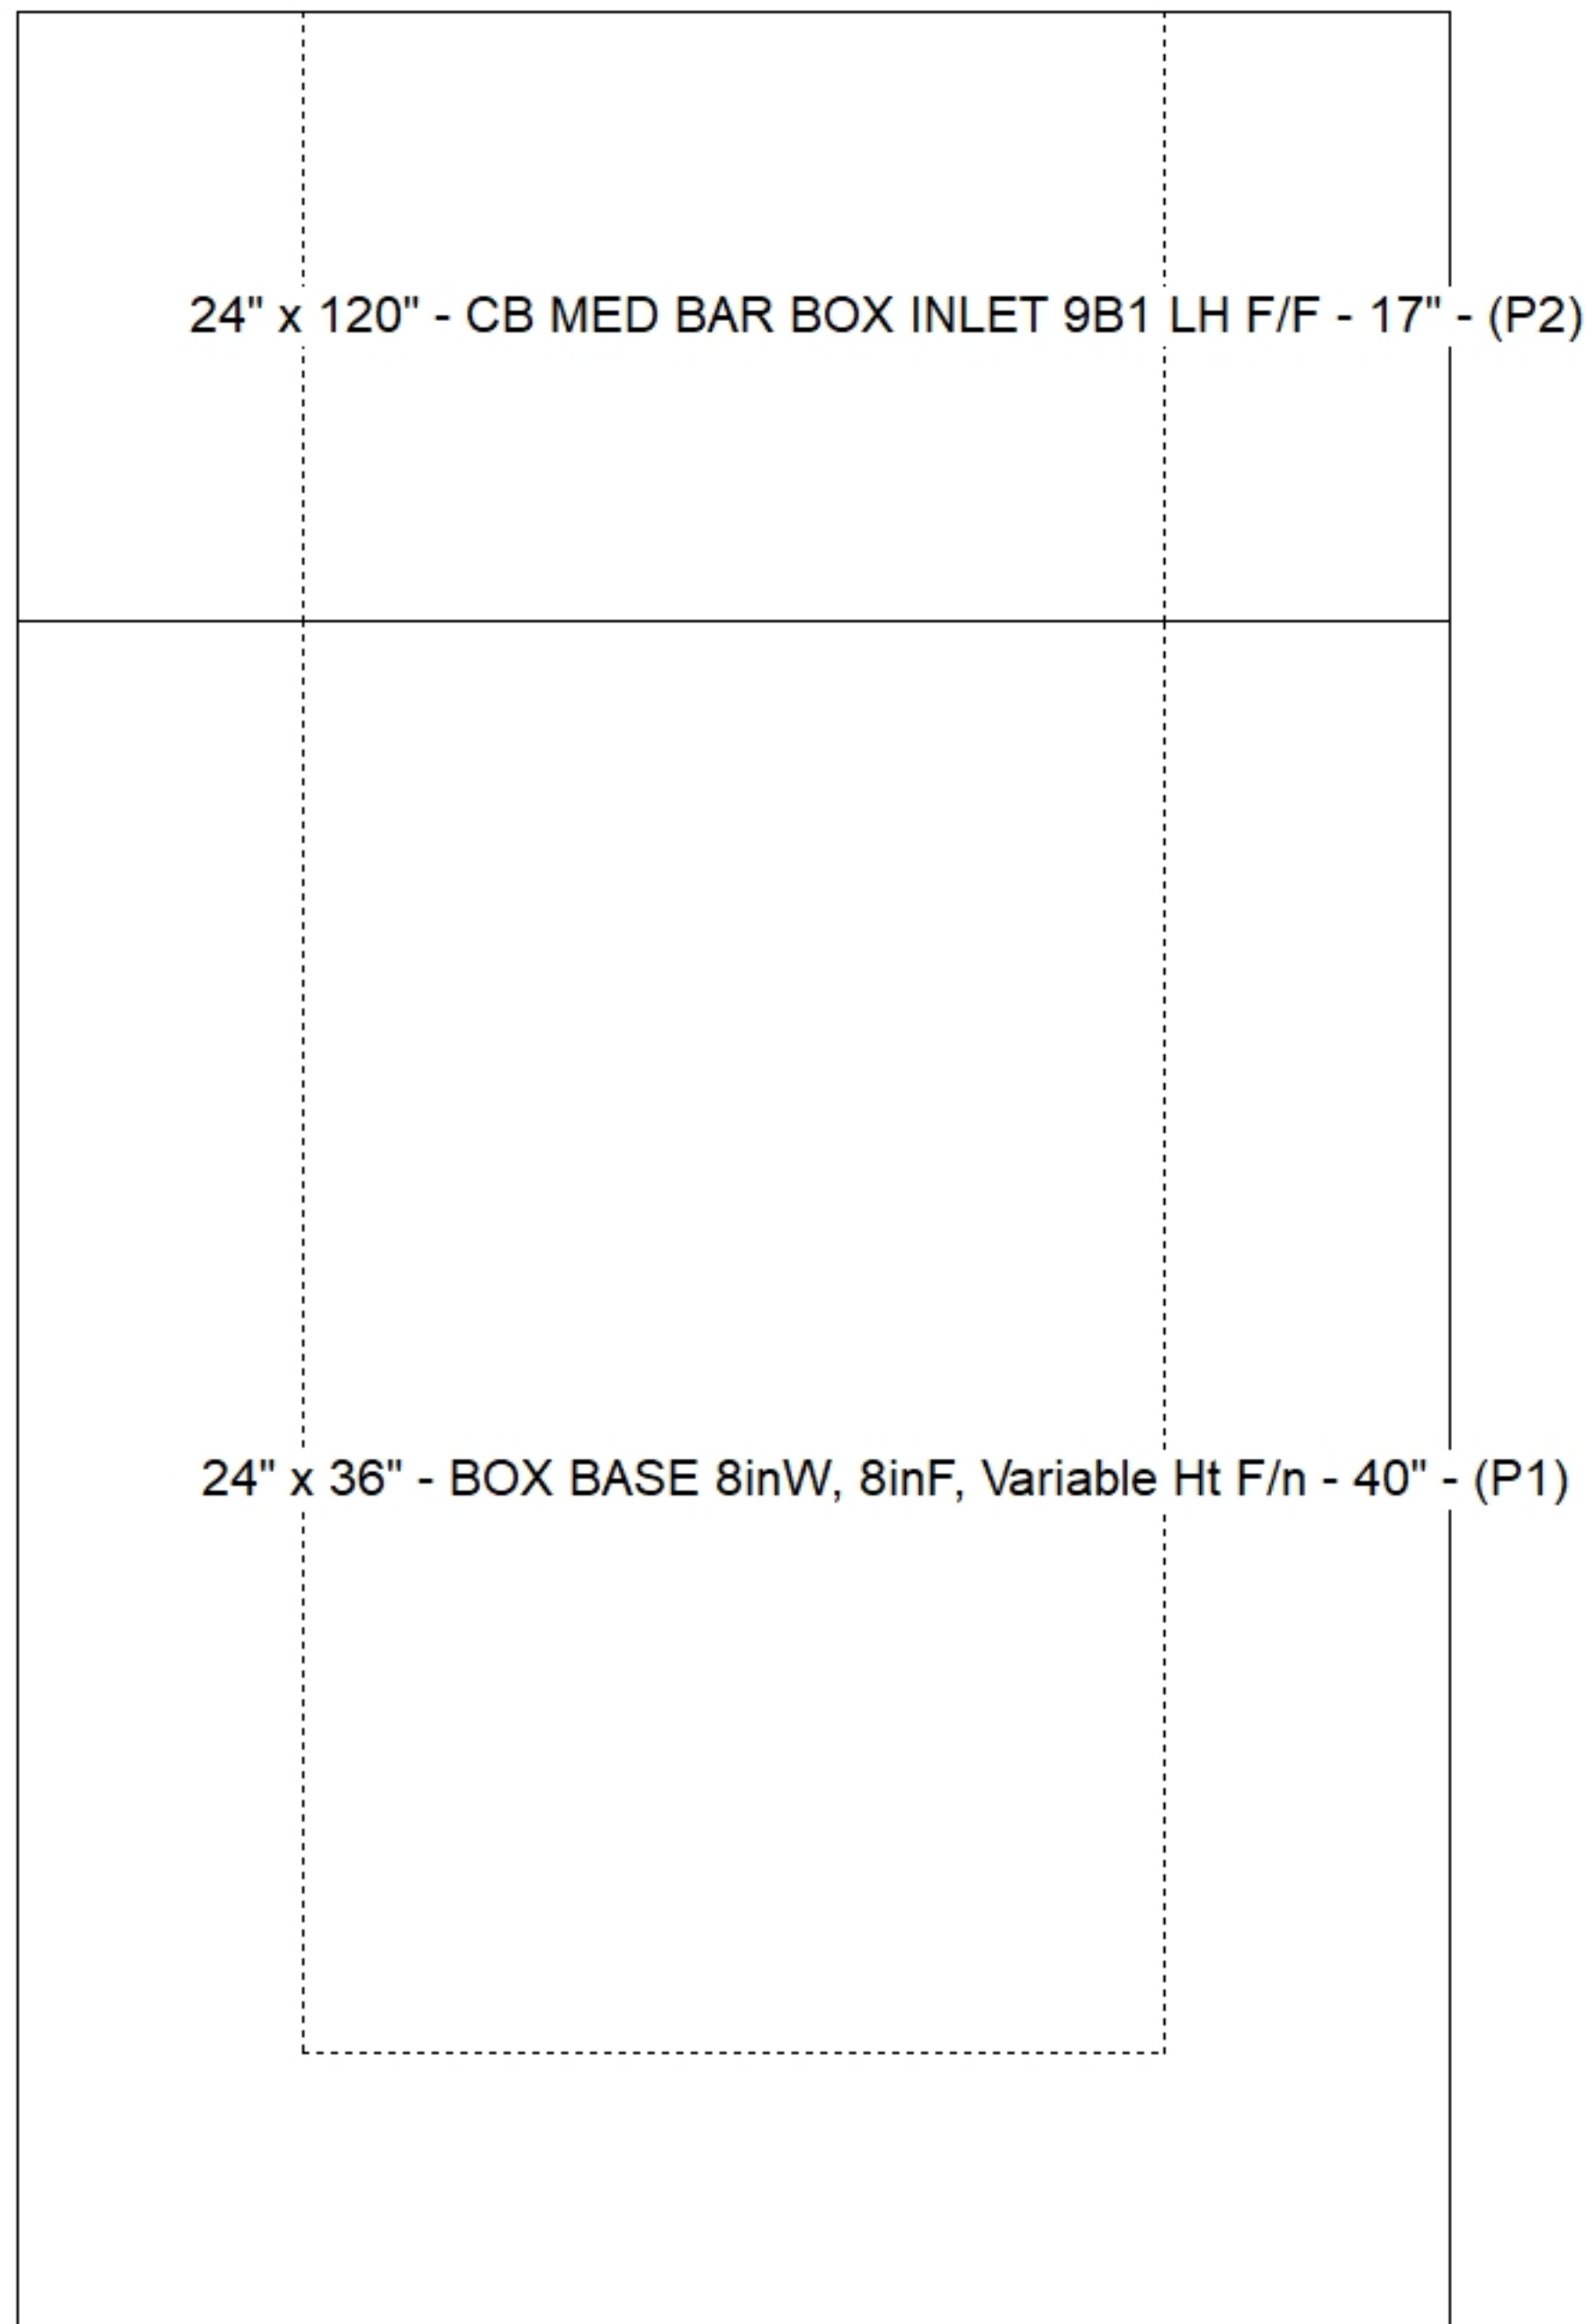

**Cast (Int. Dim.) - Interior Dimensions**

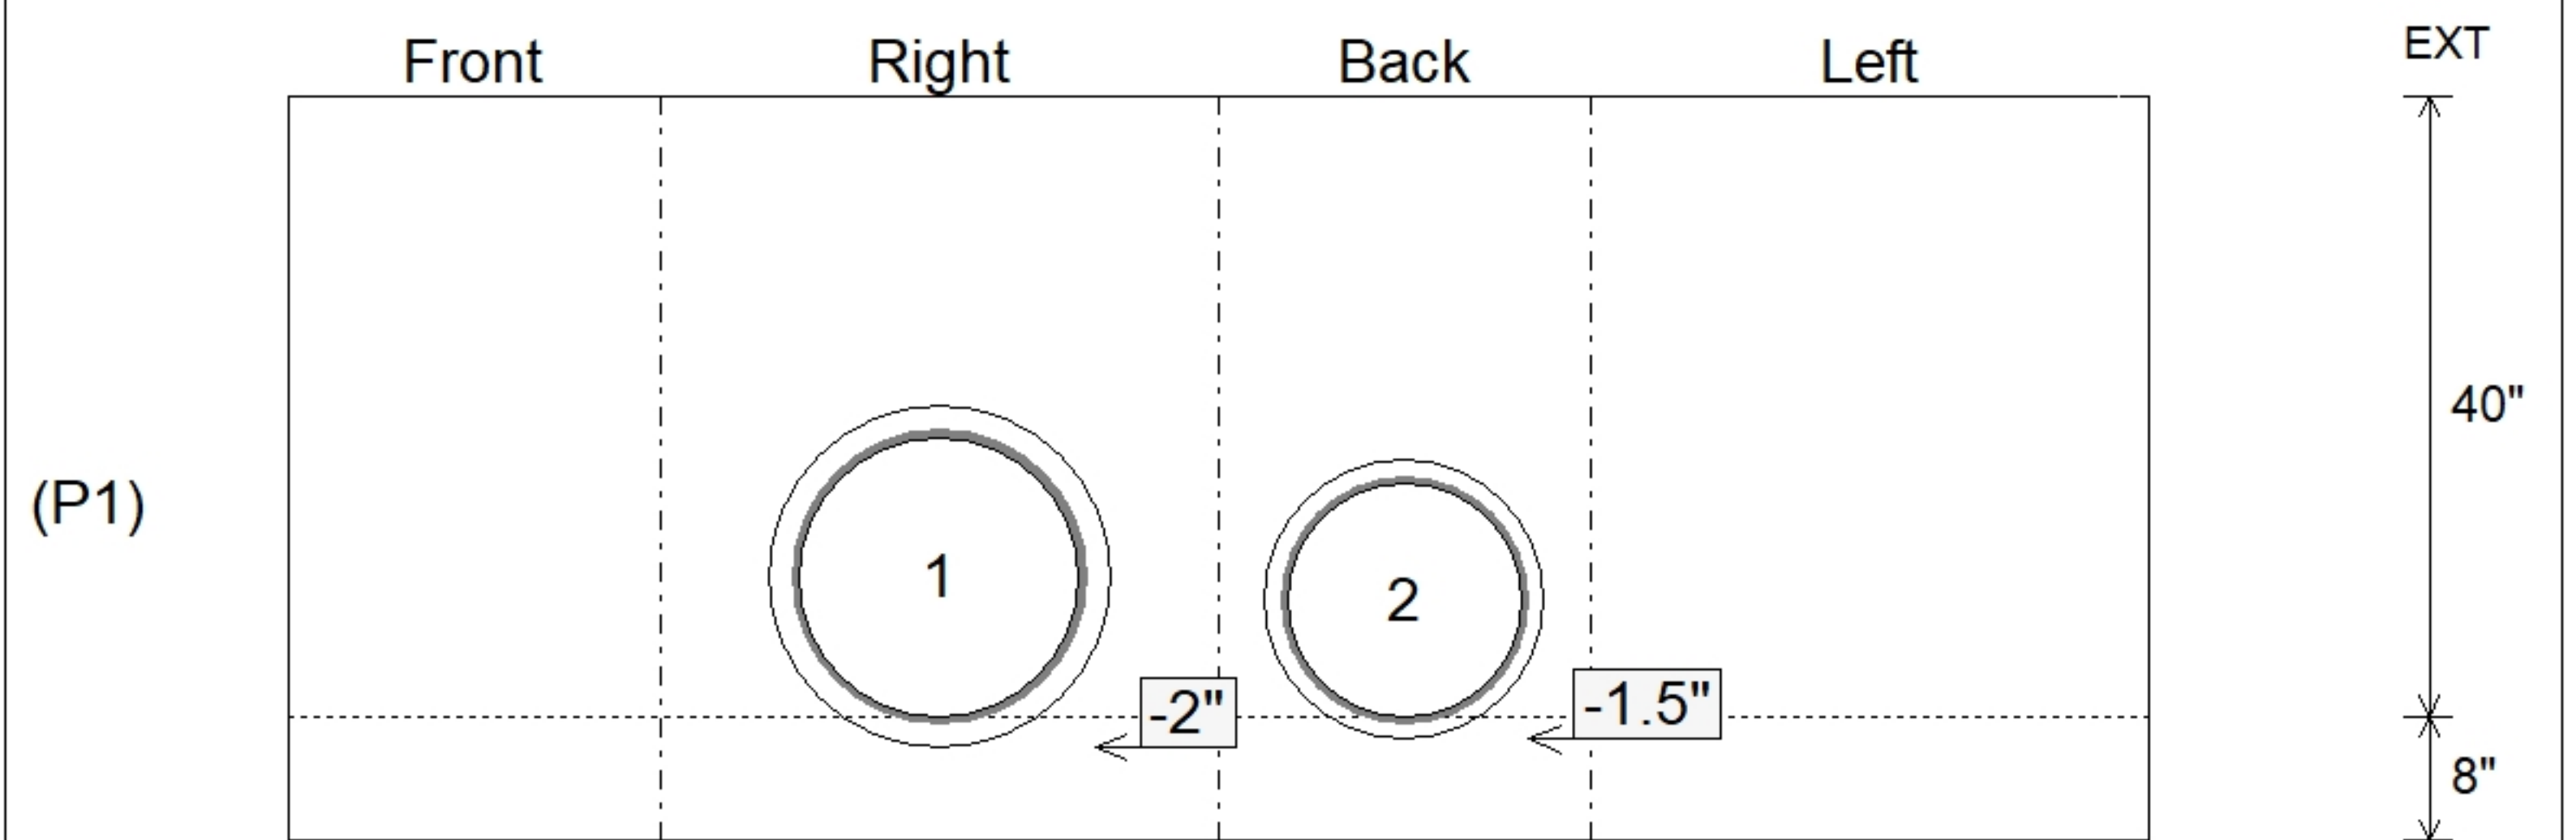

Submittal Drawing  
11/24/2025 2:09:03 PM

SUBMITTAL  
APPROVED BY:
