


Job Name: 25-1684P12 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
6/24/2026 1:33:11 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 1014+08 RT CBIA INLET 14

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht

- P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 29"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22"

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.


Structure Total: 12301 lb

Rim: 588.91' Rim to Invert: 5.11' Slack: 4.32" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	583.8'	135°	31.858"	18" CMP	19"	Hole 22	22"	31.113"	-2"	-10"
Invert 2	583.8'	315°	31.858"	18" CMP	19"	Hole 22	22"	31.113"	-2"	-10"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

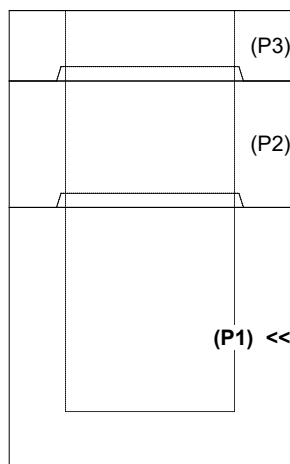


Invert: 1
Degree: 135°
Horz: 15.858"
Hole: 22"
Up(): -2"



Invert: 2
Degree: 315°
Horz: 15.858"
Hole: 22"
Up(): -2"


Invert: 2
Degree: 315°
Horz: 15.858"
Hole: 22"
Up(): -2"



Invert: 1
Degree: 135°
Horz: 15.858"
Hole: 22"
Up(): -2"

INSIDE WALL DIMENSIONS

(P1)

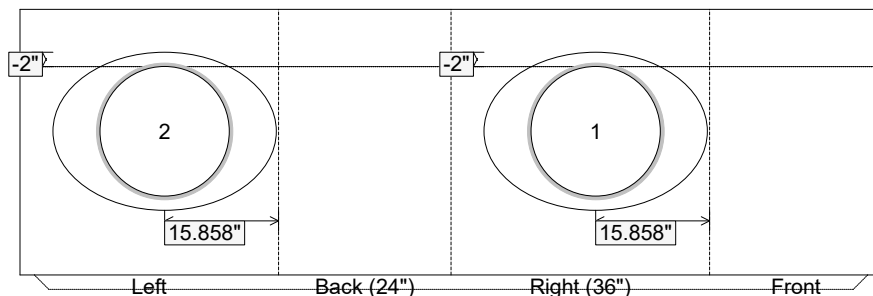

8"
29"
EXT

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 29"
Height (Ext): 37"

Weight (Net): 3634 lb
Volume (Net): 0.93cu.yd
