

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Spec: KYTC
Type: CBI TYPE A (10')
Size: 24" x 36"

Rim: 588.91'	Sump: 0"
Invert: 583.8'	Floor (Top): 583.8'
Rim to Invert: 5.11'	Floor Height: 8"

Floor (Bot): 583.133'
Overall Height: 5.417'
Slack: 4.32"


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 29"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22

3398 lb
5270 lb
3634 lb
0 lb
0 lb

Structure Total: 12301 lb

Invert: 1
Degree: 135°

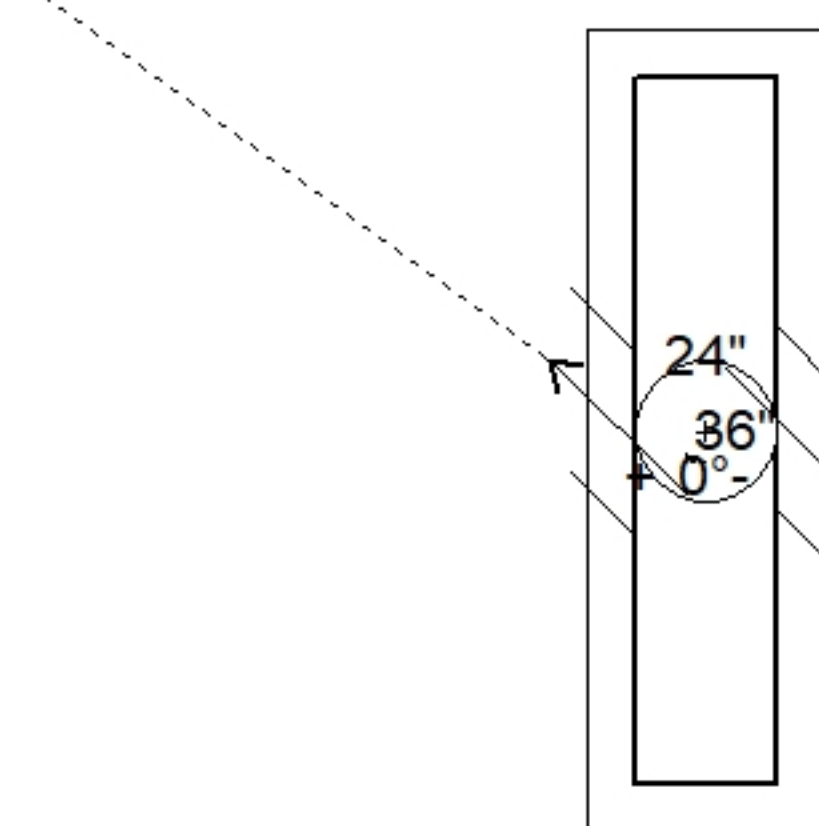

Invert: 2
Degree: 315°


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	588.91'							
Reducer								
Invert 1	583.8'	135°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	583.8'	315°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP RIGHT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 29" - (P1)

Default - Interior Dimensions

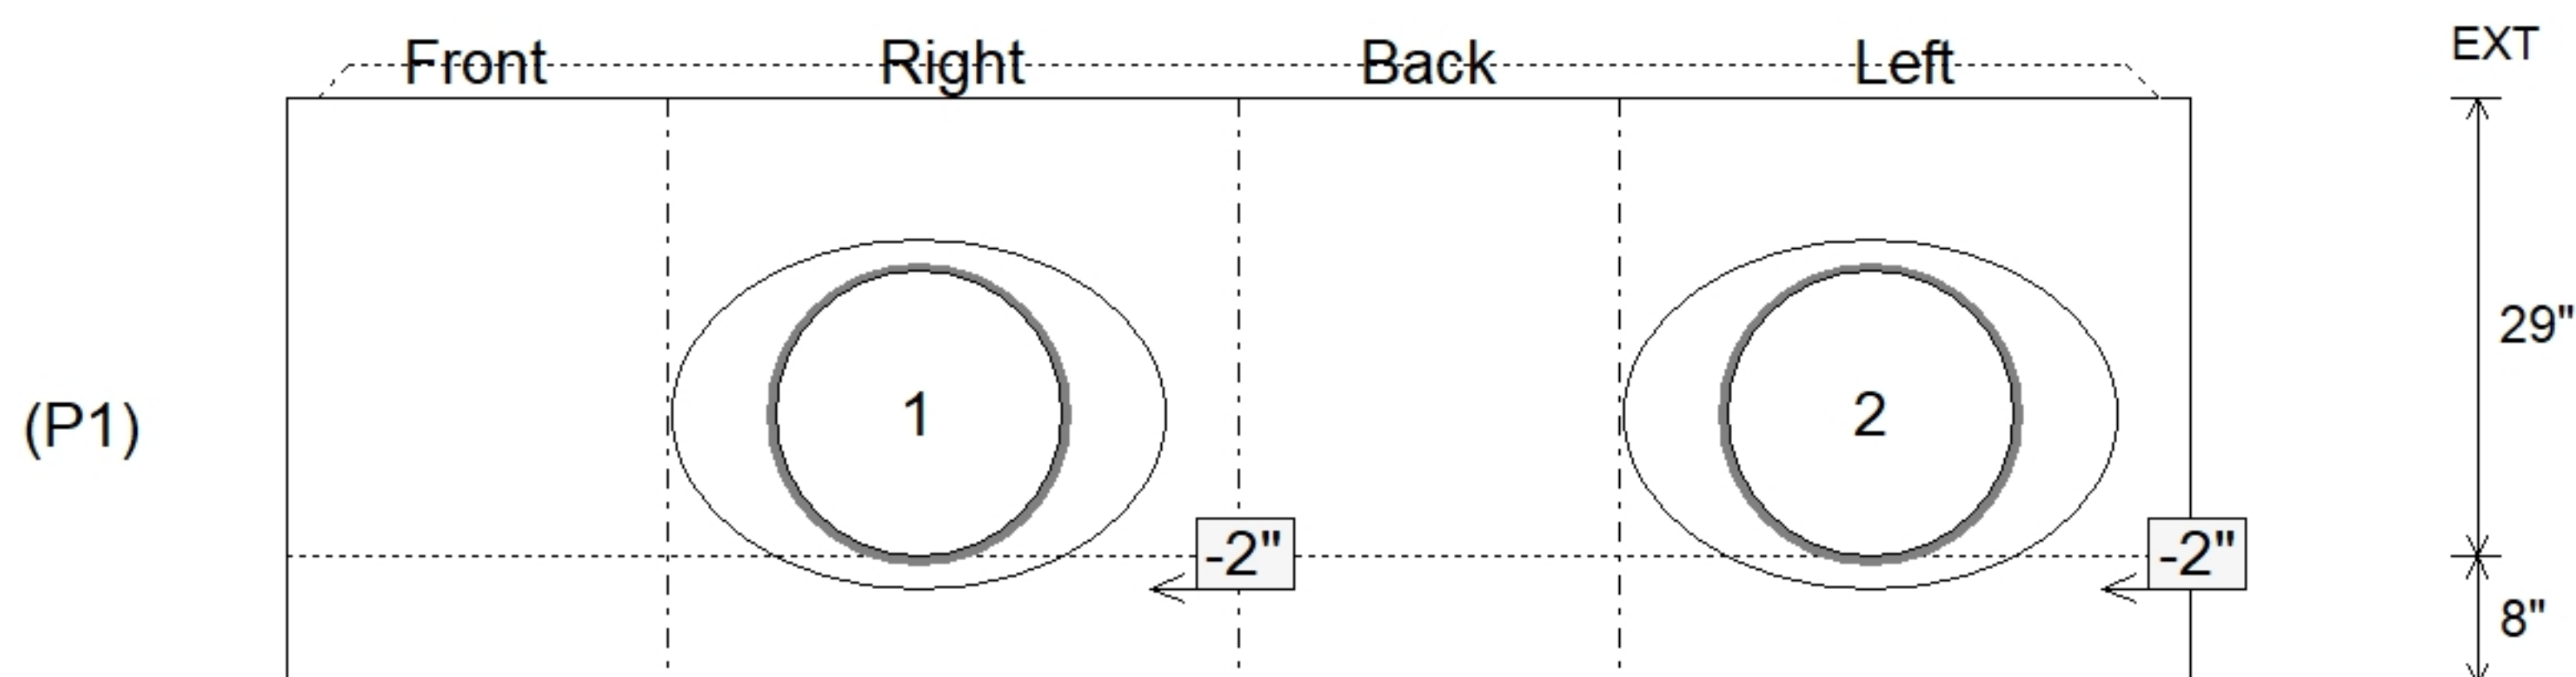

Submittal Drawing
6/24/2026 3:39:20 PM

SUBMITTAL
APPROVED BY:
