

Job Name: 25-1684P12 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

6/24/2026 1:33:05 PM

Tech: J. Coppage

PC: T. Ryan



Structure ID: 1021+10 LT CBIB INLET 20

P1 BX2436-08BA24

BOX BASE 8inW, 8inF

P4) 8" x 120" - CB INLET KY B 10' TOP - 9"
P3) 24" x 120" - CB INLET KY B 10' BOTTOM LEFT - 17"
P2) 24" x 36" - CB FT REDUCER 24"X24" HOLE - 8"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 24"
1) 24" x 36" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 22"

1660 lb
2650 lb
1010 lb
3318 lb
0 lb
0 lb
0 lb

Structure Total: 8638 lb


Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

Rim: 580.68' Rim to Invert: 4.93' Slack: 1.16" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	575.75'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 2	575.75'	110°	29.023"	18" CMP	19"	Hole 22	22"	23.412"	-2"	-4"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

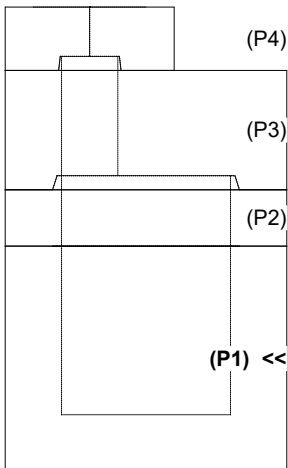

Invert: 2
Degree: 110°
Horz: 18.111"
Hole: 22"
Up(): -2"

Invert: 1
Degree: 0°
Horz: 12"
Hole: 22"
Up(): -2"




Invert: 2
Degree: 110°
Horz: 18.111"
Hole: 22"
Up(): -2"

Invert: 1
Degree: 0°
Horz: 12"
Hole: 22"
Up(): -2"

INSIDE WALL DIMENSIONS

(P1)

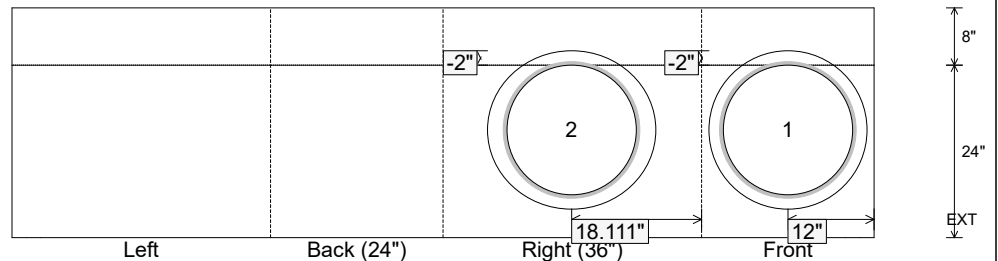

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 24"
Height (Ext): 32"

Weight (Net): 3318 lb
Volume (Net): 0.85cu.yd
