

Job Name: 25-1684P12 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
6/24/2026 1:33:49 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 1021+10 LT CBIB INLET 20

P2 BX024036-08TS024024

CB FT REDUCER 24"X24" HOLE


- P4) 8" x 120" - CB INLET KY B 10' TOP - 9"
P3) 24" x 120" - CB INLET KY B 10' BOTTOM LEFT - 17"
P2) 24" x 36" - CB FT REDUCER 24"X24" HOLE - 8"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 24"
1) 24" x 36" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 22

1660 lb
2650 lb
1010 lb
3318 lb
0 lb
0 lb
0 lb


Structure Total: 8638 lb

Structure Notes:

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

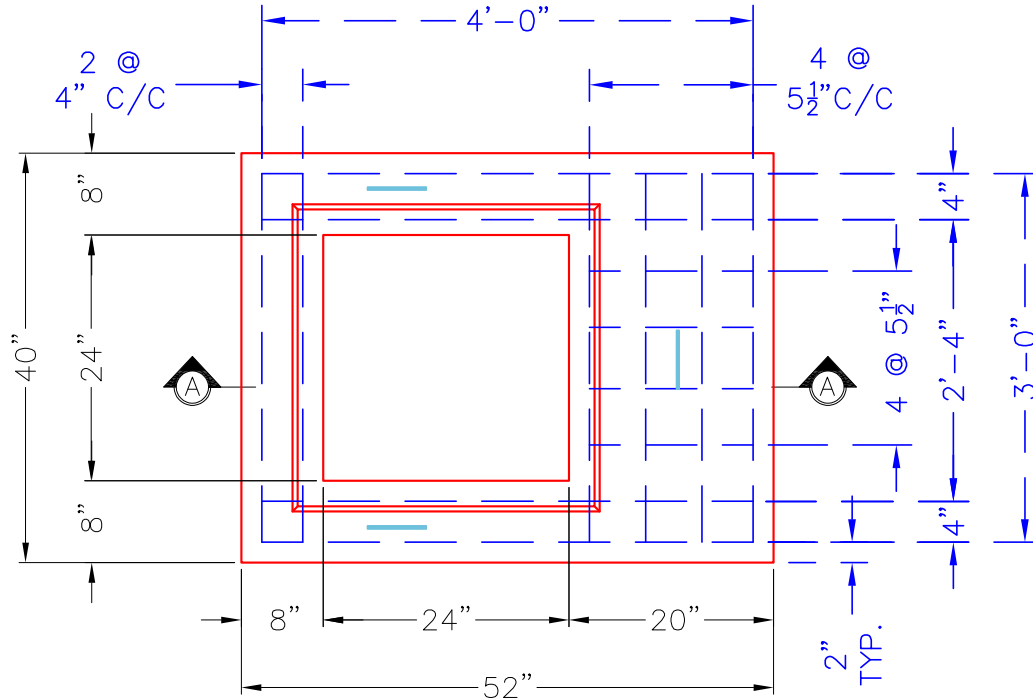

PLAN VIEW

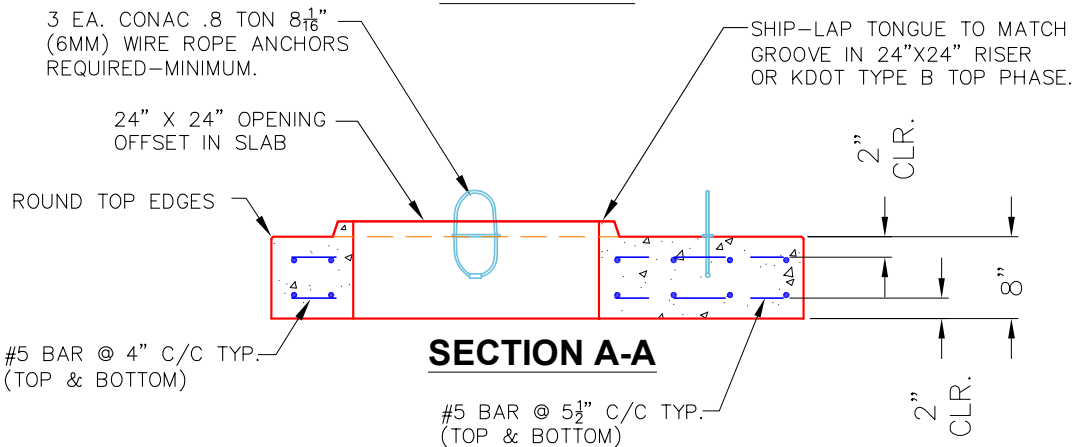

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURED TO KYTC & ASTM C-913 SPECIFICATIONS.
- REINFORCING: #5 BAR AS SHOWN-GRADE 60. (T&B LAYER)
- KYTC STATE CERTIFICATIONS REQUIRED.
- 3 EA. CONAC WIRE LIFTING LOOPS REQUIRED (MIN.)

#5 BAR CUT LIST

- 8 EA. @ 48" LG.
- 12 EA. @ 36" LG.
- 8 EA. @ 16" LG.

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1010 lb
Volume (Net): 0.26cu.yd
