

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	




Slack: 1.16"


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

P4) 8" x 120" - CB INLET KY B 10' TOP - 9"	1660 lb
P3) 24" x 120" - CB INLET KY B 10' BOTTOM LEFT - 17"	2650 lb
P2) 24" x 36" - CB FT REDUCER 24"X24" HOLE - 8"	1010 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF - 24"	3318 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) 24" x 24" - Conseal CS-102 1.00"	0 lb
2) Hole - 22	0 lb


Structure Total: 8638 lb

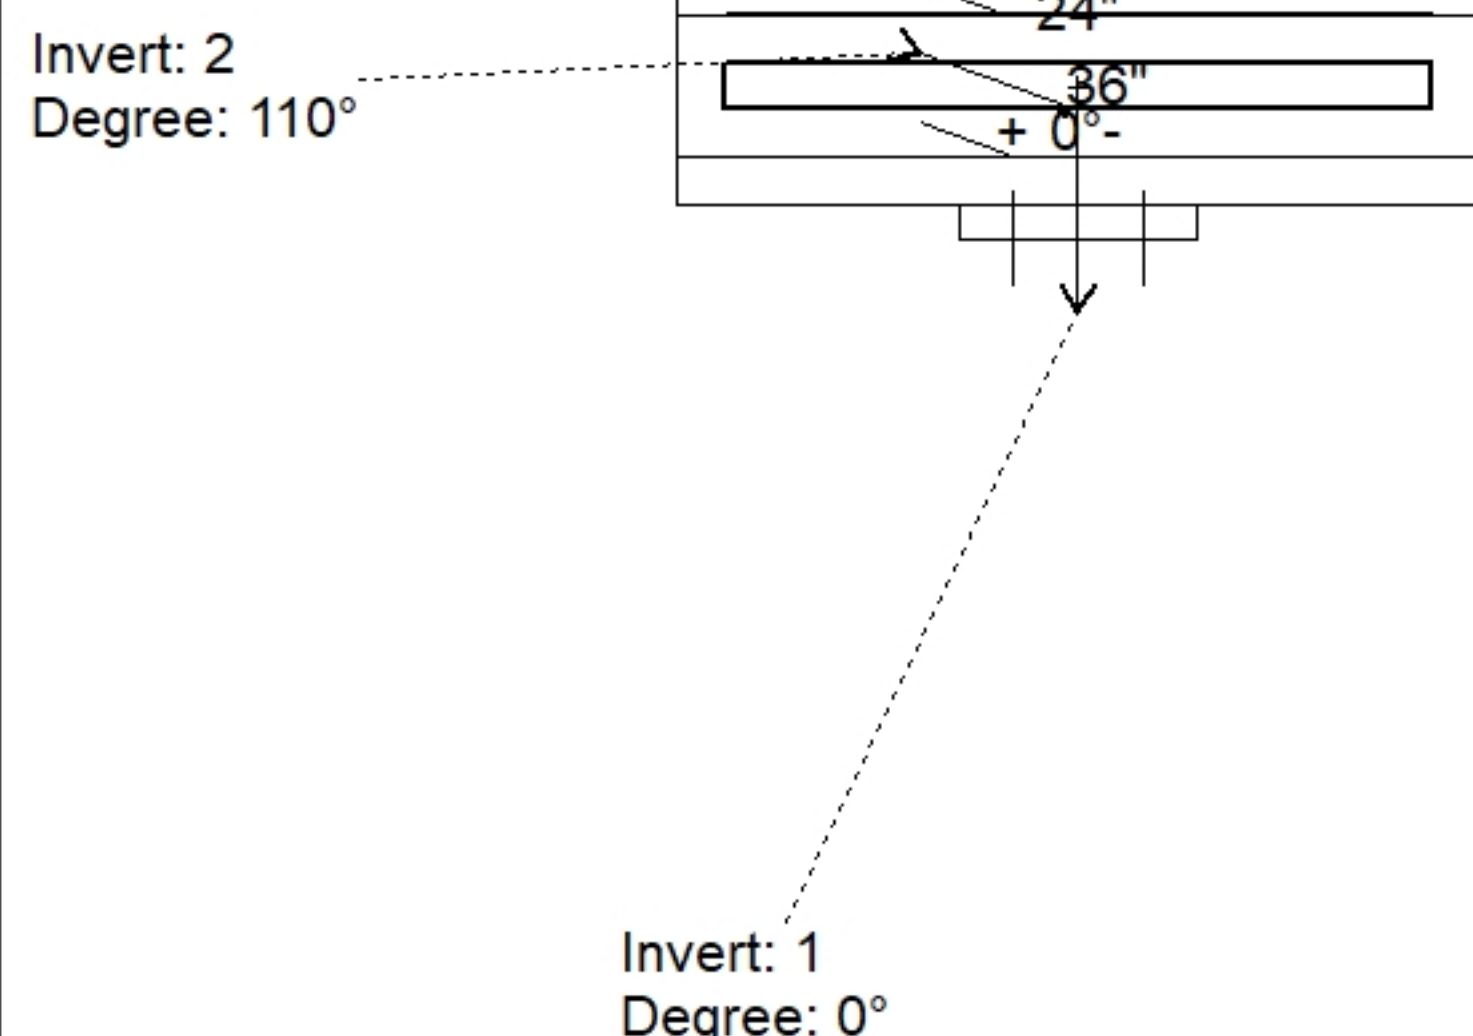

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	580.68'							
Reducer	577.75'							
Invert 1	575.75'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	575.75'	110°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

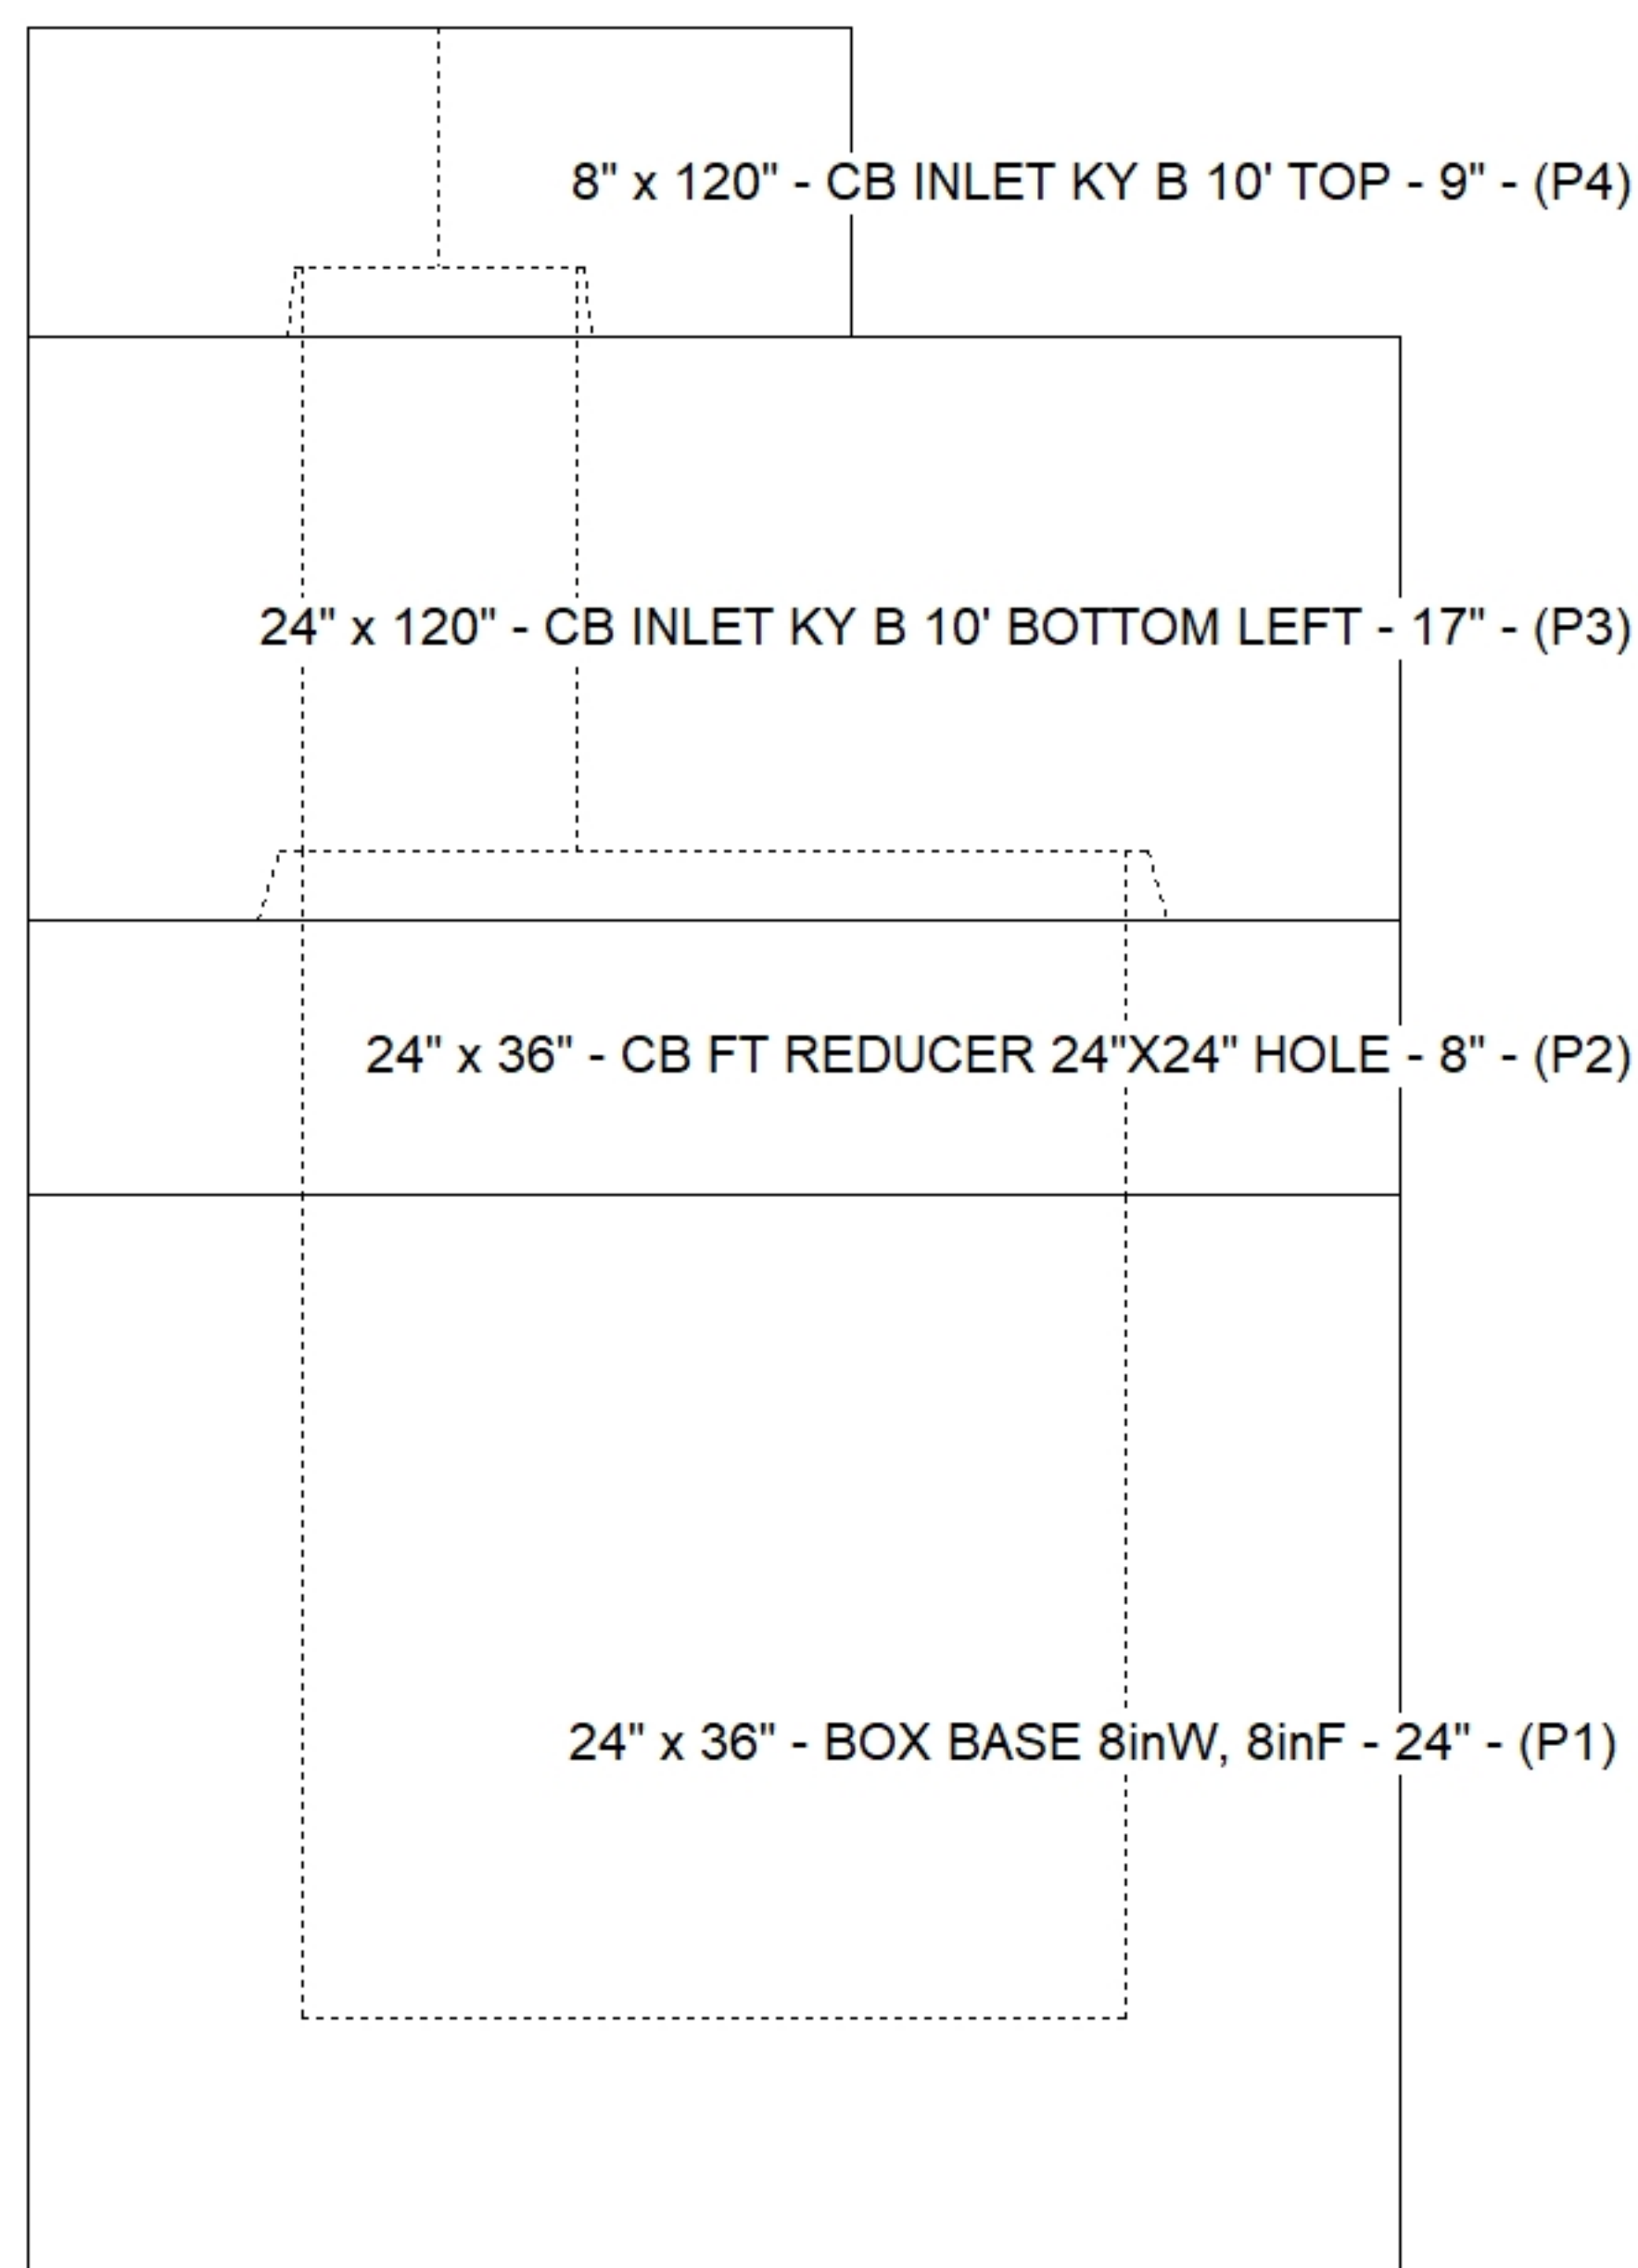

Default - Interior Dimensions

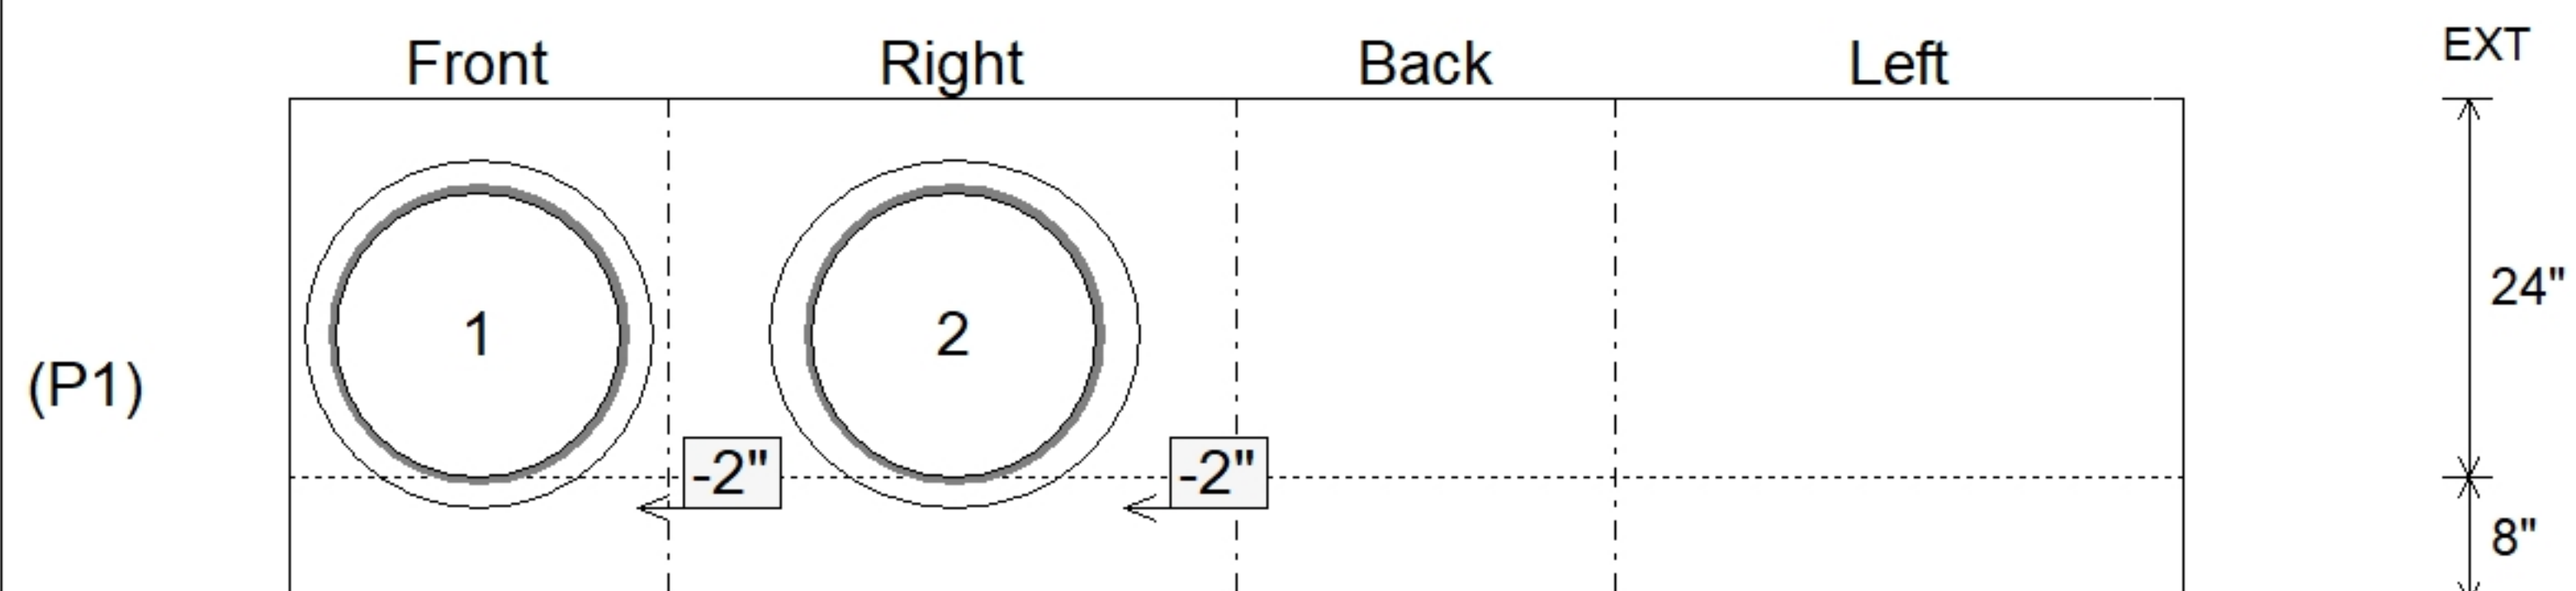

Submittal Drawing
6/24/2026 3:39:18 PM

SUBMITTAL
APPROVED BY:
