


Job Name: 25-1684P12 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
6/24/2026 1:33:12 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 119+10 LT CBIA INLET 16

P1 BX2436-08BA30

BOX BASE 8inW, 8inF

P3) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22"

3400 lb
5270 lb
4193 lb
0 lb
0 lb

Structure Total: 12863 lb


Structure Notes: .
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

Rim: 591.2' Rim to Invert: 5.18' Slack: 4.16" Sump: 0" Step Position:



Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	586.02'	75°	24.782"	18" CMP	19"	Hole 22	22"	22.776"	-2"	4"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

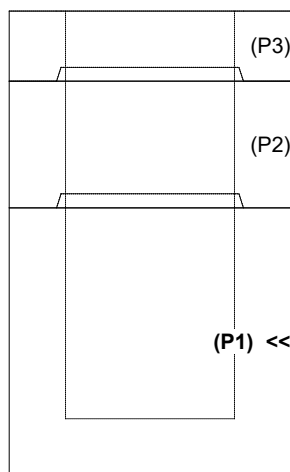


Invert: 1
Degree: 75°
Horz: 18.926"
Hole: 22"
Up(_): -2"



Invert: 1
Degree: 75°
Horz: 18.926"
Hole: 22"
Up(_): -2"

INSIDE WALL DIMENSIONS

(P1)

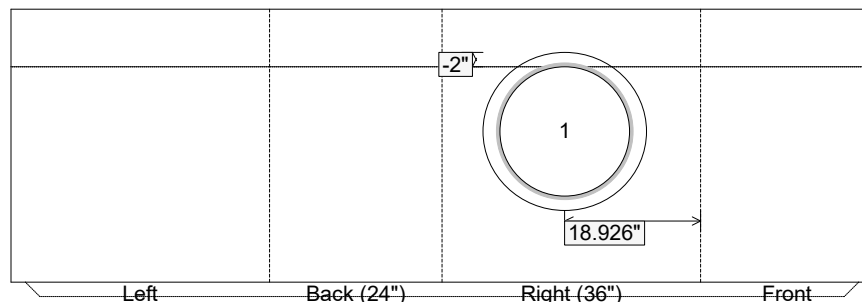

8"
30"
EXT

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 30"
Height (Ext): 38"

Weight (Net): 4193 lb
Volume (Net): 1.07cu.yd
