

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Size: 24" x 36"

Rim to Invert: 4.91'

Floor Height: 8"


Slack: 4.92"

-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

P3) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 18

3400 lb
5270 lb
3878 lb
0 lb
0 lb


Structure Total: 12548 lb

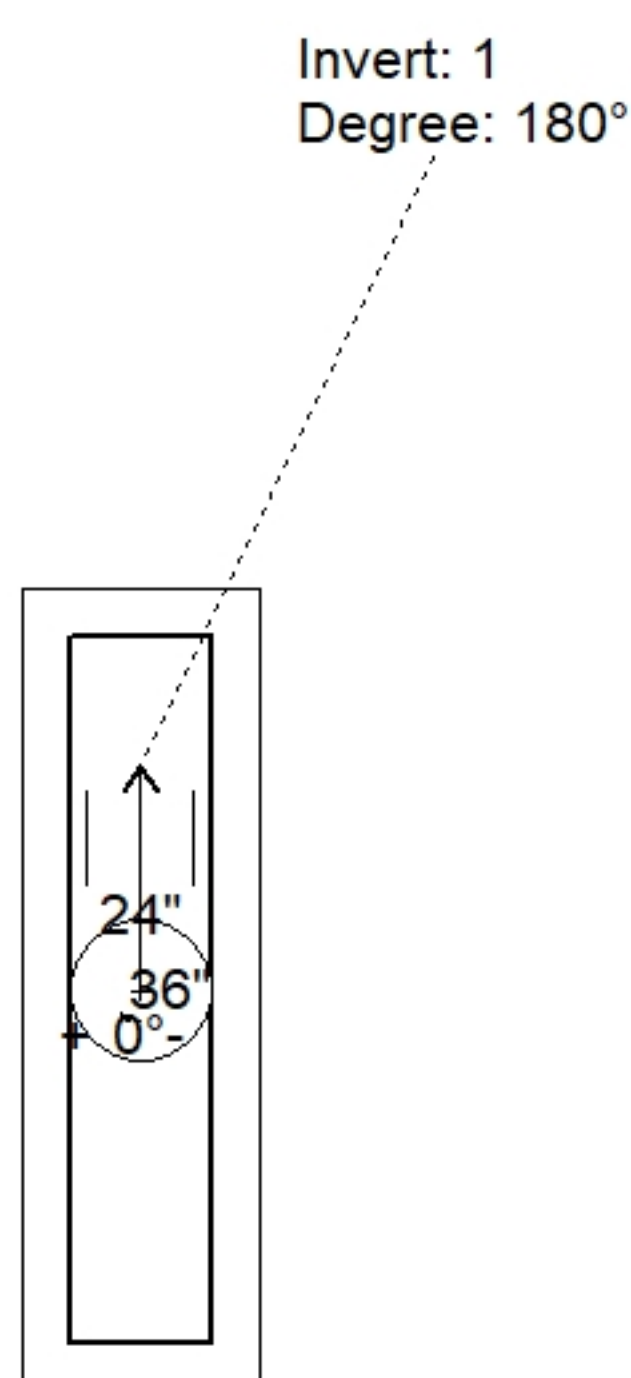

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	593.21'							
Reducer								
Invert 1	588.3'	180°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26" - (P1)

Default - Interior Dimensions

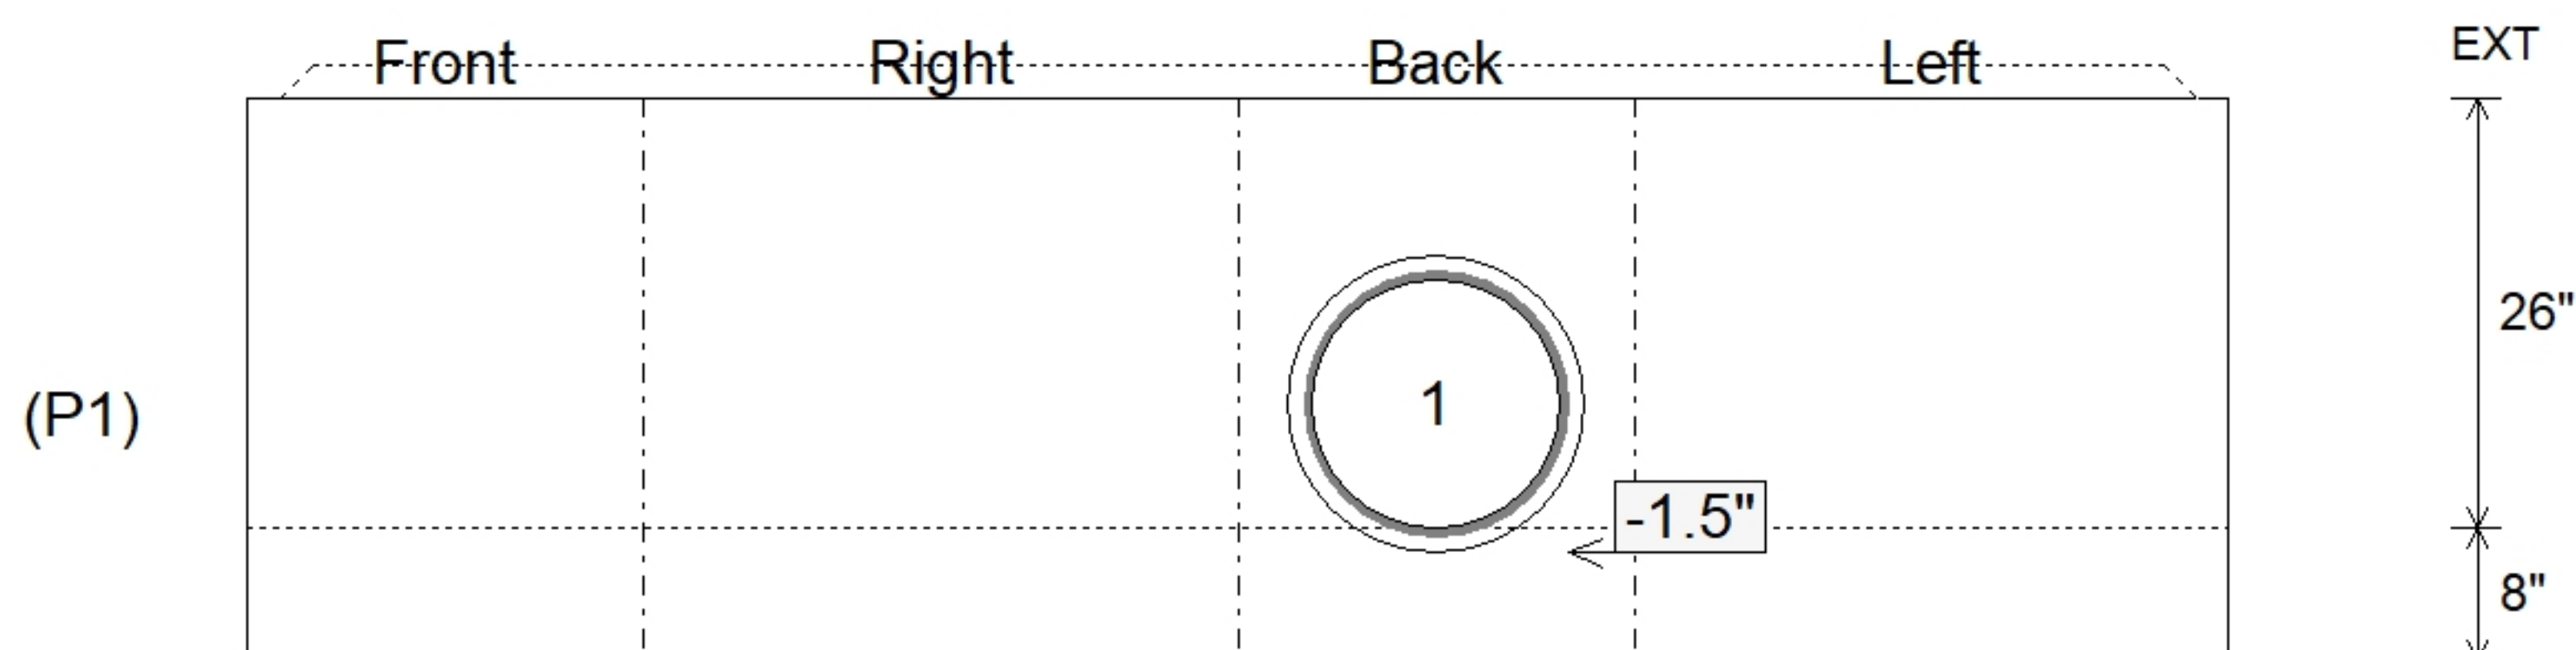

Submittal Drawing
6/24/2026 3:39:19 PM

SUBMITTAL
APPROVED BY:
