

Job Name: 25-1684P12 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
6/24/2026 1:33:10 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 123+80 LT CBIA INLET 28

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht

- P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"
P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"
P2) 24" x 36" - BOX RISER 8inW, Variable Ht - 48"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"
2) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22
2) Hole - 18

Structure Notes: .
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.




Structure Total: 16940 lb

Rim: 593.09' Rim to Invert: 8.99' Slack: 5.88" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	584.1'	50°	22.272"	18" CMP	19"	Hole 22	22"	28.719"	-2"	10"
Invert 2	584.1'	180°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

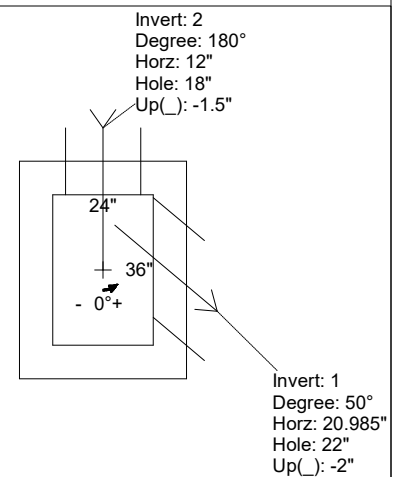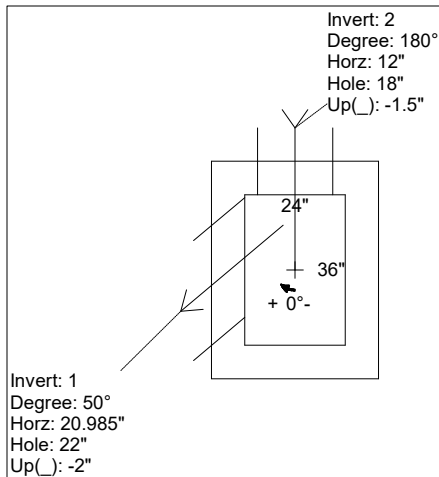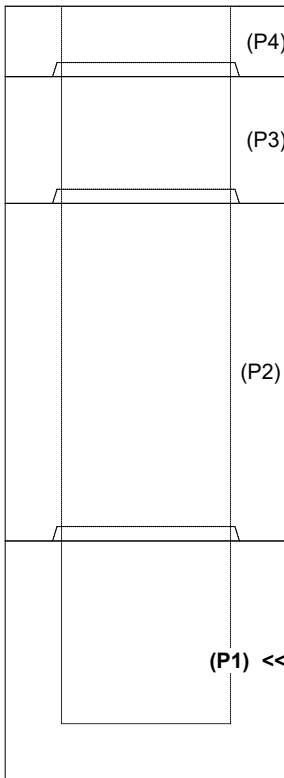

INSIDE WALL DIMENSIONS

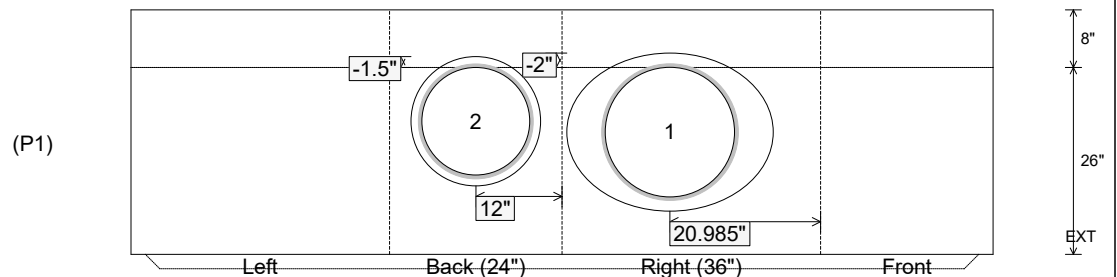

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 26"
Height (Ext): 34"

Weight (Net): 3545 lb
Volume (Net): 0.91cu.yd
