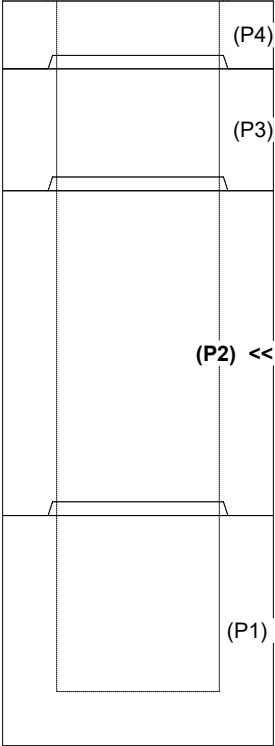
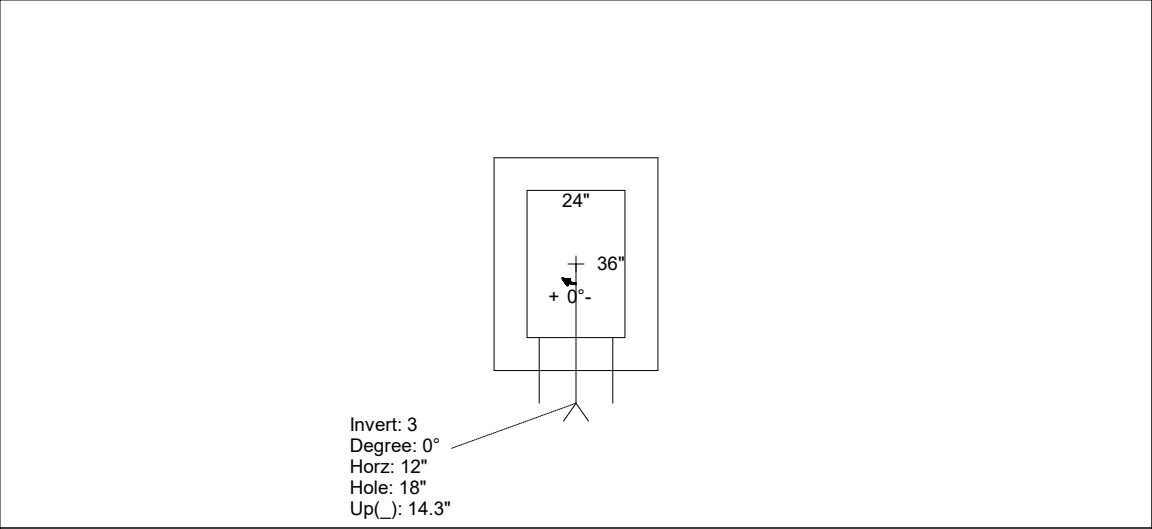
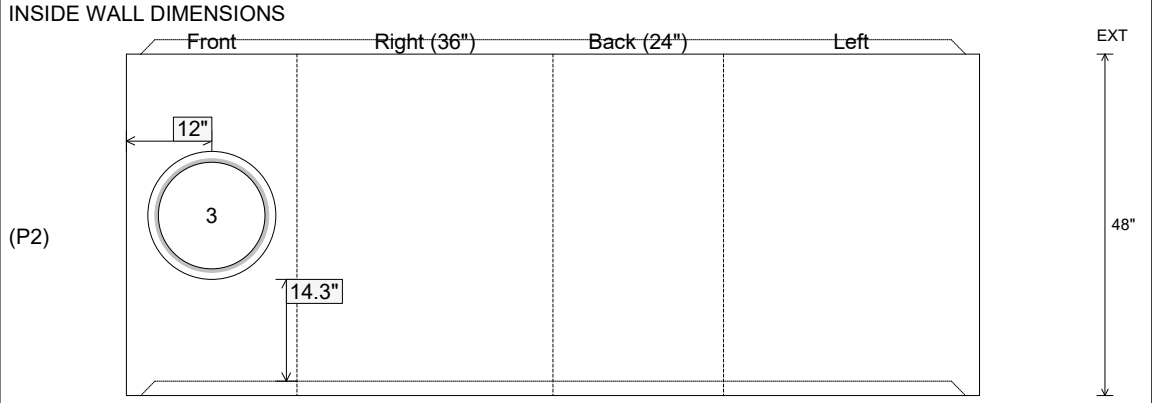


Job Name: 25-1684P12 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 6/24/2026 1:34:24 PM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 123+80 LT CBIA INLET 28											
P2		BX2436-08R-VH		BOX RISER 8inW, Variable Ht							
P4) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18" P2) 24" x 36" - BOX RISER 8inW, Variable Ht - 48" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26" 2) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 2) Hole - 18						3398 lb 5270 lb 4727 lb 3545 lb 0 lb 0 lb 0 lb ----- Structure Total: 16940 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.			
Rim: 593.09'		Rim to Invert: 8.99'		Slack: 5.88"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3	587.75'	0°	20"	15" CMP	16"	Hole 18	18"	18"	14.3"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 8" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 4727 lb Volume (Net): 1.21cu.yd		
