

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	




Slack: 5.88"


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

0 lb


Structure Total: 16940 lb

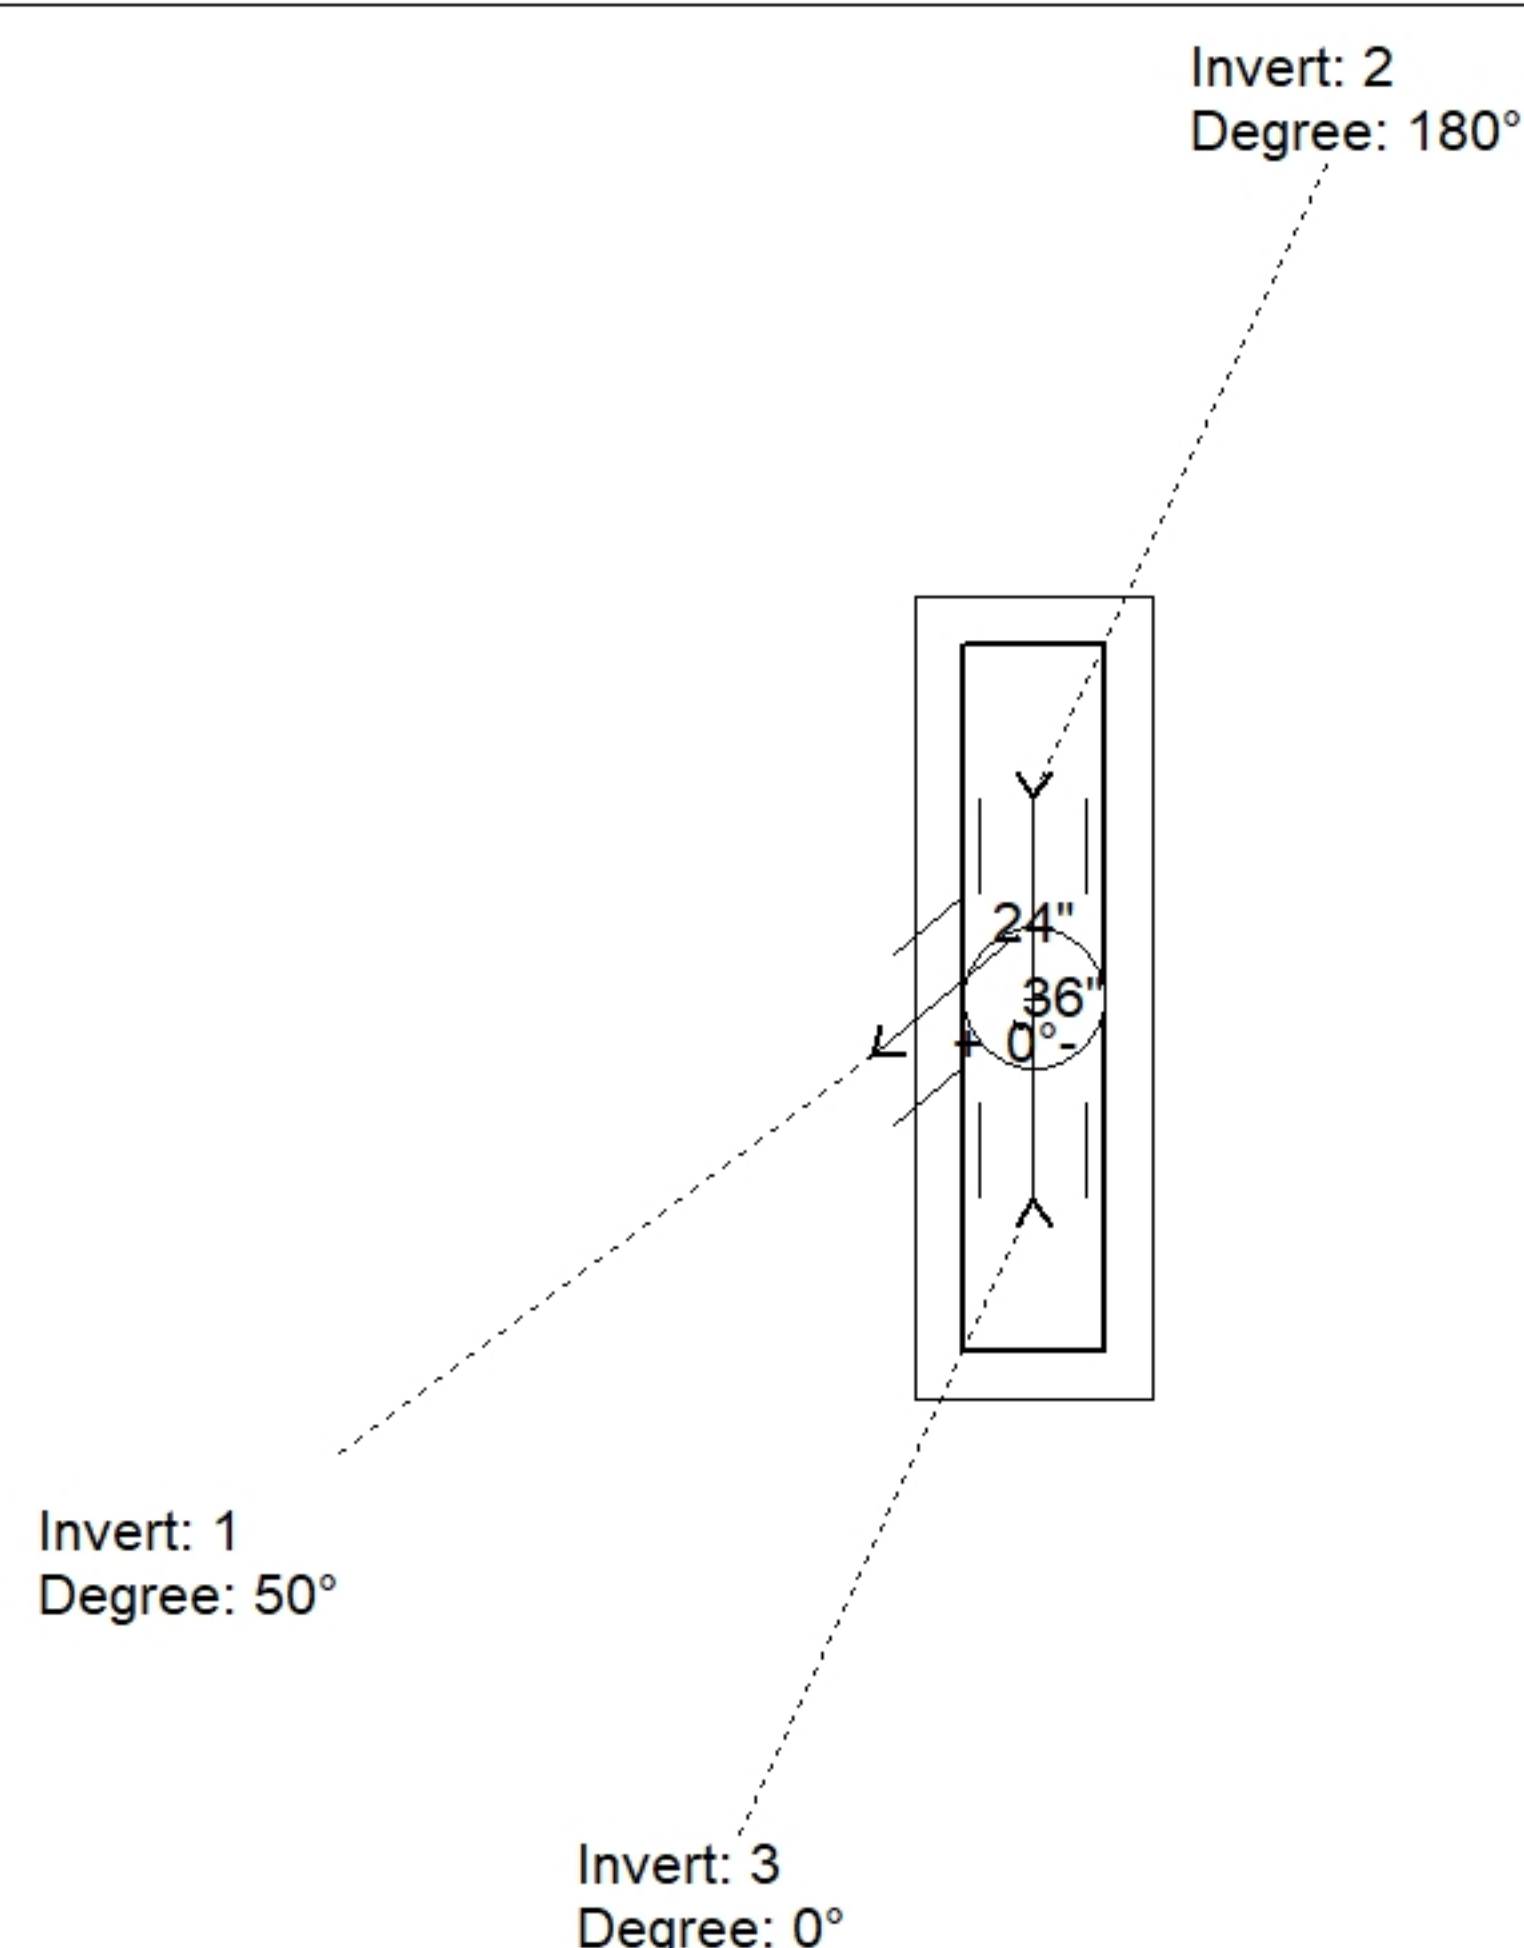

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (_)	Ref
Rim	593.09'							
Reducer								
Invert 1	584.1'	50°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	584.1'	180°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3	587.75'	0°	15" CMP	16"	18"	Hole 18	14.3"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

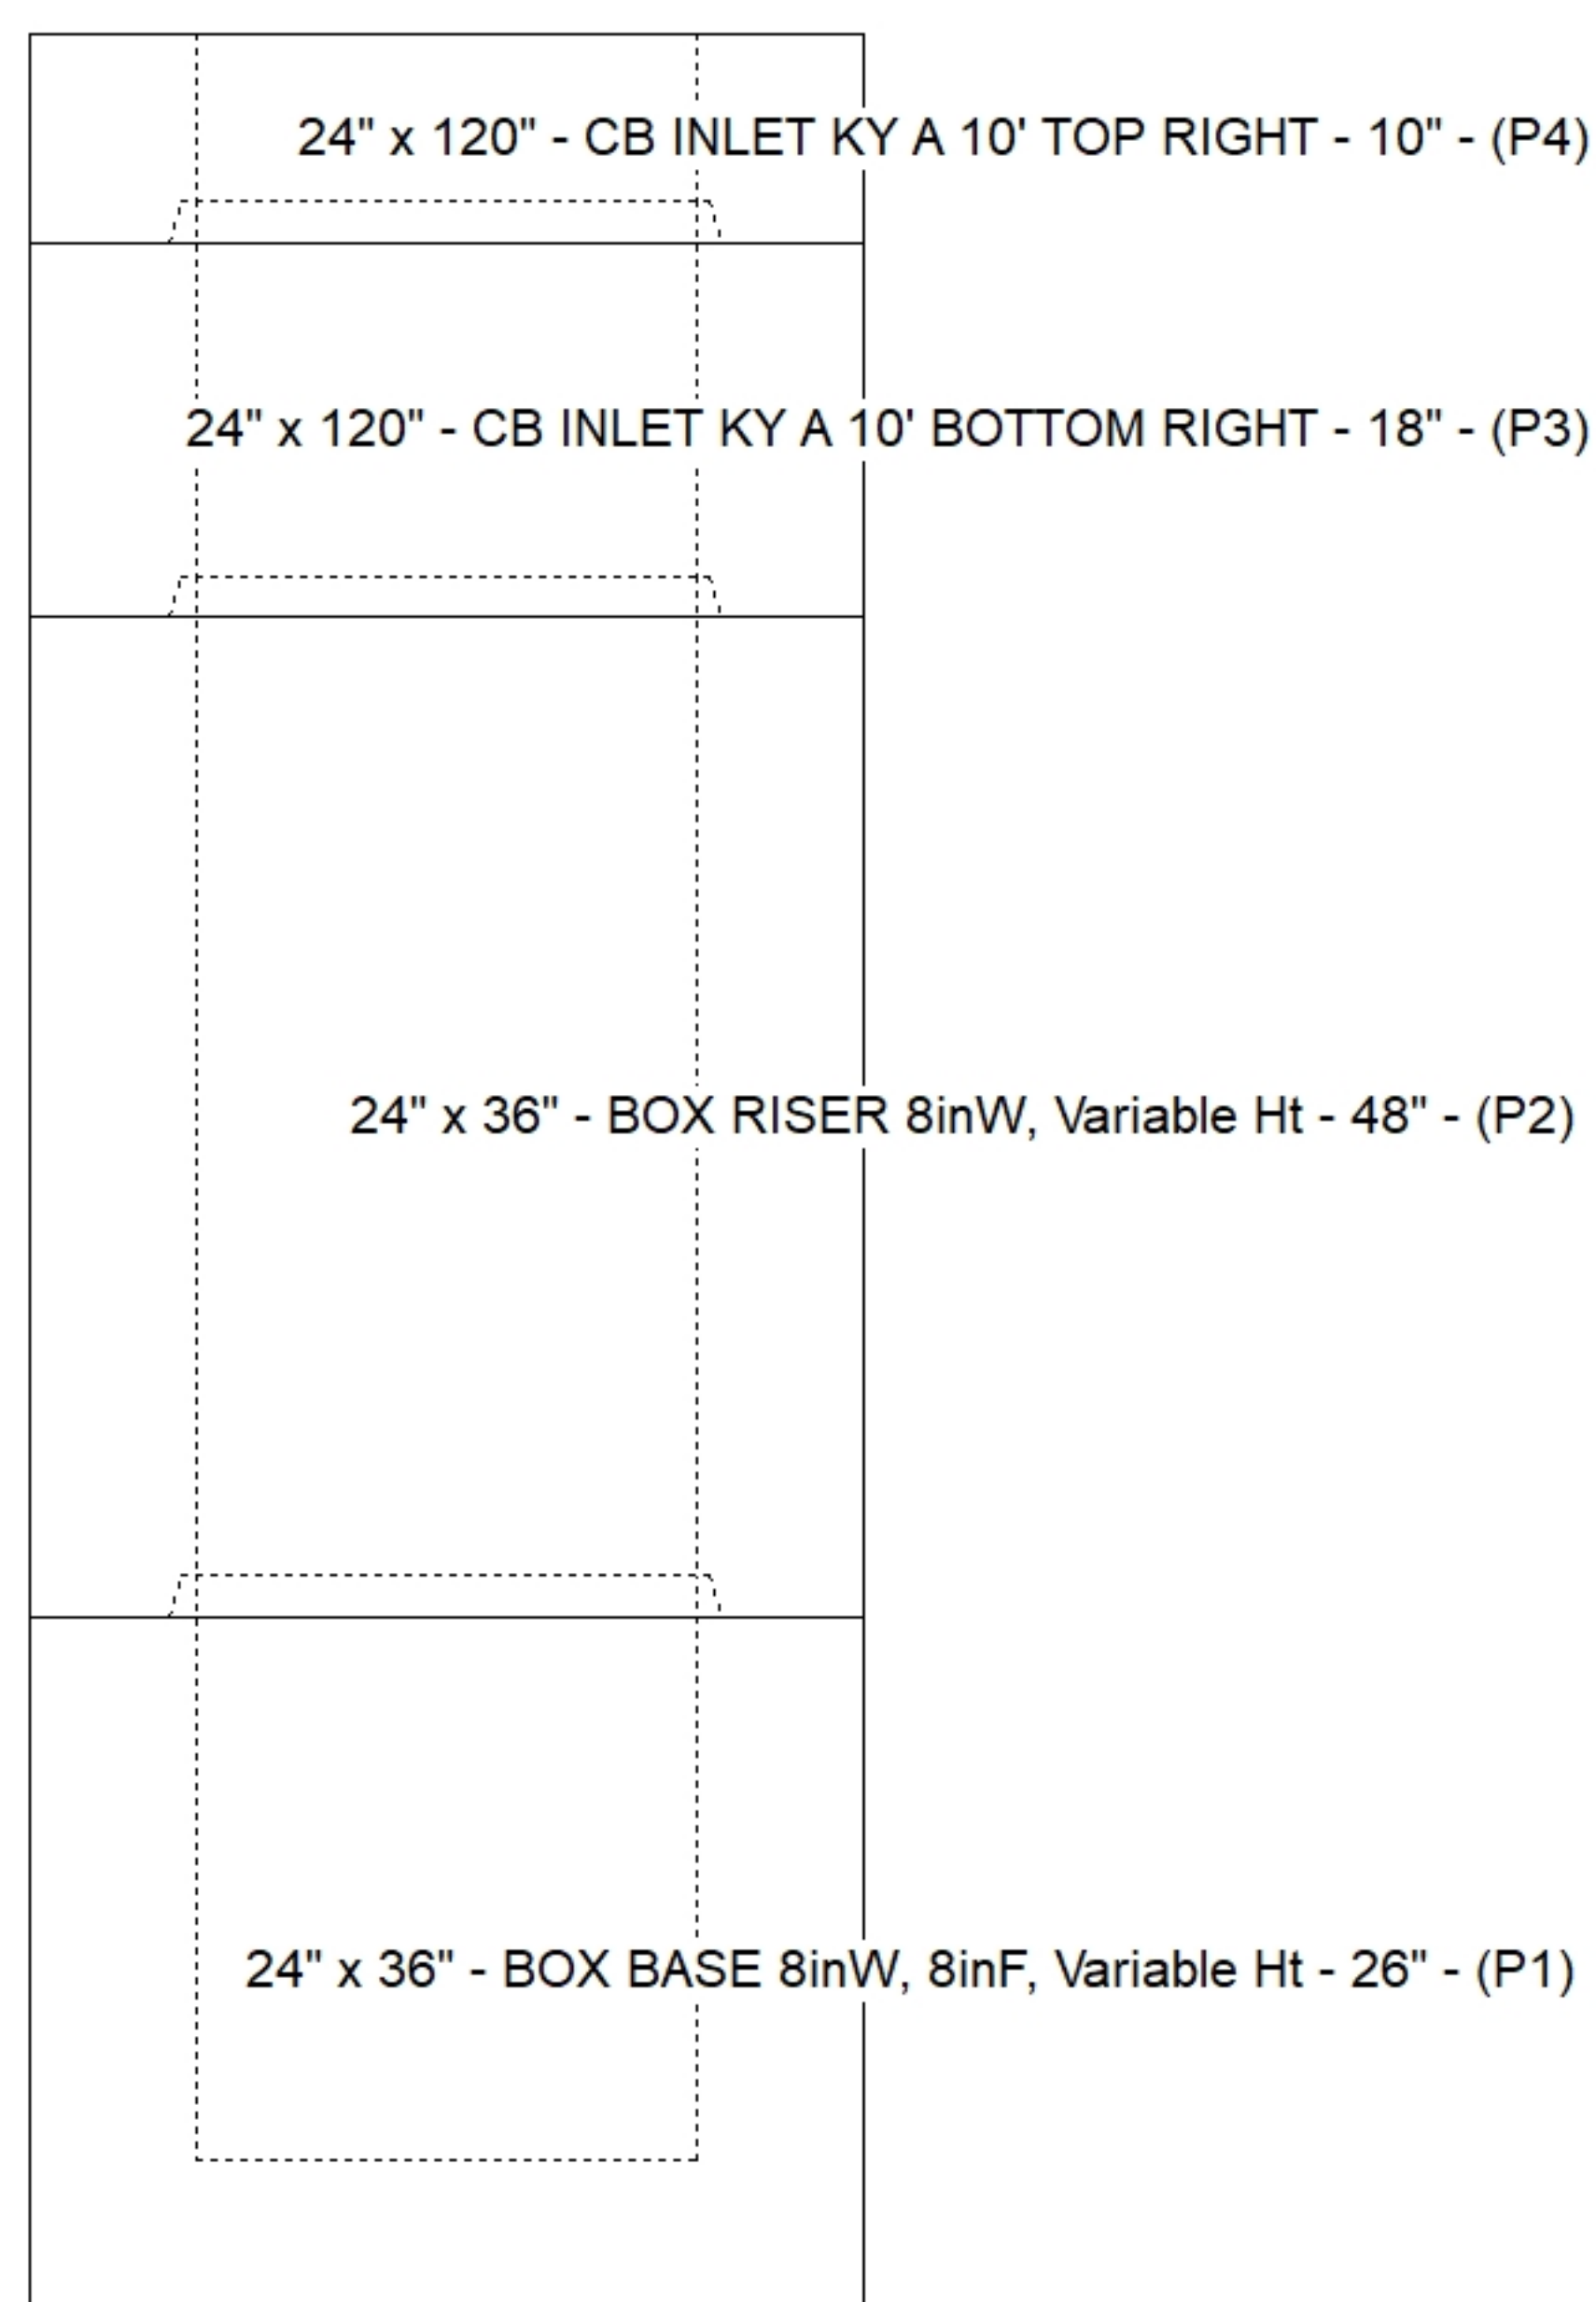

Default - Interior Dimensions

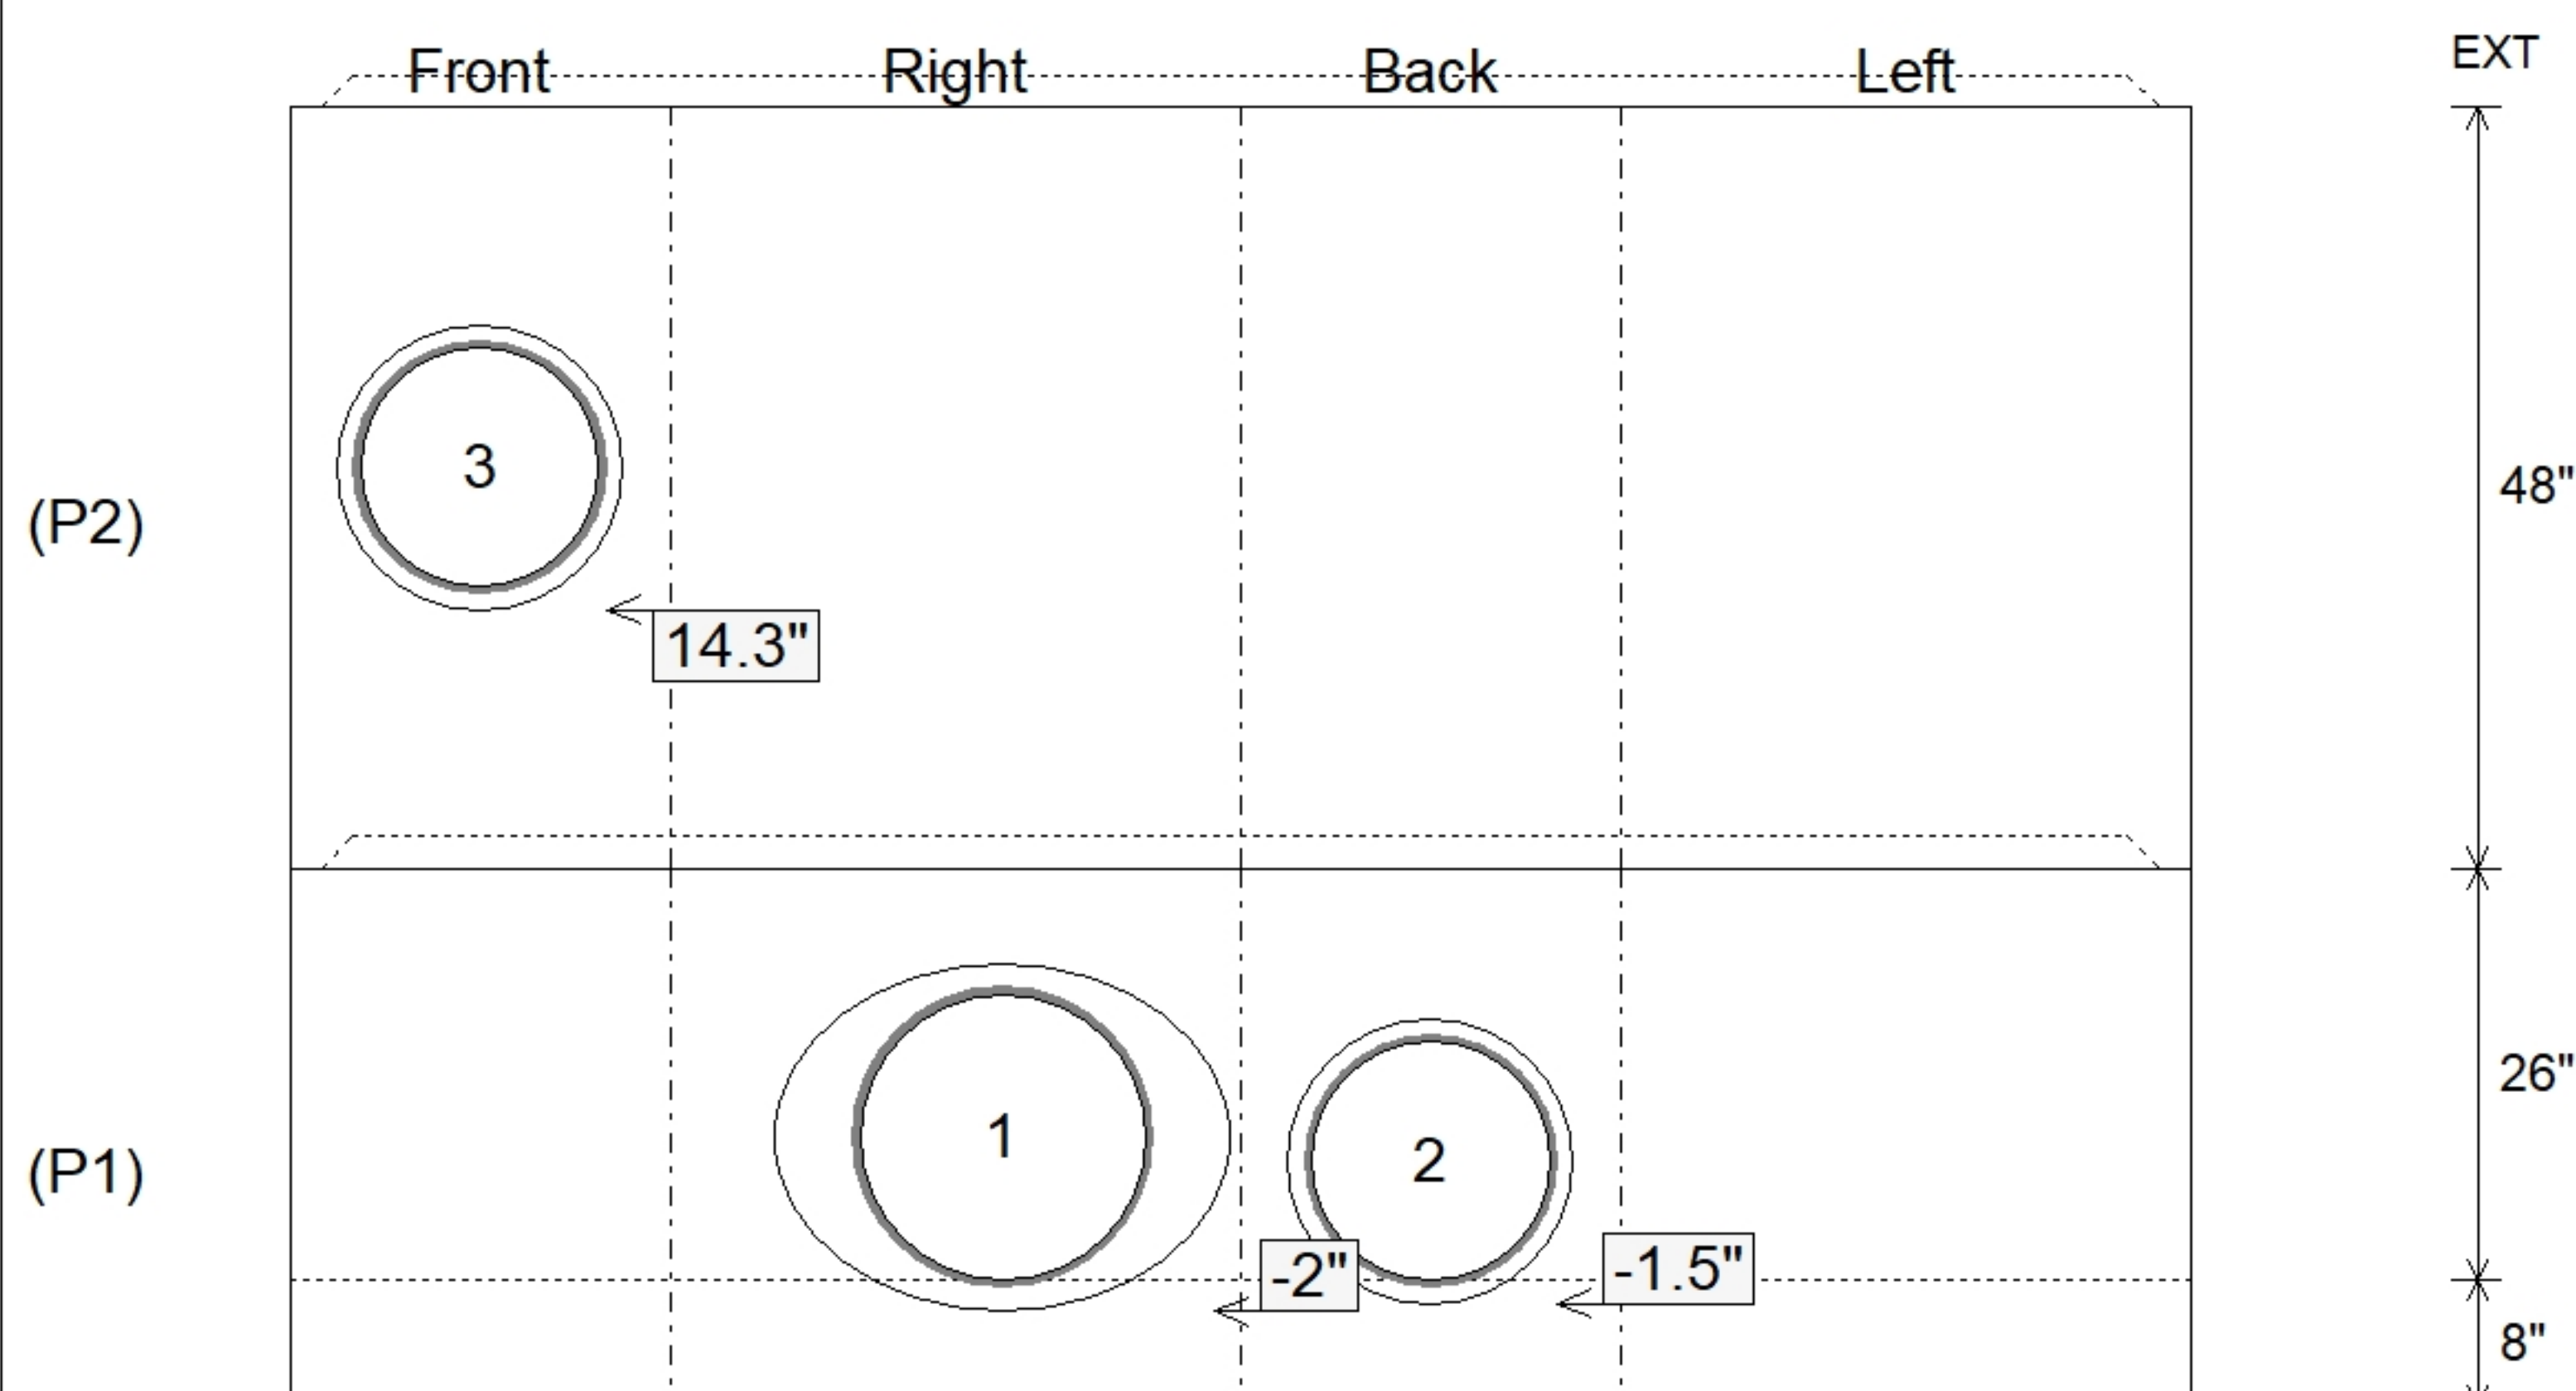

Submittal Drawing
6/24/2026 3:39:19 PM

SUBMITTAL
APPROVED BY:
