


Job Name: 25-1684P12 KYTC Jefferson Co. Call 200 (251007)
 Job Location: I-264 Louisville, Ky.
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
 6/24/2026 1:33:07 PM

Tech: J. Coppage
 PC: T. Ryan



Structure ID: 2002+20 LT CBIB INLET 25

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht

- P4) 8" x 120" - CB INLET KY B 10' TOP - 9"
 P3) 24" x 120" - CB INLET KY B 10' BOTTOM RIGHT - 17"
 P2) 24" x 36" - CB FT REDUCER 24"X24" HOLE - 8"
 P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 29"
 1) 24" x 36" - Conseal CS-102 1.00"
 1) 24" x 24" - Conseal CS-102 1.00"
 2) Hole - 22"

Structure Notes:
 -KYTC STATE PROJECT 251007
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
 -KYTC CERTIFICATIONS REQUIRED.



Structure Total: 9120 lb

Rim: 587.88' Rim to Invert: 5.28' Slack: 0.36" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	582.6'	250°	18.721"	18" CMP	19"	Hole 22	22"	23.412"	-2"	0"
Invert 2	583.01'	335°	16.128"	18" CMP	19"	Hole 22	22"	23.996", 0.598"	2.92"	7.479"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

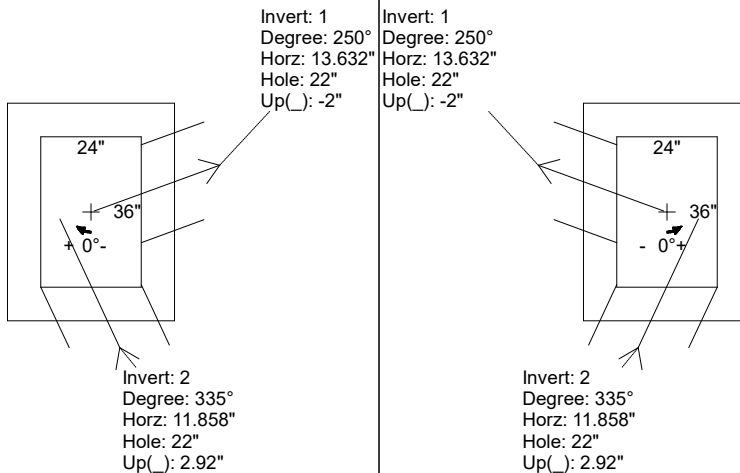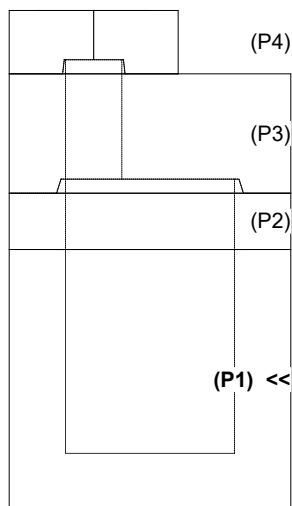

INSIDE WALL DIMENSIONS

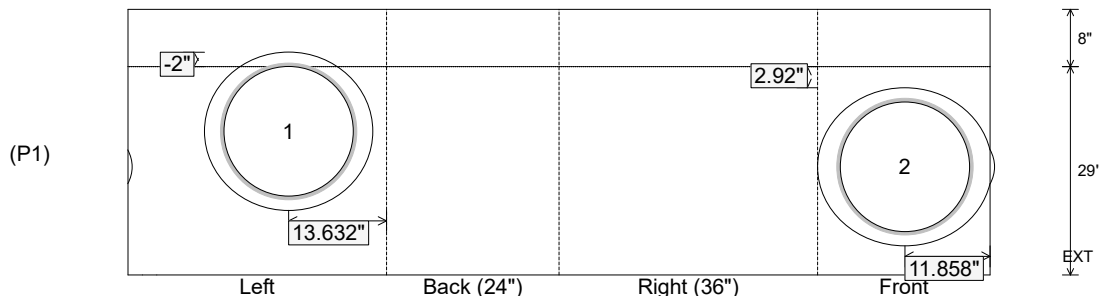

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 29"
 Height (Ext): 37"

Weight (Net): 3800 lb
 Volume (Net): 0.97cu.yd
