


Job Name: 25-1684P13 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

7/21/2026 12:34:11 PM

Tech: N. Richards

PC: J. Jarvis



Structure ID: 5125+00 RT DBI TYPE 1-MOD.

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"

P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 28"

1) 36" x 36" - Conseal CS-102 1.00"

1) DOGHOUSE INVRTD - 30"x28"

0 lb

4580 lb

0 lb

0 lb

Structure Total:

4580 lb

Structure Notes:

-KYTC STATE PROJECT 251007

-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)

-FRAME & GRATES BY OTHERS.

-KYTC CERTIFICATIONS REQUIRED.

-#5 BAR EXTENDED OUT OF TOP OF BOX 20" AT 12" C/C.

Rim: 561.38'

Rim to Invert: 3'

Slack: 0"



Sump: 0"

Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	558.38'	0°	26"	24" CMP	25"	DOGHOUSE INVRTD 30"x28"	30" x 28"	30"	-2"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

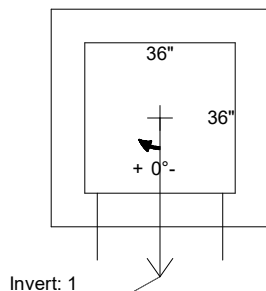


Invert: 1
Degree: 0°
Horz: 18"
Hole: 30" x 28"
Up(): -2"



Invert: 1
Degree: 0°
Horz: 18"
Hole: 30" x 28"
Up(): -2"

INSIDE WALL DIMENSIONS

(P1)



8"
28"
EXT

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 28"
Height (Ext): 36"

Weight (Net): 4580 lb
Volume (Net): 1.17cu.yd
