

Job Name: 25-1684P13 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

Tech: N. Richards

7/21/2026 12:37:18 PM

PC: J. Jarvis



Structure ID: 5130+98 RT CBBI-MOD B1


P2 CMBBIT9-B1LH

CB MED BAR BOX INLET 9B1 LH

- P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 34"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22
1) Hole - 18

- 0 lb Structure Notes:
4000 lb -KYTC STATE PROJECT 251007
4440 lb -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
0 lb -CASTING FRAMES & GRATES BY OTHERS.
0 lb -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
0 lb -KYTC CERTIFICATIONS REQUIRED.

Structure Total: 8440 lb

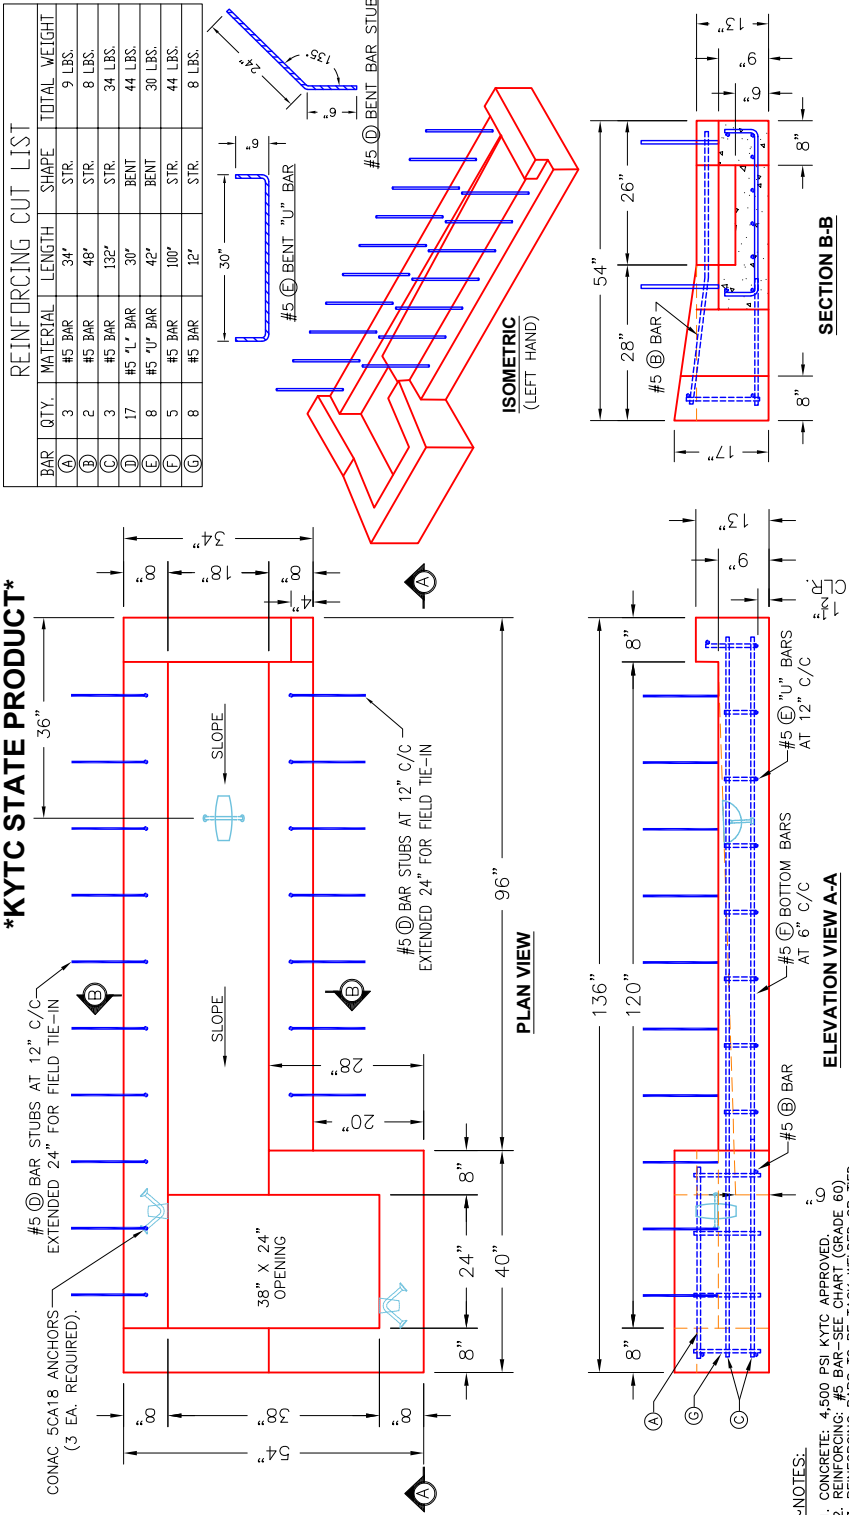

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 17"

Weight (Net): 4000 lb
Volume (Net): 0cu.yd
