


Job Name: 25-1684P13 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

7/21/2026 12:34:09 PM

Tech: N. Richards

PC: J. Jarvis



Structure ID: 5132+72 RT DBI TYPE 1-NA

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
P2) 36" x 36" - BOX RISER 8inW - 30"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 46"
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 18"

Structure Total: 10624 lb



Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-TOP SLAB WITH FRAME & GRATES BY OTHERS (NO APRON).
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.
-#5 BAR EXTENDED OUT OF TOP OF RISER 20" AT 12" C/C.

Rim: 562.8' Rim to Invert: 7' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	555.8'	0°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

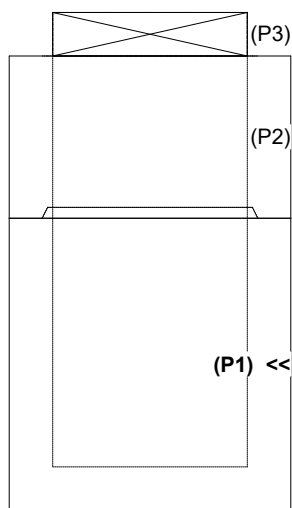


Invert: 1
Degree: 0°
Horz: 18"
Hole: 18"
Up(): -1.5"

Invert: 1
Degree: 0°
Horz: 18"
Hole: 18"
Up(): -1.5"

INSIDE WALL DIMENSIONS

(P1)

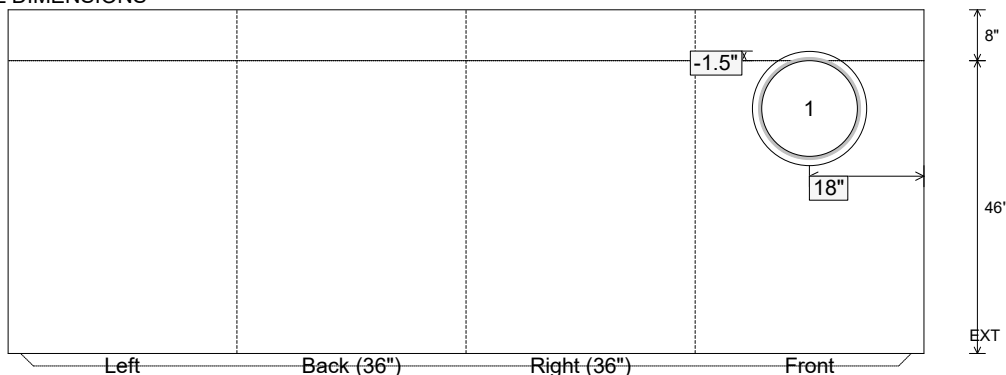

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 46"
Height (Ext): 54"

Weight (Net): 7079 lb
Volume (Net): 1.81cu.yd
