

Job Name: 25-1684P13 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

Tech: N. Richards

7/21/2026 12:34:08 PM

PC: J. Jarvis



Structure ID: 5137+49 RT JB-A

P1 BX2424-08BA24

BOX BASE 8inW, 8inF

- P2) 24" x 24" - CB FLAT TOP 8"W SOLID - 8"
P1) 24" x 24" - BOX BASE 8inW, 8inF - 24"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 22
1) Hole - 18

1074 lb
2455 lb
0 lb
0 lb
0 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.




Structure Total: 3529 lb

Rim: 556' Rim to Invert: 2.76' Slack: 1.12' Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	553.24'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 2	553.24'	90°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 3	553.24'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

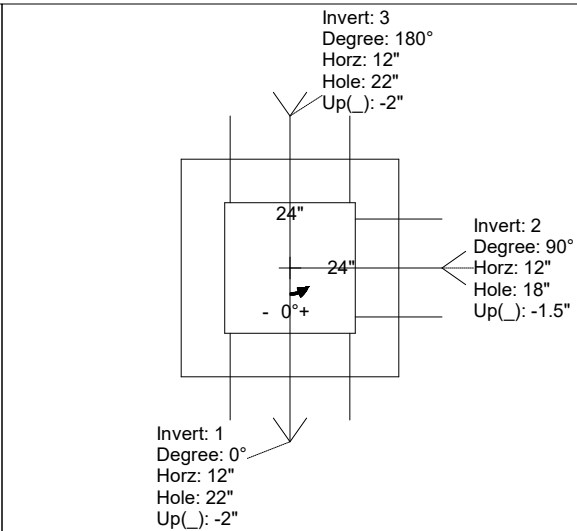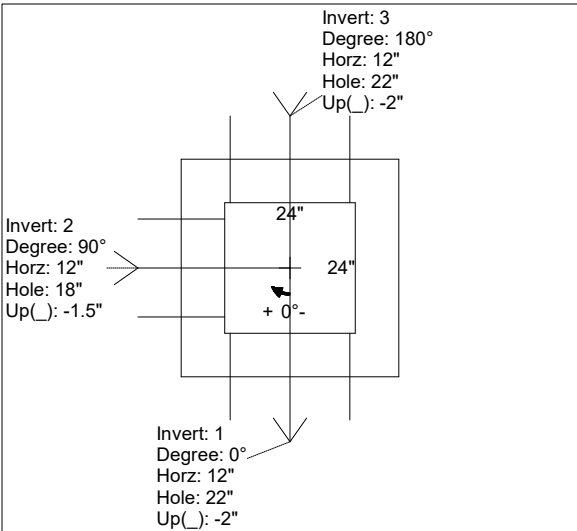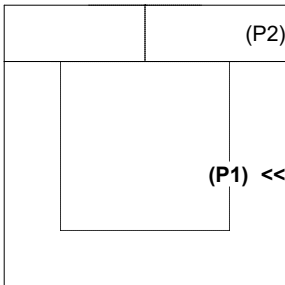

INSIDE WALL DIMENSIONS

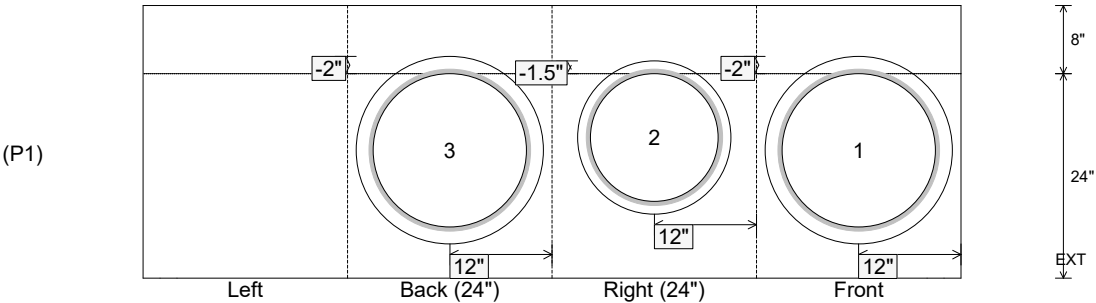

Coating (Int):
Coating (Ext):
Seam Up: Flat
Seam Dn: n/a
Wall Thickness: 8"
Floor Height: 8"
Height (Int): 24"
Height (Ext): 32"
Weight (Net): 2455 lb
Volume (Net): 0.63cu.yd
