




Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:21 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 11+79 CBBI-MOD B1											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CASTING (cast in) - 3" P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 40" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 26					0 lb 4000 lb 4955 lb 0 lb 0 lb 0 lb ----- Structure Total: 8955 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 570.17' Rim to Invert: 5.1' Slack: 4.2" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	565.07'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	565.07'	180°	20"	18" RCP B WALL	23"	Hole 26	26"	25"	-4"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

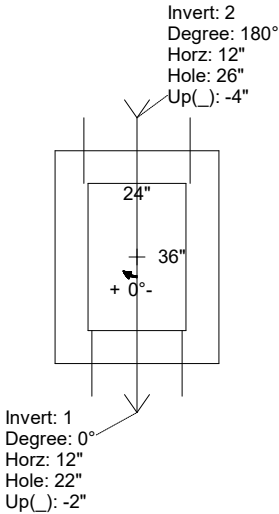

RIGHT-SIDE UP VIEW (int. dimensions)

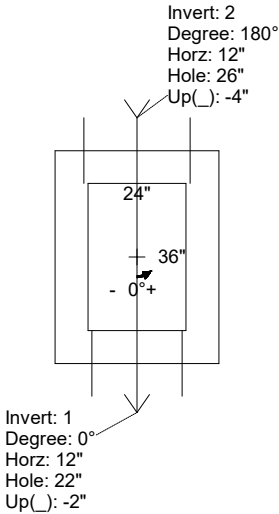


UPSIDE-DOWN VIEW (int. dimensions)

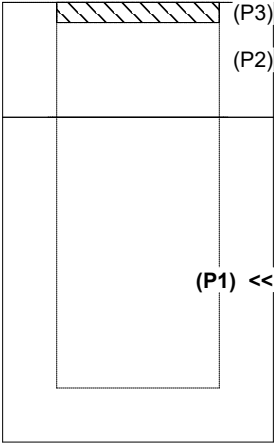

(P1) <<

INSIDE WALL DIMENSIONS

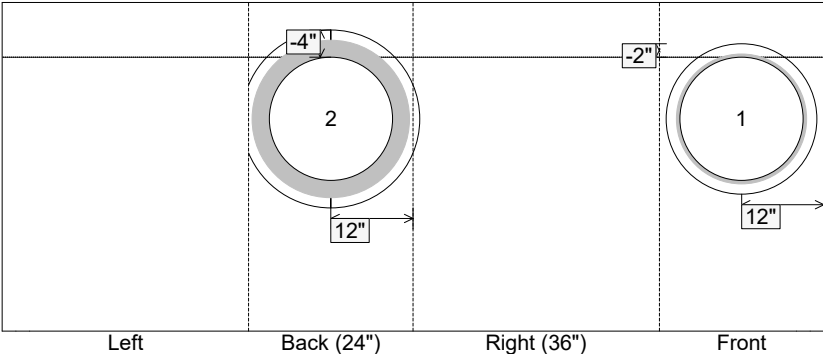

Left Back (24") Right (36") Front

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 4955 lb Volume (Net): 1.27cu.yd
----------------------------------	-------------------------------	--	--	--
