

Contractor: Cleary Construction, Inc.

PC: T. Ryan

TECH: J. Coppage

Plant: Beaver Dam, KY




Structure ID: 14+27 CBBI-MOD B1			
Spec: KYTC	Rim: 566.6'	Sump: 0"	Floor (Bot): 558.933'
Type: MBI TYPE 9	Invert: 559.6'	Floor (Top): 559.6'	Overall Height: 7.333'
Size: 24" x 36"	Rim to Invert: 7'	Floor Height: 8"	Slack: 4"

Structure Notes:


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

STRUCTURE SUMMARY:	
P4) 24" x 120" - CASTING (cast in) - 3"	0 lb
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"	4000 lb
P2) 24" x 36" - BOX RISER 8inW, Variable Ht - 21"	2143 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 42"	5427 lb
2) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 22	0 lb


Structure Total:	11569 lb

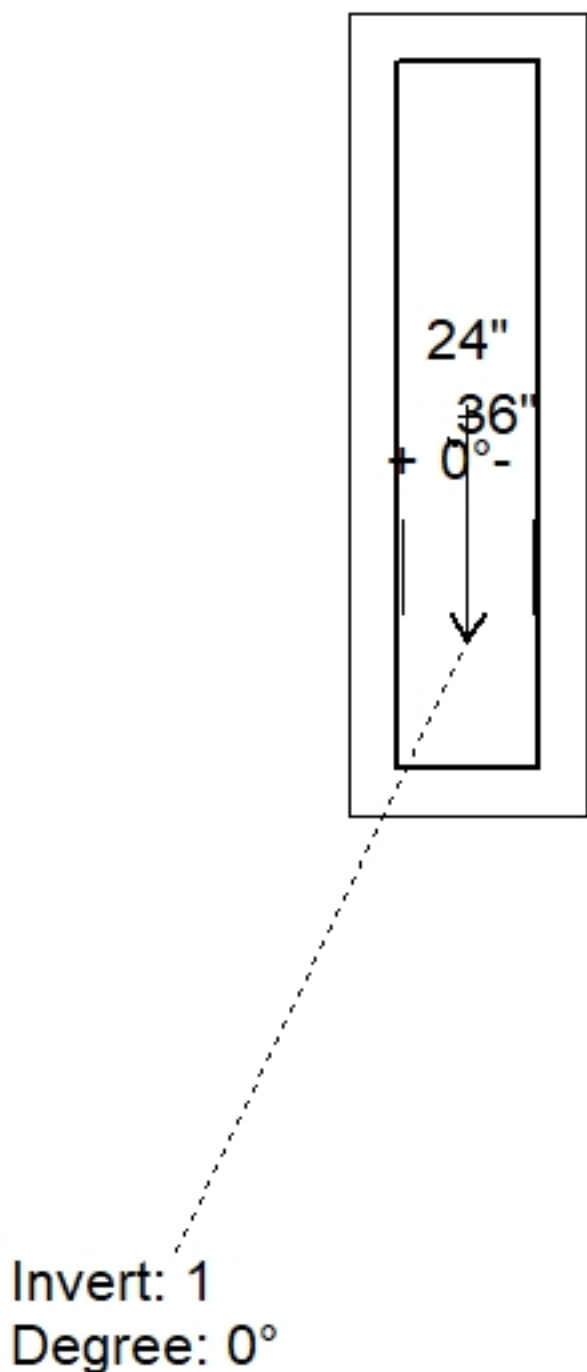

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	566.6'							
Reducer								
Invert 1	559.6'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

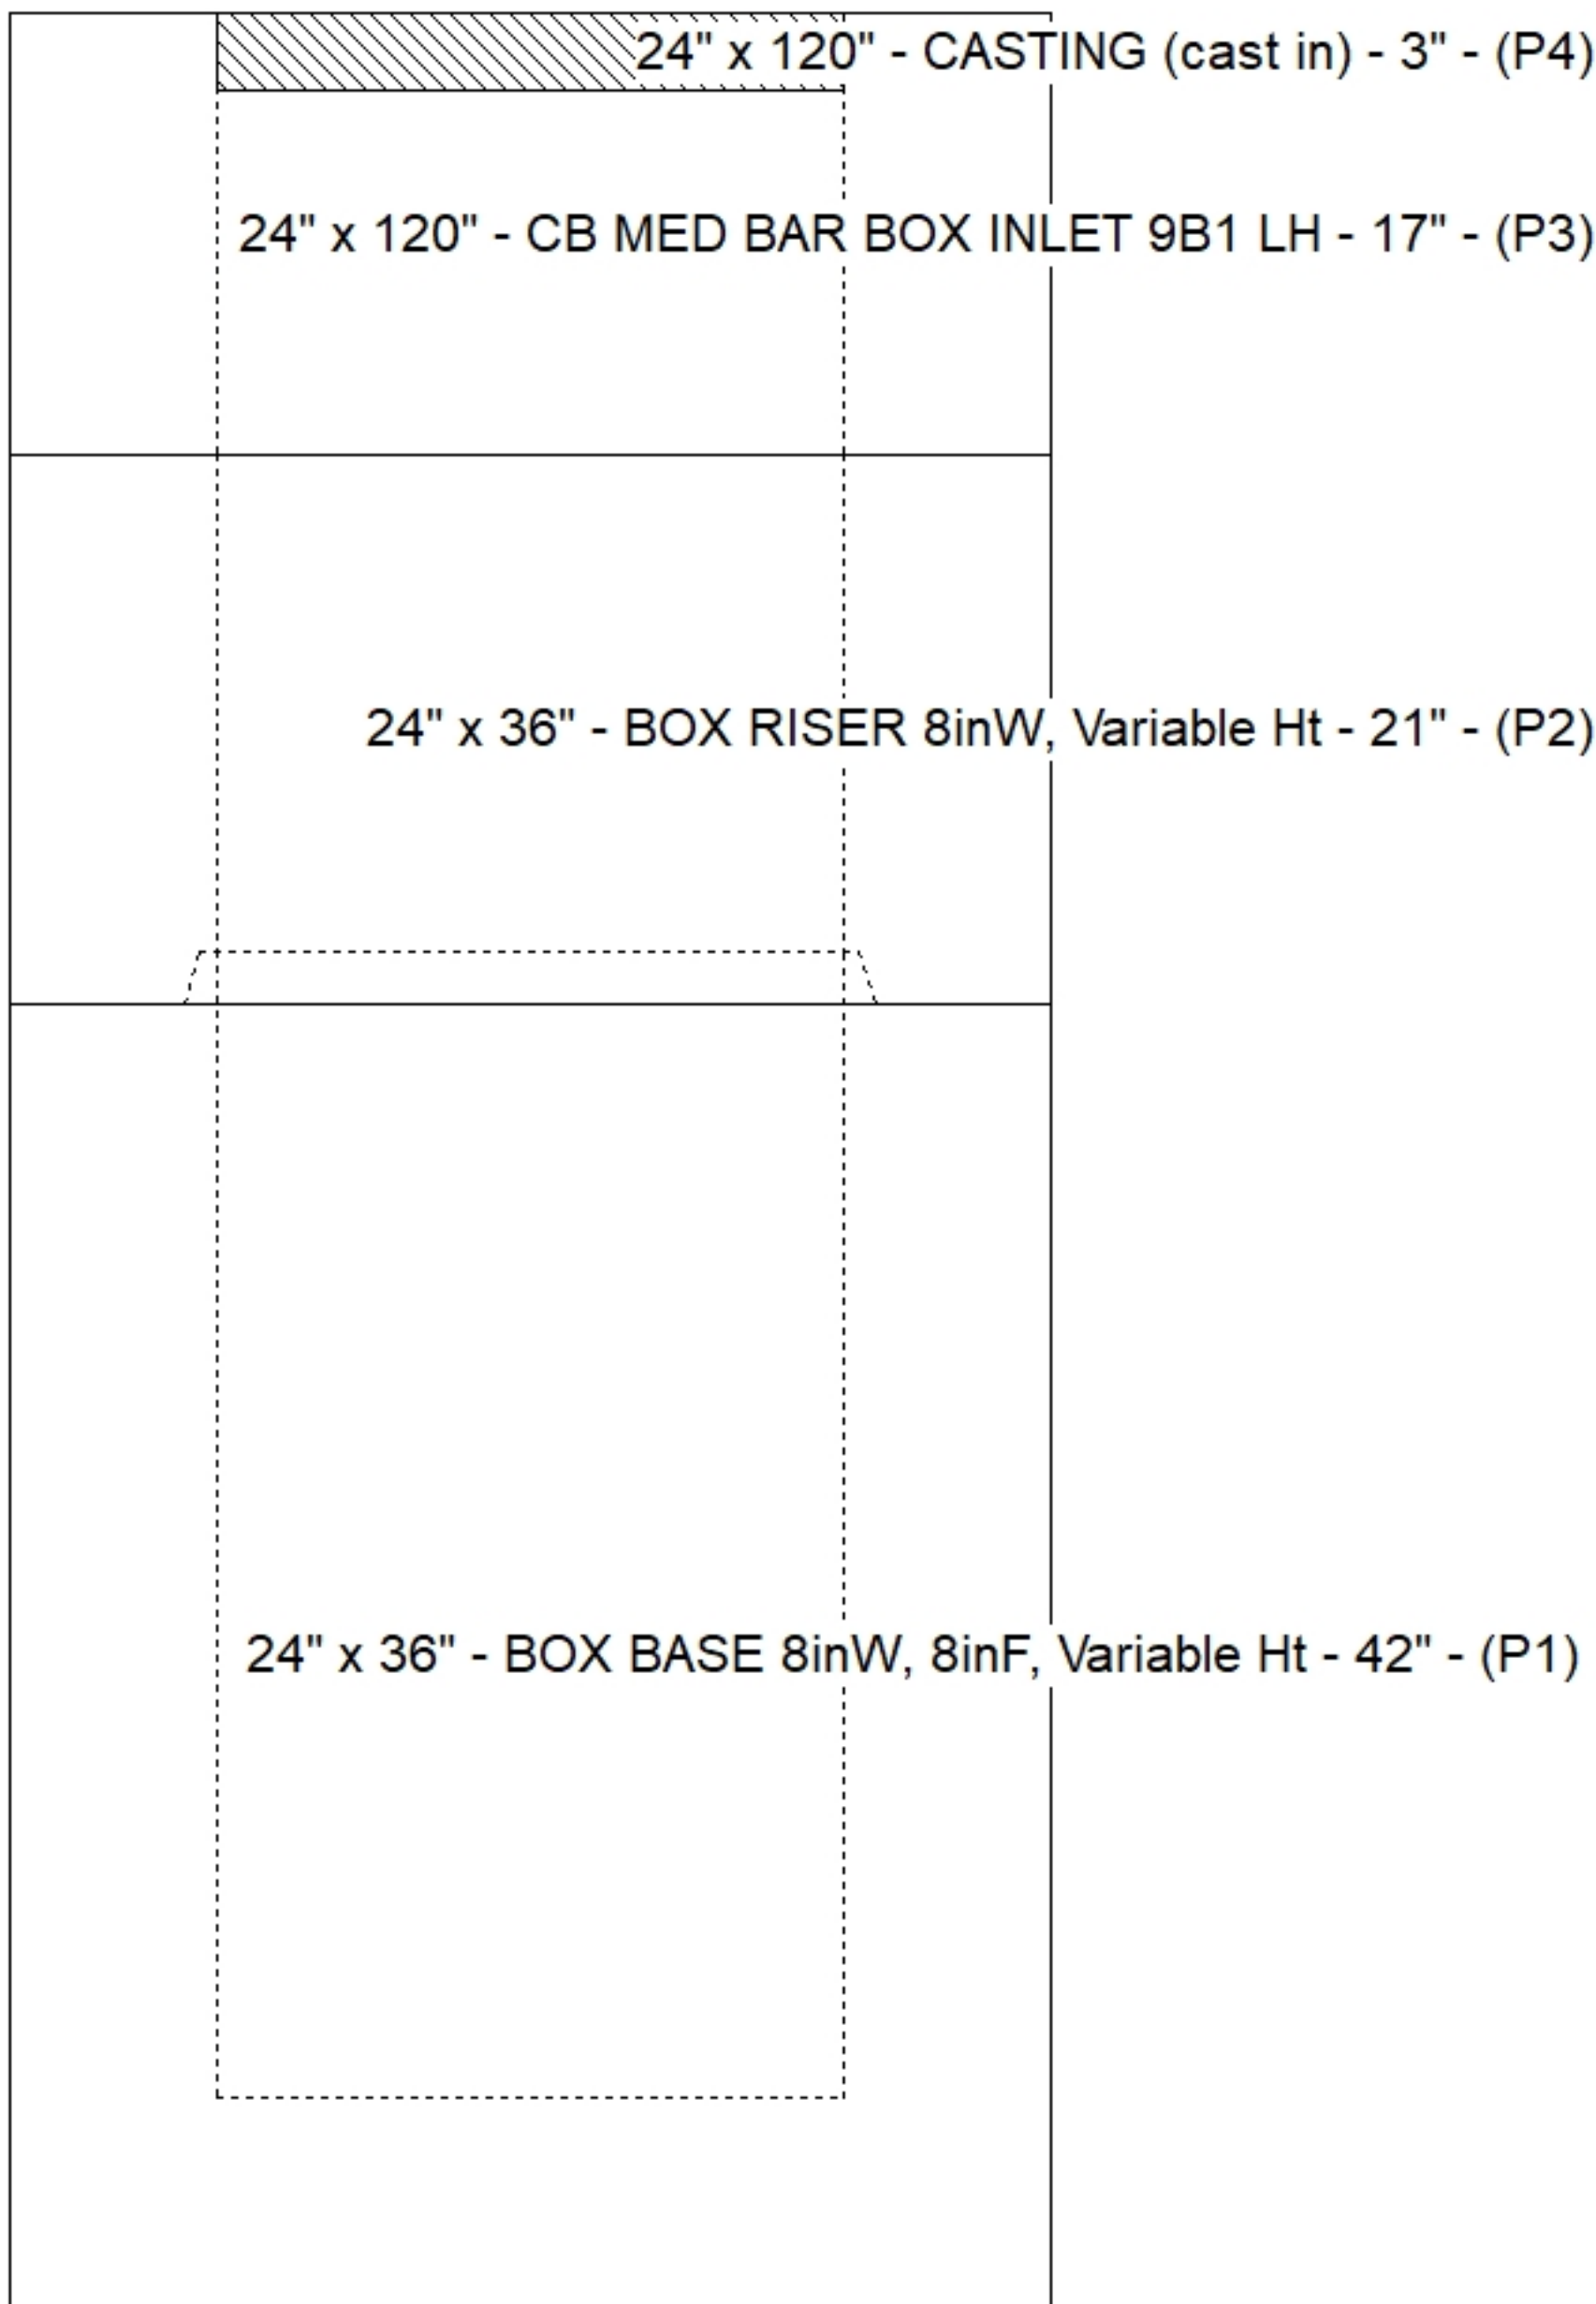

Default - Interior Dimensions

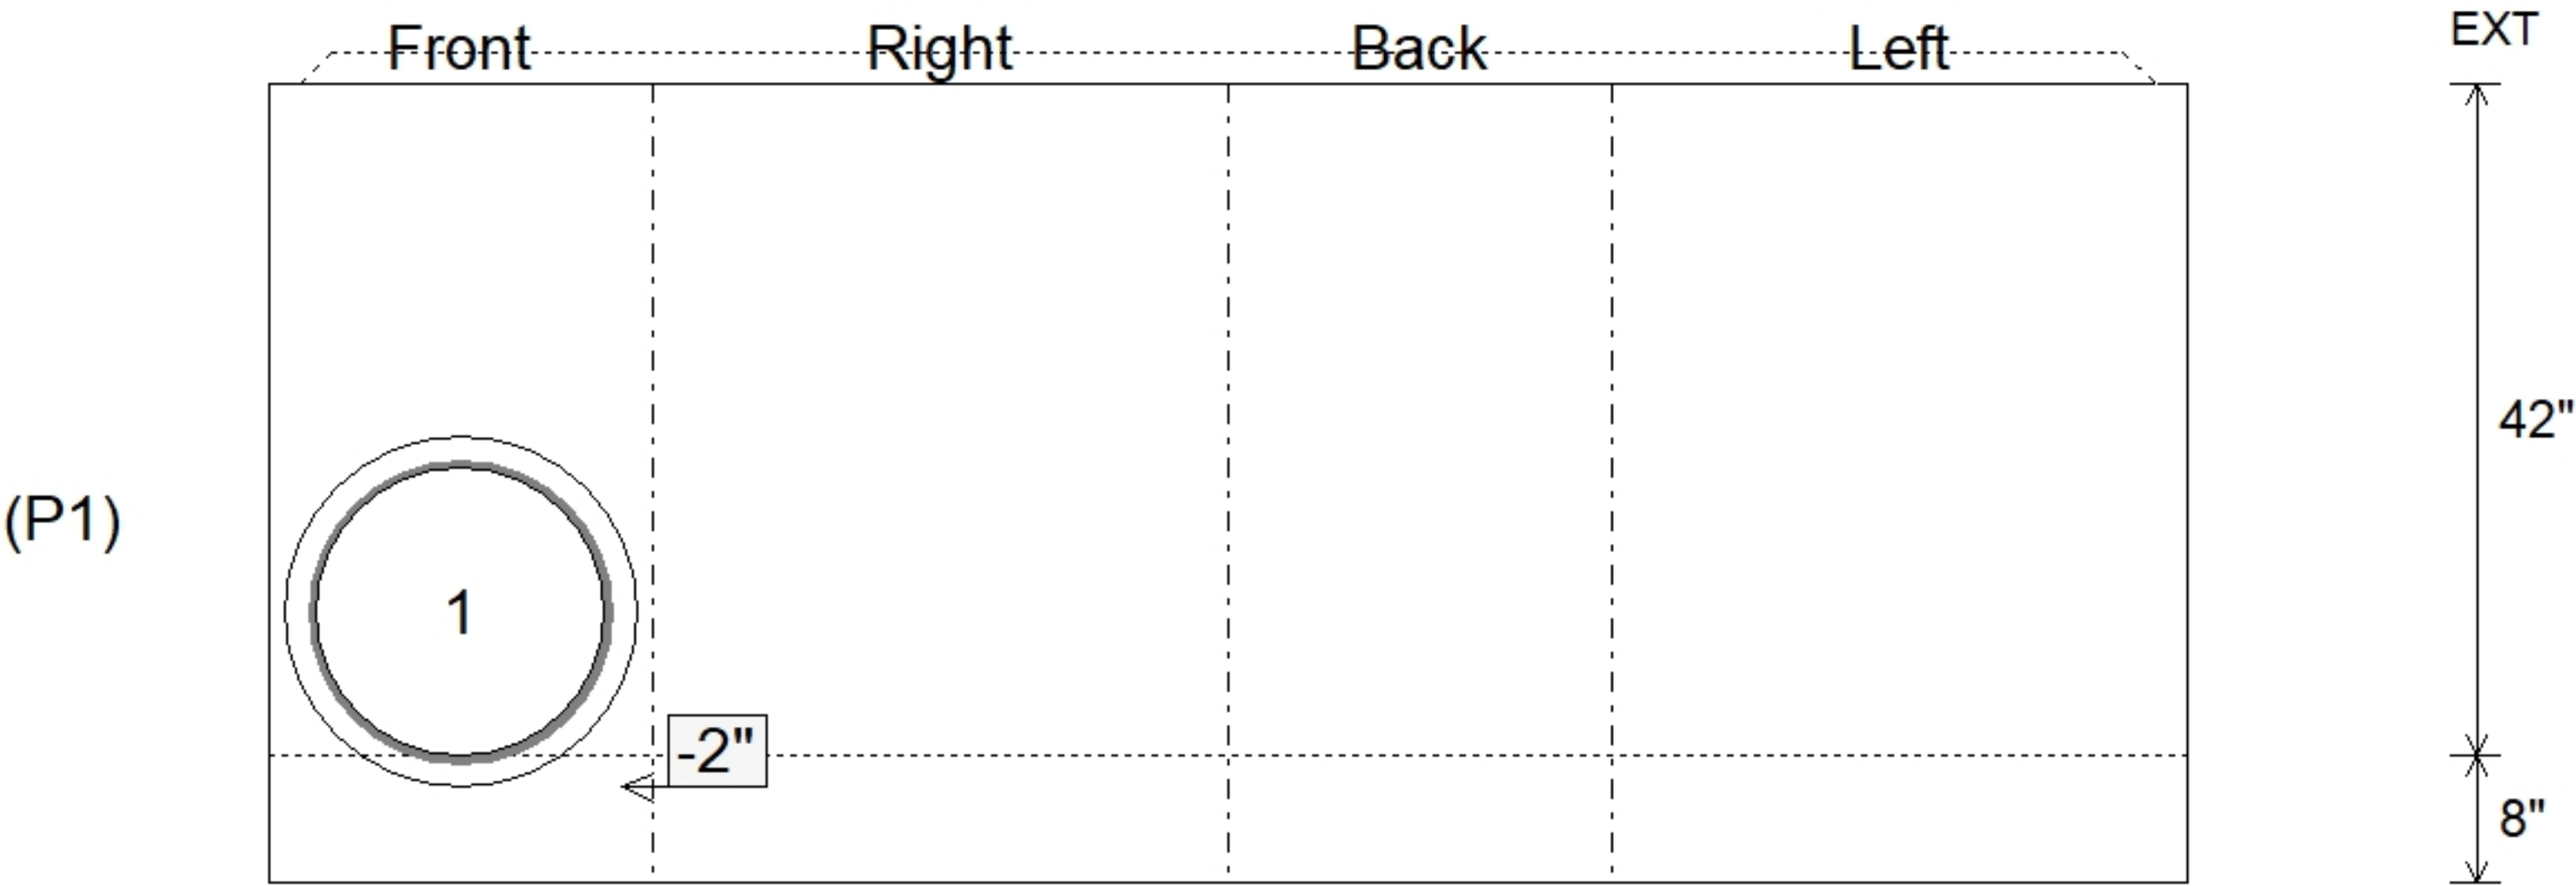

Submittal Drawing
8/10/2026 11:02:39 AM

SUBMITTAL
APPROVED BY:
