

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:28:39 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 15+26 CBBI-MOD B1


P3 CMBBIT9-B1LH

CB MED BAR BOX INLET 9B1 LH

- P4) 24" x 120" - CASTING (cast in) - 3"
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P2) 24" x 36" - BOX RISER 8inW, Variable Ht - 54"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 60"
2) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22

0 lb
4000 lb
5510 lb
7263 lb
0 lb
0 lb
0 lb
Structure Total: 16773 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CASTING FRAMES & GRATES BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

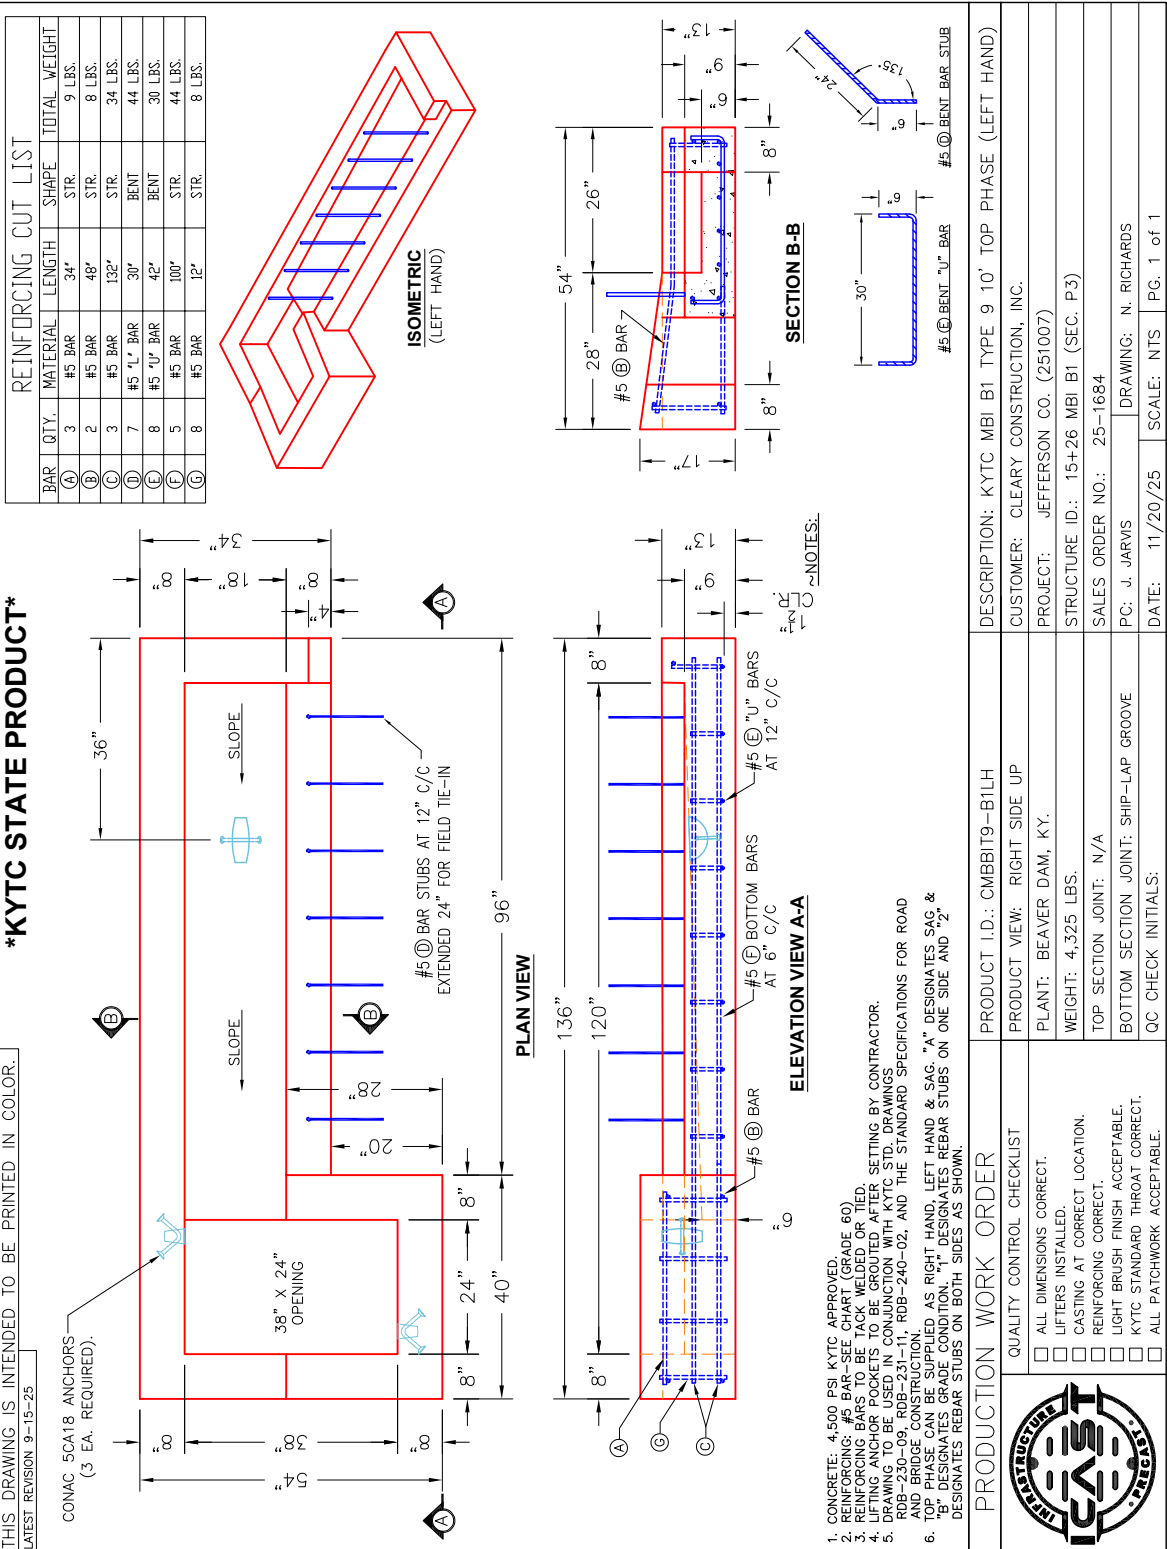

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 17"

Weight (Net): 4000 lb
Volume (Net): 0cu.yd
