


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/5/2026 8:13:00 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 16+15 JB-B1 INLET 36

P1 BX6060-08BA66

BOX BASE 8inW, 8inF

P3) CASTING (cast in) - 0
P2) 60" x 60" - BX FLAT LID 8inW SPEC. (KY JB-B1) - 8"
P1) 60" x 60" - BOX BASE 8inW, 8inF - 66"
1) SECONDARY POUR - WALLS
2) Hole - 52

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.).
-CASTING BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

Structure Total:

0 lb
3574 lb
13077 lb
0 lb
0 lb



16651 lb

FIRST POUR DRAWING

Rim: 558.2' Rim to Invert: 6.23' Slack: 0.76" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	551.97'	0°	38"	48" CMP	49"	Hole 52	52"	52"	-2"	0"
Invert 2	551.97'	180°	38"	48" CMP	49"	Hole 52	52"	52"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

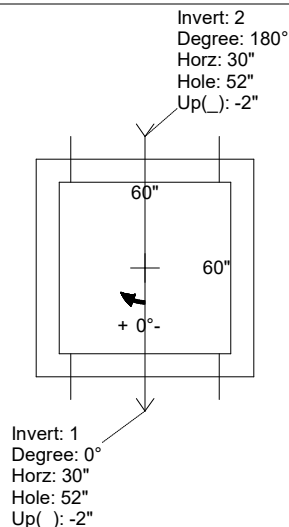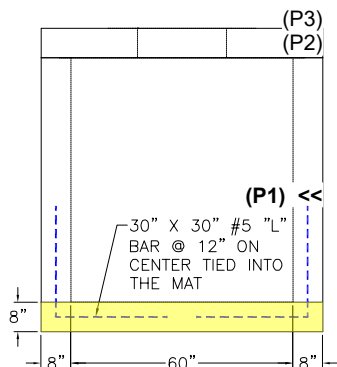

WEIGHTS:

FIRST POUR: 3,877 LBS
SECOND POUR: 9,200 LBS
TOTAL: 13,077 LBS

INSIDE WALL DIMENSIONS

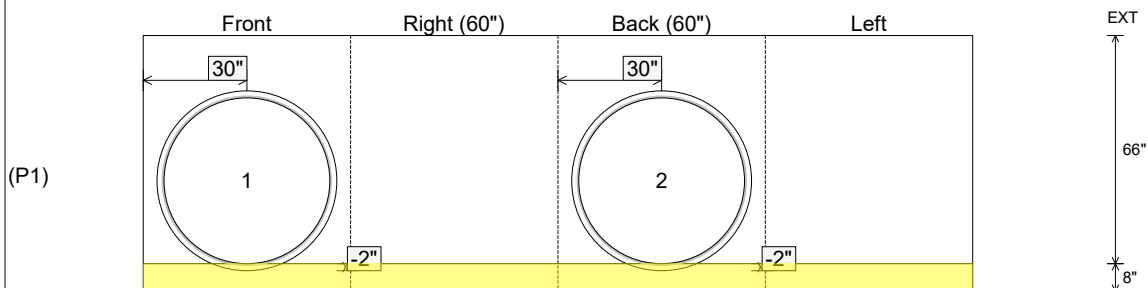

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"


Height (Int): 66"
Height (Ext): 74"

Weight (Net): 13077 lb
Volume (Net): 3.34cu.yd

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/5/2026 8:13:00 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 16+15 JB-B1 INLET 36

P1 BX6060-08BA66

BOX BASE 8inW, 8inF

- P3) CASTING (cast in) - 0
P2) 60" x 60" - BX FLAT LID 8inW SPEC. (KY JB-B1) - 8"
P1) 60" x 60" - BOX BASE 8inW, 8inF - 66"
1) SECONDARY POUR - WALLS
2) Hole - 52

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.).
-CASTING BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

Structure Total:

0 lb
3574 lb
13077 lb
0 lb
0 lb



16651 lb

SECOND POUR DRAWING

Rim: 558.2' Rim to Invert: 6.23' Slack: 0.76" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	551.97'	0°	38"	48" CMP	49"	Hole 52	52"	52"	-2"	0"
Invert 2	551.97'	180°	38"	48" CMP	49"	Hole 52	52"	52"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

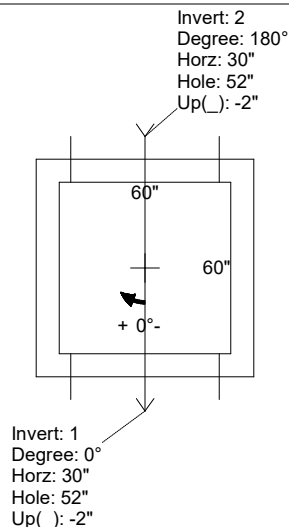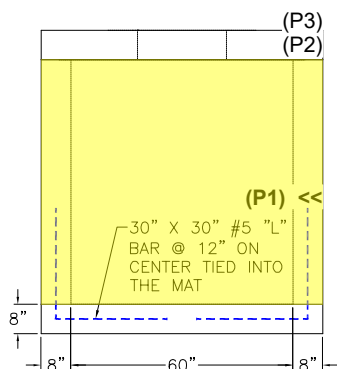

WEIGHTS:


FIRST POUR: 3,877 LBS

SECOND POUR: 9,200 LBS

TOTAL: 13,077 LBS

4 ea. 5CA14 CONAC A-ANCHOTS
FOR PLANT & FIELD HANDLING.
INSTALLED IN 90-DEGREE &
270-DEGREE WALLS, 18" FROM
THE TOP OF THE WALLS.

INSIDE WALL DIMENSIONS

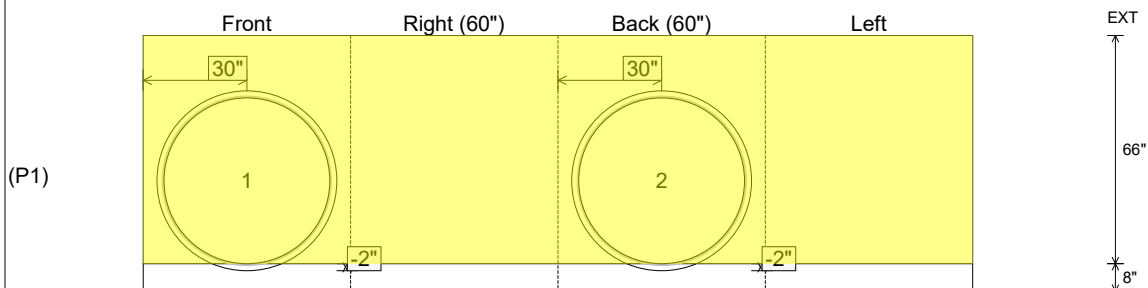

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 66"
Height (Ext): 74"

Weight (Net): 13077 lb
Volume (Net): 3.34cu.yd
