

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:28:52 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 16+15 JB-B1 INLET 36

P2 BX060060-08LD08S

BX FLAT LID 8inW SPEC. (KY JB-B1)

P3) CASTING (cast in) - 0
P2) 60" x 60" - BX FLAT LID 8inW SPEC. (KY JB-B1) - 8"
P1) 60" x 60" - BOX BASE 8inW, 8inF - 66"
2) Hole - 52


Structure Total:

0 lb
3574 lb
13077 lb
0 lb
16651 lb

Structure Notes:

-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.).
-CASTING BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

KYTC STATE PROJECT

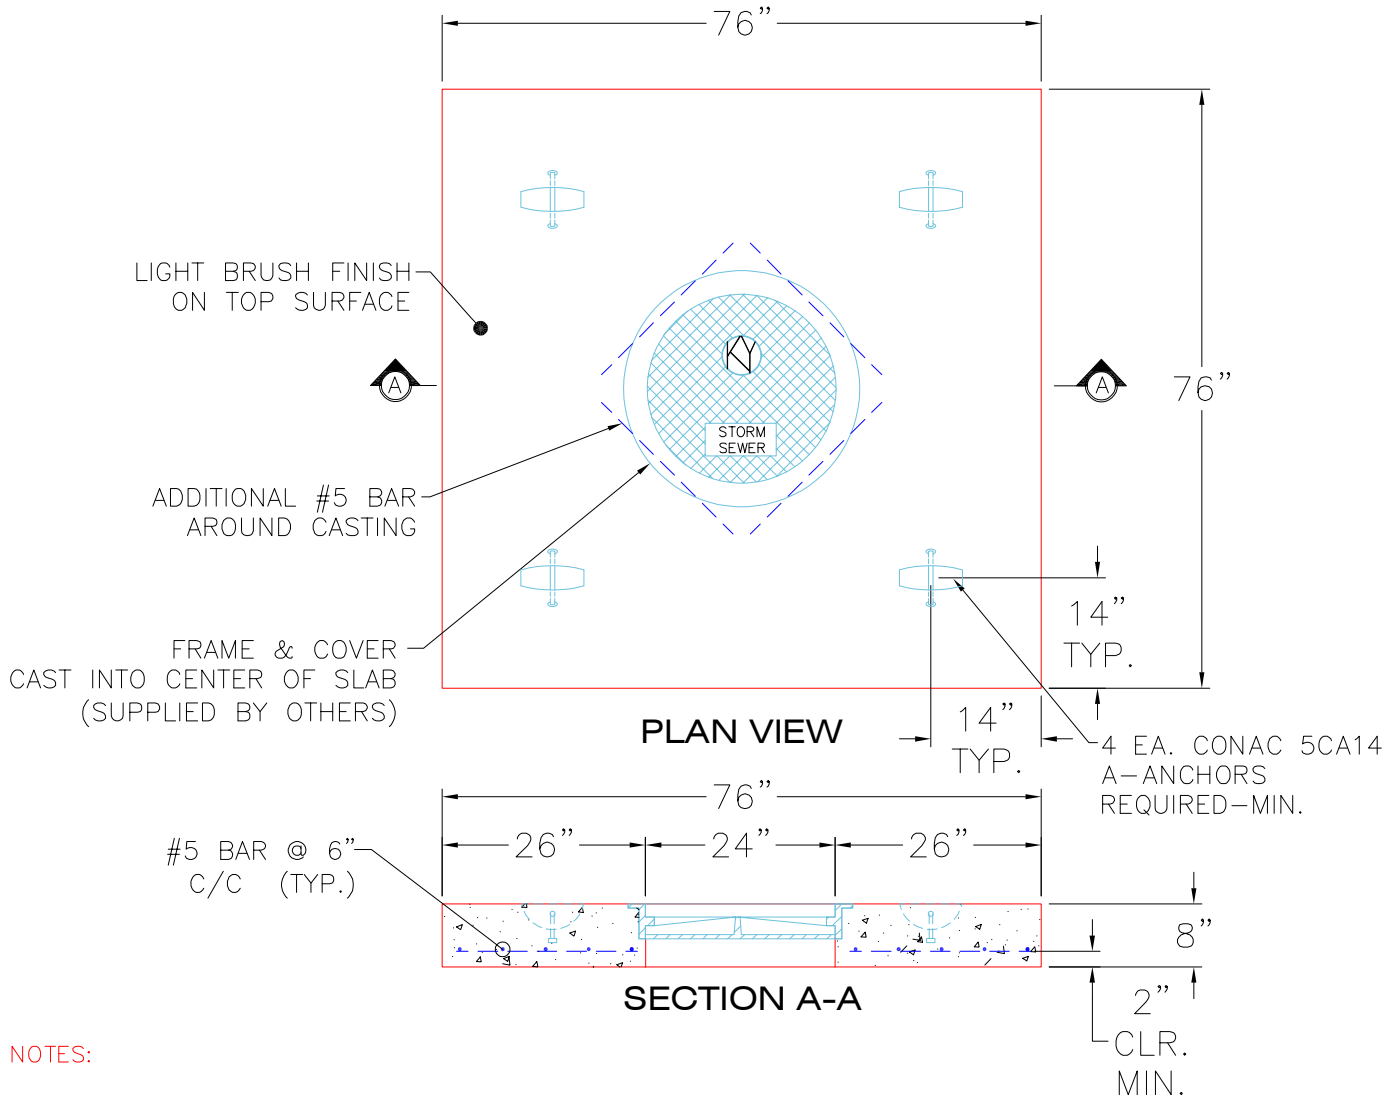

NOTES:

-CONCRETE: 4500 PSI @ 28 DAYS.
-MANUFACTURED TO KYTC & ASTM C-913 SPECIFICATIONS.
-REINFORCING: #4 BAR @ 6" C.C. E.W. -GRADE 60.
-KYTC STATE CERTIFICATIONS REQUIRED.
-4 EA. CONAC 5CA14 A-ANCHORS REQUIRED (MIN.)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 3574 lb
Volume (Net): 0.91cu.yd
