

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, KY	




Slack: 0.76"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.).
- CASTING BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

P3) CASTING (cast in) - 0
P2) 60" x 60" - BX FLAT LID 8inW SPEC. (KY JB-B1) - 8"
P1) 60" x 60" - BOX BASE 8inW, 8inF - 66"
1) SECONDARY POUR - WALLS
2) Hole - 52

0 lb
3574 lb
13077 lb
0 lb
0 lb

Structure Total: 16651 lb

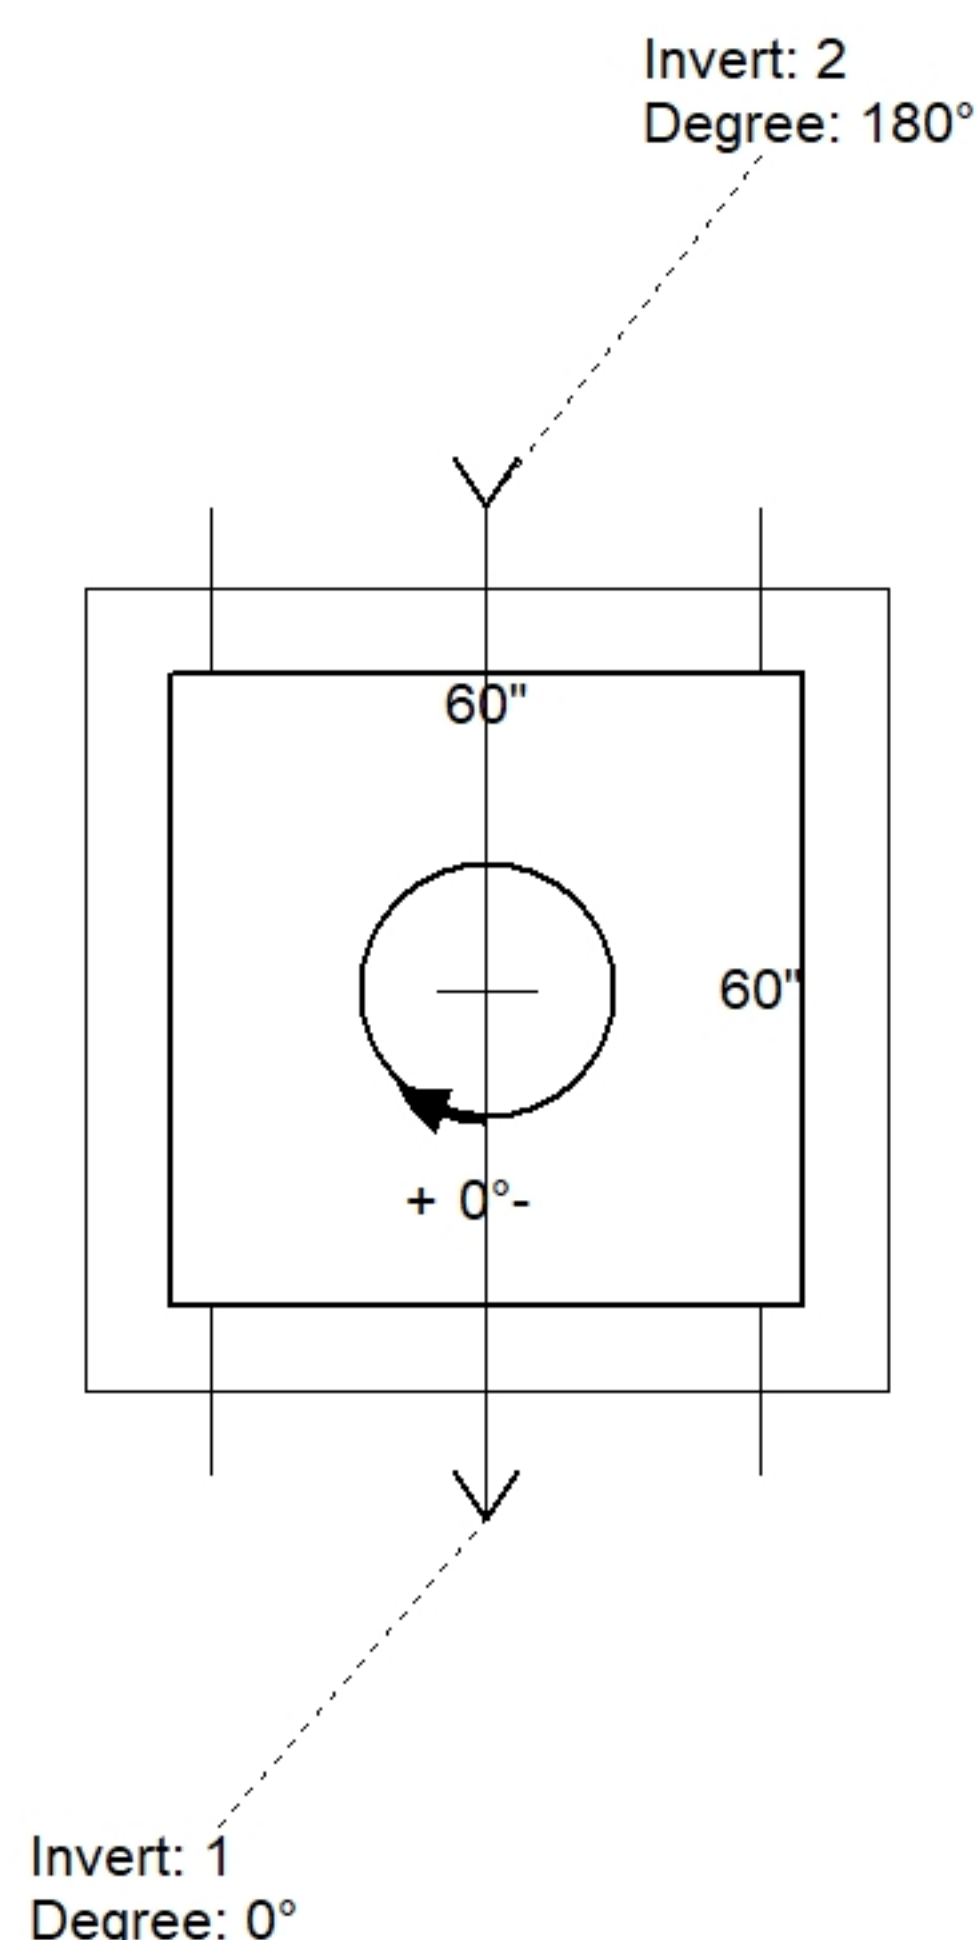


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	558.2'							
Reducer								
Invert 1	551.97'	0°	48" CMP	49"	52"	Hole 52	-2"	P1
Invert 2	551.97'	180°	48" CMP	49"	52"	Hole 52	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

60" x 60" - BX FLAT LID 8inW SPEC. (KY JB-B1) - 8" - (P2)

60" x 60" - BOX BASE 8inW, 8inF - 66" - (P1)

Default - Interior Dimensions

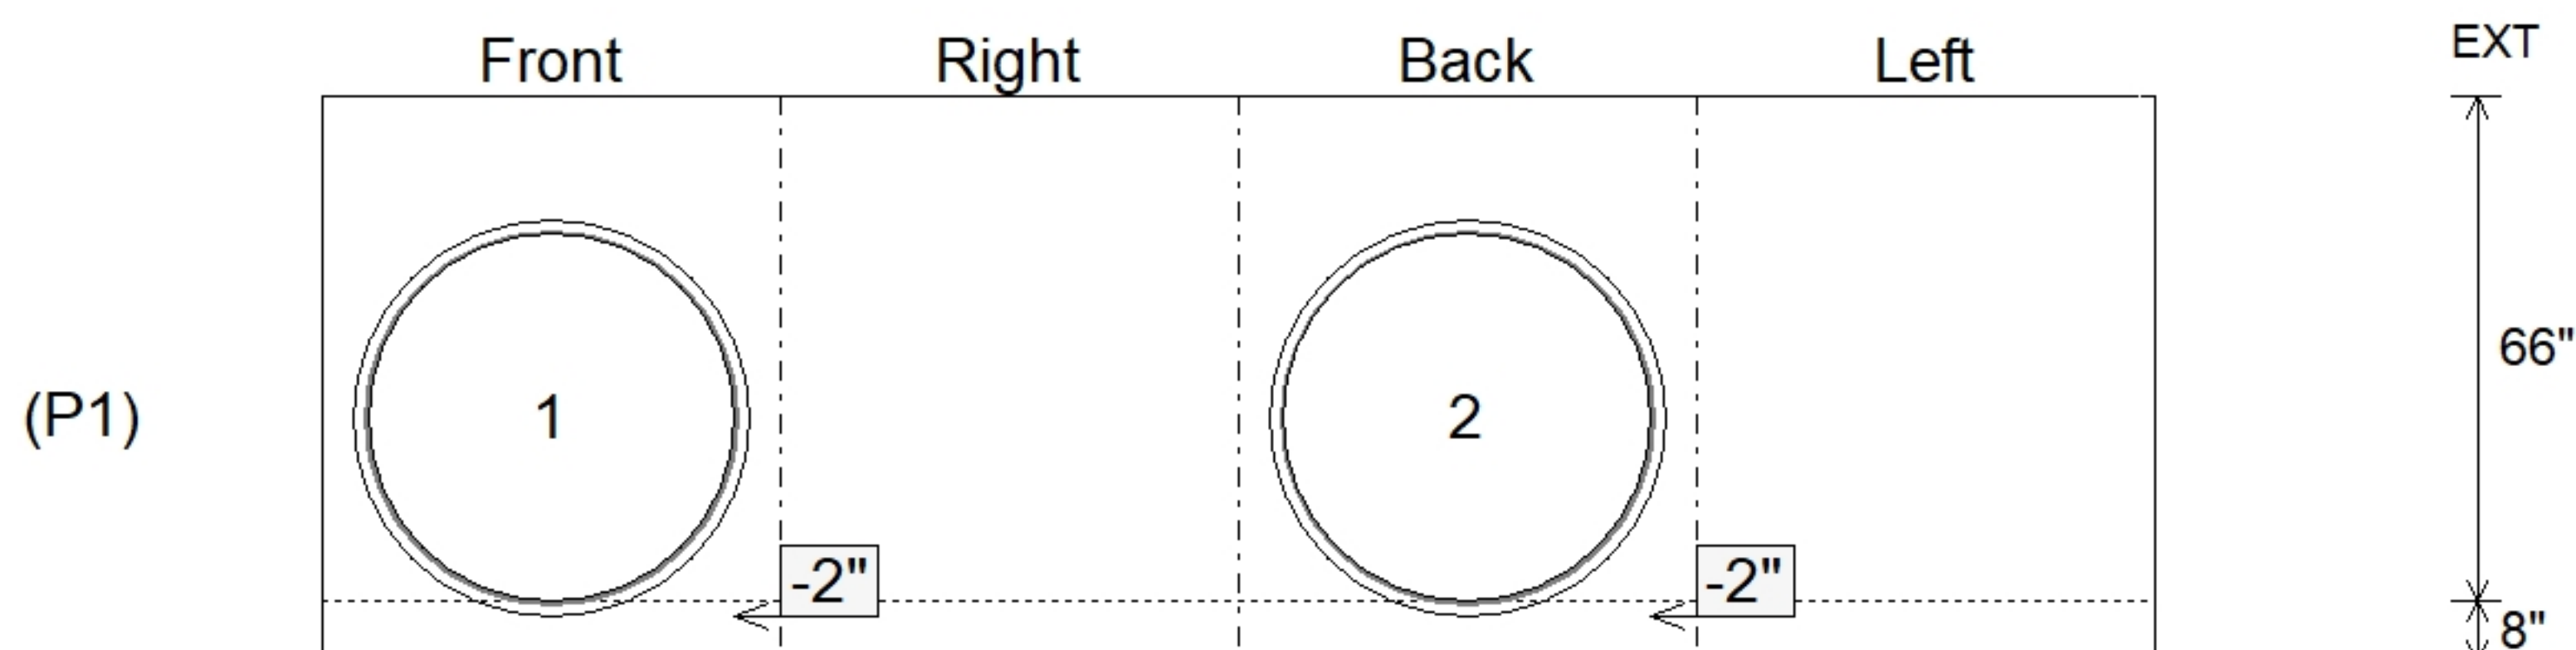

Submittal Drawing
8/10/2026 11:03:00 AM

SUBMITTAL
APPROVED BY:
