

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:26:19 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 16+47 DBI 2-MOD

P1 BX3648-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

P2) 36" x 48" - P.I.P. - BY OTHERS - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 46"
1) 36" x 48" - Conseal CS-102 1.00"
2) Hole - 40

0 lb
6934 lb
0 lb
0 lb

Structure Total: 6934 lb



Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CASTING FRAMES & GRATES BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.
-#5 BAR EXTENDED OUT OF TOP OF BOX 20" AT 12" C/C.

Rim: 556.86' Rim to Invert: 4.5' Slack: 0" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	552.36'	0°	26"	36" CMP	37"	Hole 40	40"	38"	-2"	0"
Invert 2	552.36'	90°	32"	36" CMP	37"	Hole 40	40"	40"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

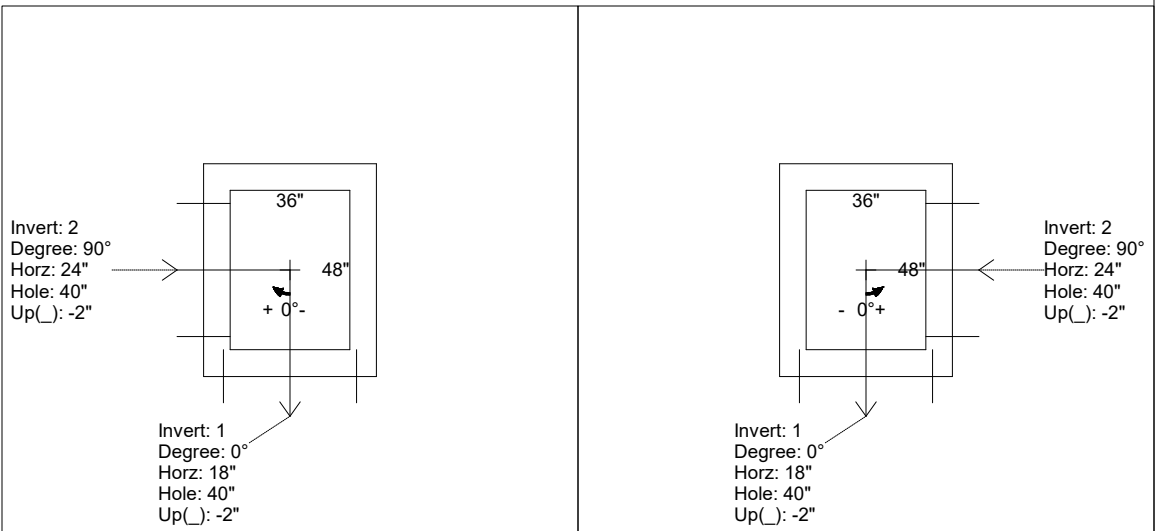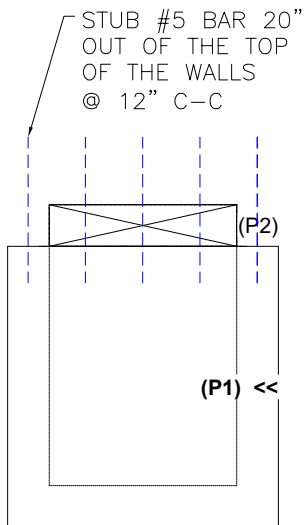

INSIDE WALL DIMENSIONS

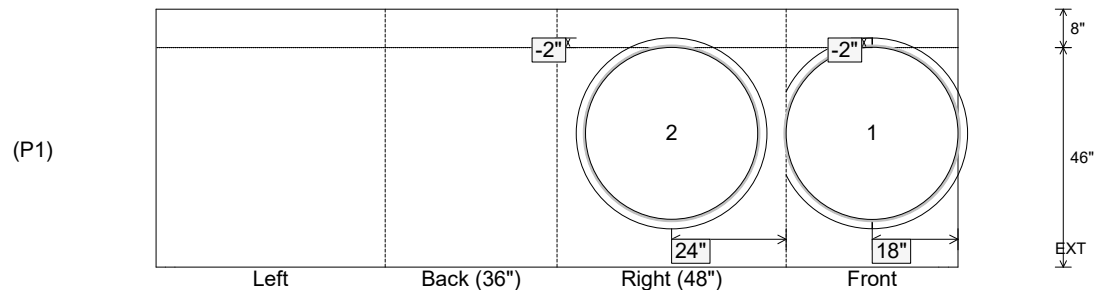

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 46"
Height (Ext): 54"

Weight (Net): 6934 lb
Volume (Net): 1.77cu.yd
