

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/6/2026 12:06:19 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 17+62 CBBI-MOD B1

P1 BX3648-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 45"
1) 36" x 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 40
2) Hole - 22

Structure Notes: .
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CASTING FRAMES & GRATES BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.



Structure Total: 12576 lb

Rim: 562.88' Rim to Invert: 6.2' Slack: 4.4" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	556.68'	90°	32"	36" CMP	37"	Hole 40	40"	40"	-2"	0"
Invert 2	556.68'	180°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 3	556.68'	270°	32"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

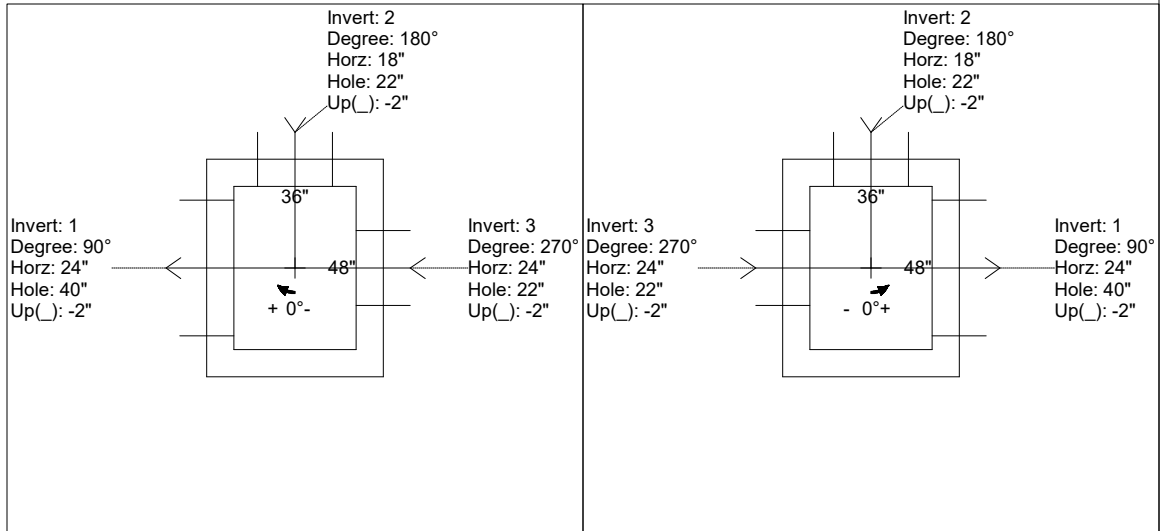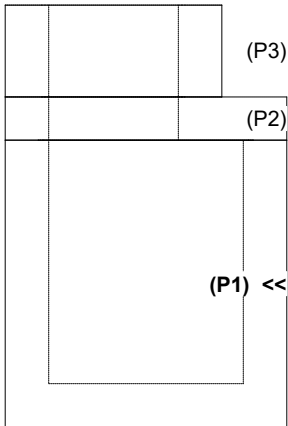

INSIDE WALL DIMENSIONS

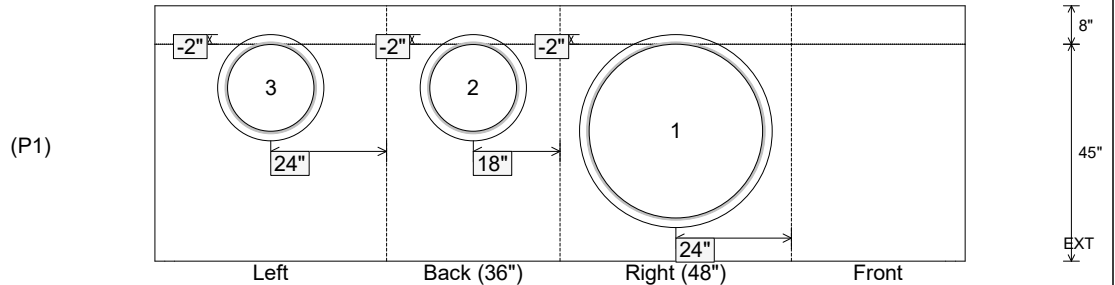

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 45"
Height (Ext): 53"

Weight (Net): 6922 lb
Volume (Net): 1.77cu.yd
