

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/6/2026 12:06:38 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 17+62 CBBI-MOD B1


P3 CMBBIT9-B1LH

CB MED BAR BOX INLET 9B1 LH

- P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 45"
1) 36" x 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 40
2) Hole - 22

- 4000 lb Structure Notes:
1654 lb -KYTC STATE PROJECT 251007
6922 lb -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
0 lb -CASTING FRAMES & GRATES BY OTHERS.
0 lb -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
0 lb -KYTC CERTIFICATIONS REQUIRED.

Structure Total: 12576 lb

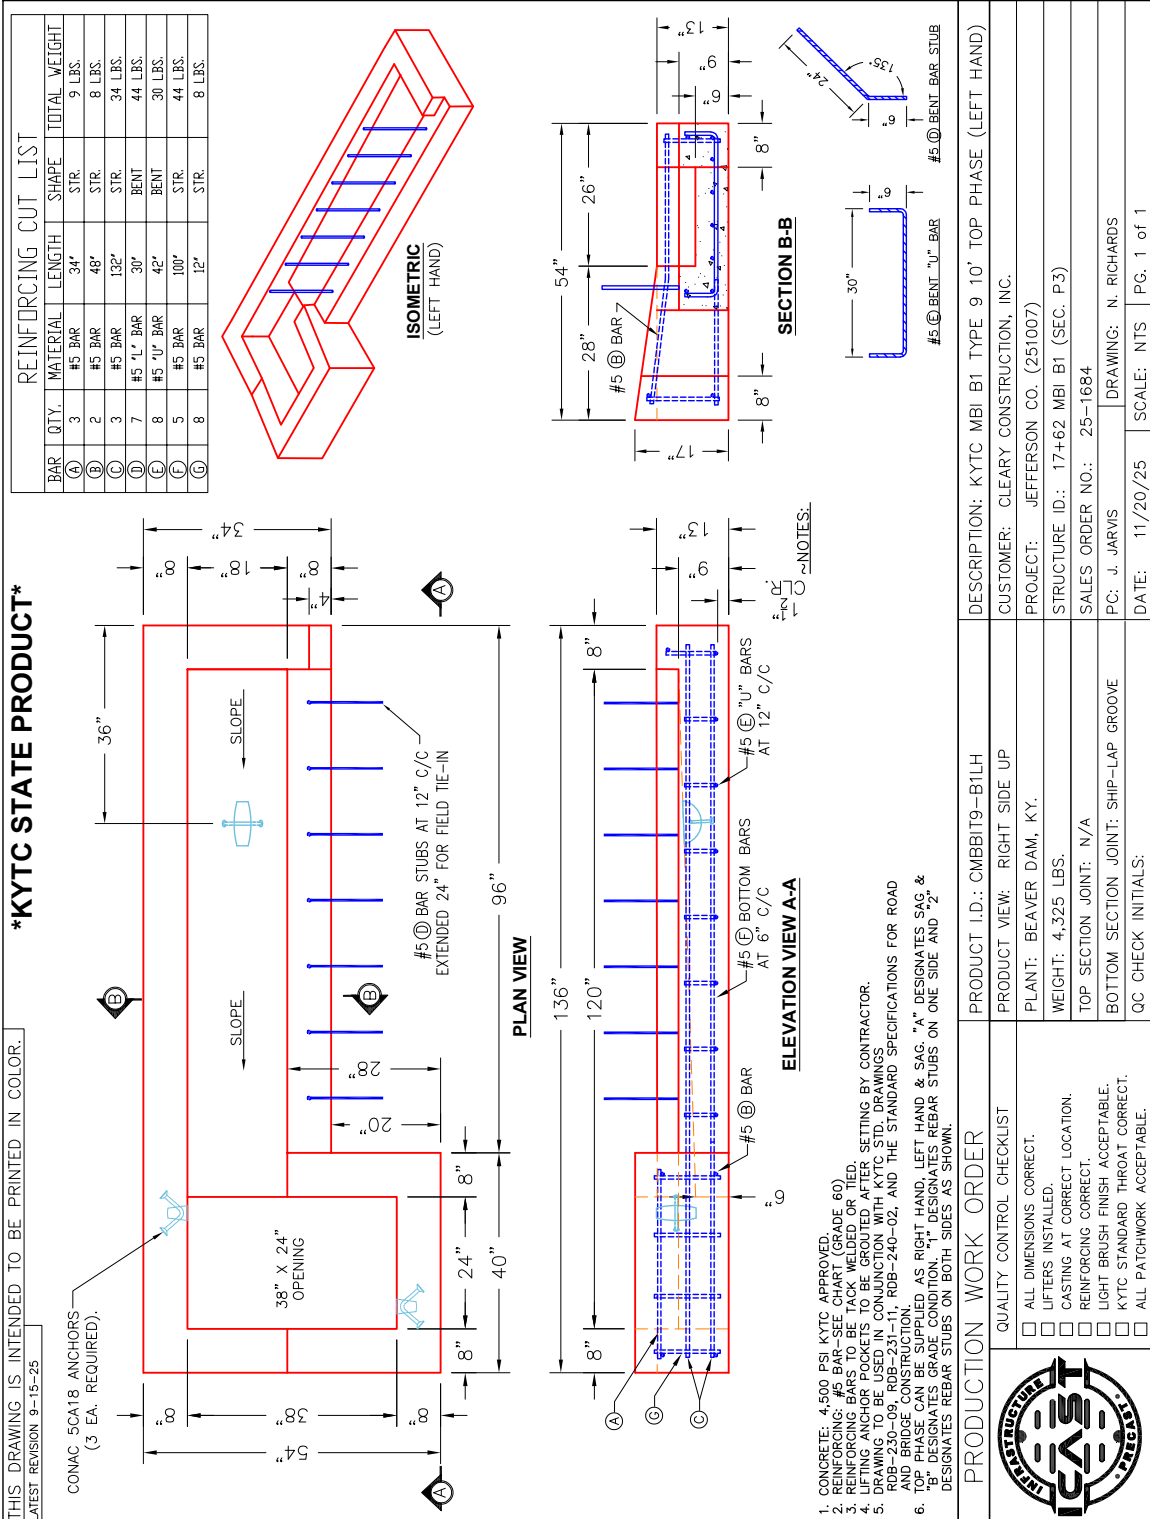

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 17"

Weight (Net): 4000 lb
Volume (Net): 0cu.yd
