

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)  
Job Location: I-264 Louisville, Ky.  
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY  
8/4/2026 11:28:38 AM

Tech: J. Coppage  
PC: T. Ryan



Structure ID: 18+23 CBBI-MOD A1


P2 CMBBIT9-A1SG

CB MED BAR BOX INLET 9A1 SAG

- P3) 24" x 120" - CASTING (cast in) - 3"  
P2) 24" x 120" - CB MED BAR BOX INLET 9A1 SAG - 17"  
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 40"  
1) 24" x 36" - Con seal CS-102 1.00"  
2) Hole - 22

0 lb  
4000 lb  
4967 lb  
0 lb  
0 lb  
Structure Total: 8967 lb

Structure Notes:  
-KYTC STATE PROJECT 251007  
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)  
-CASTING FRAMES & GRATES BY OTHERS.  
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).  
-KYTC CERTIFICATIONS REQUIRED.

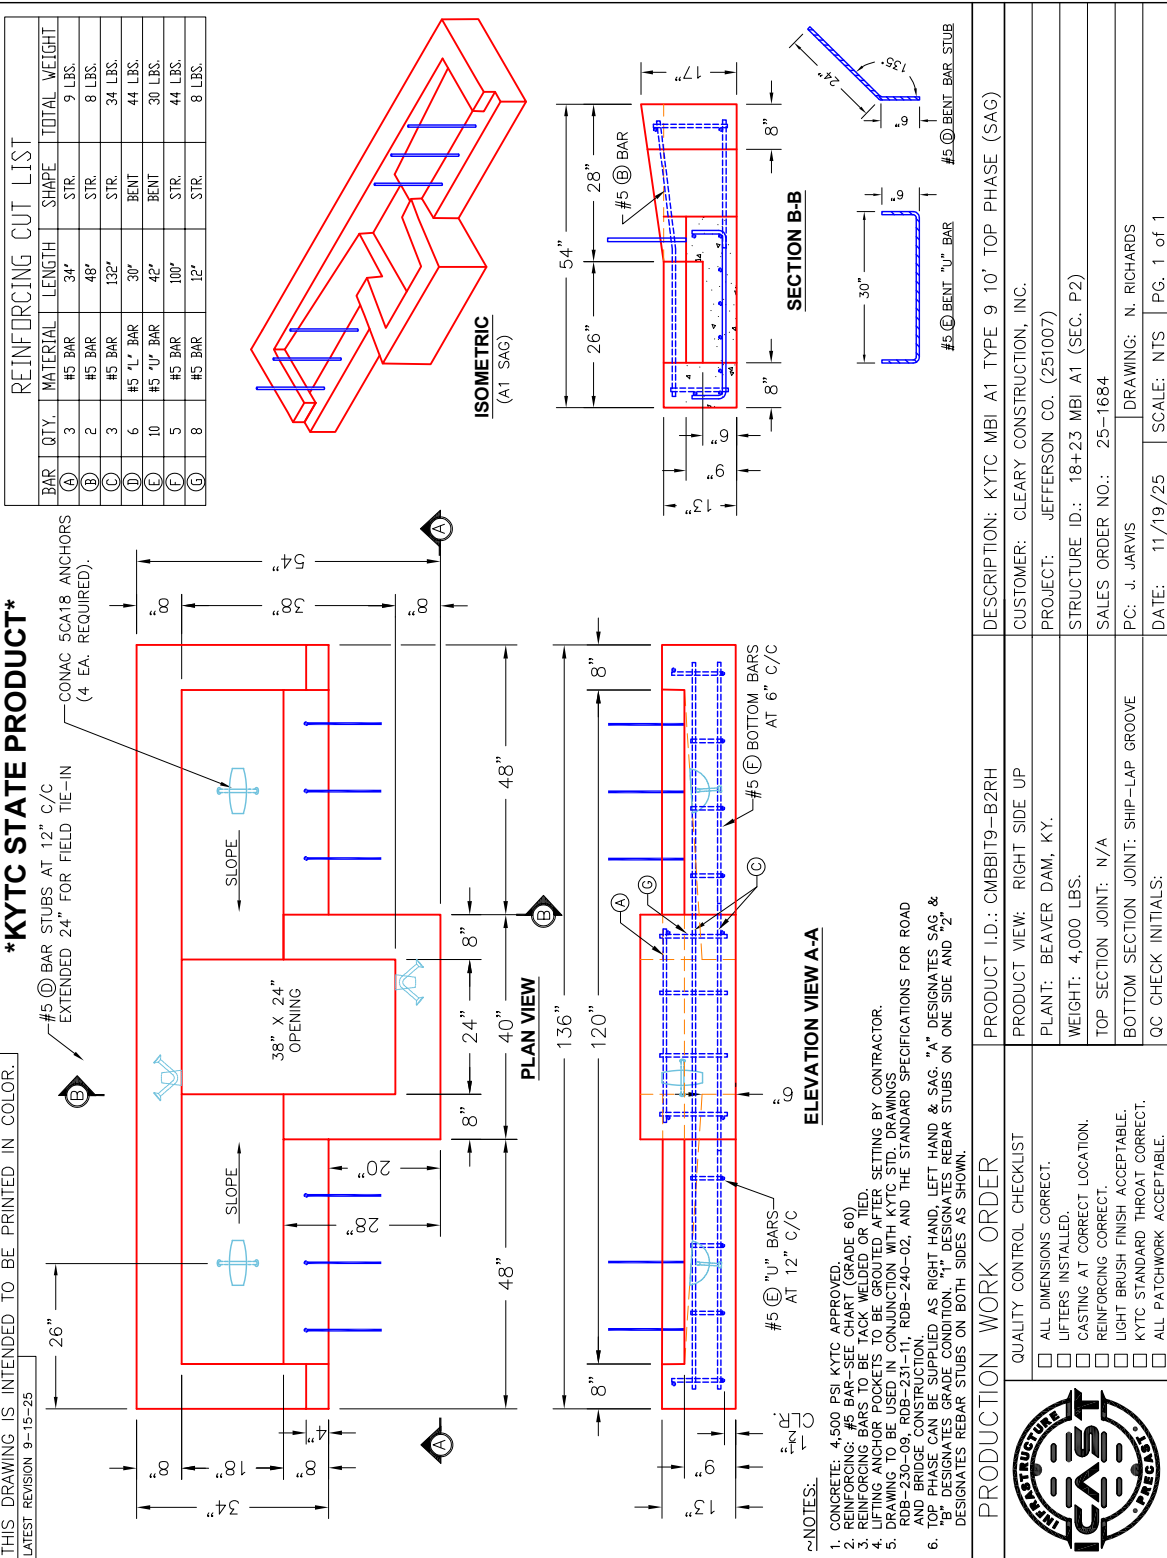

|                                  |                                |                    |                   |                                               |
|----------------------------------|--------------------------------|--------------------|-------------------|-----------------------------------------------|
| Coating (Int):<br>Coating (Ext): | Seam Up: Flat<br>Seam Dn: Flat | Wall Thickness: 8" | Height (Ext): 17" | Weight (Net): 4000 lb<br>Volume (Net): 0cu.yd |
|----------------------------------|--------------------------------|--------------------|-------------------|-----------------------------------------------|
