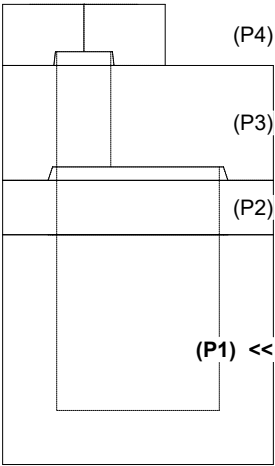
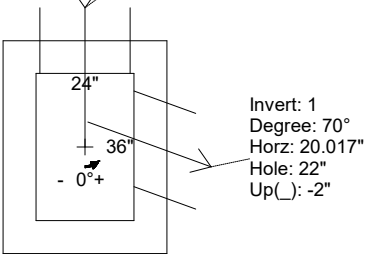
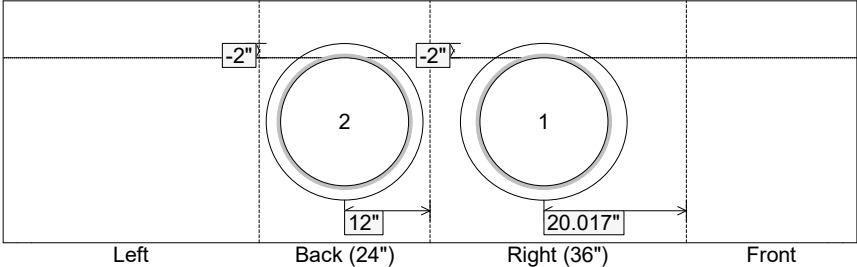


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:52 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 4001+70 LT CBIB INLET 19											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P4) 8" x 120" - CB INLET KY B 10' TOP - 9" P3) 24" x 120" - CB INLET KY B 10' BOTTOM RIGHT - 17" P2) 24" x 36" - CB FT REDUCER 24"x24" HOLE - 8" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26" 1) 24" x 36" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 22"					1660 lb 2650 lb 1010 lb 3523 lb 0 lb 0 lb 0 lb ----- Structure Total: 8842 lb		Structure Notes: -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 588.18' Rim to Invert: 5.28' Slack: 3.36" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	582.9'	70°	25.106"	18" CMP	19"	Hole 22	22"	23.412"	-2"	6"	
Invert 2	582.9'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 26" Height (Ext): 34"		Weight (Net): 3523 lb Volume (Net): 0.9cu.yd		
