

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, KY	




Slack: 3.36"


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

P4) 8" x 120" - CB INLET KY B 10' TOP - 9"	1660 lb
P3) 24" x 120" - CB INLET KY B 10' BOTTOM RIGHT - 17"	2650 lb
P2) 24" x 36" - CB FT REDUCER 24"X24" HOLE - 8"	1010 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"	3523 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) 24" x 24" - Conseal CS-102 1.00"	0 lb
2) Hole - 22	0 lb


Structure Total:	8842 lb

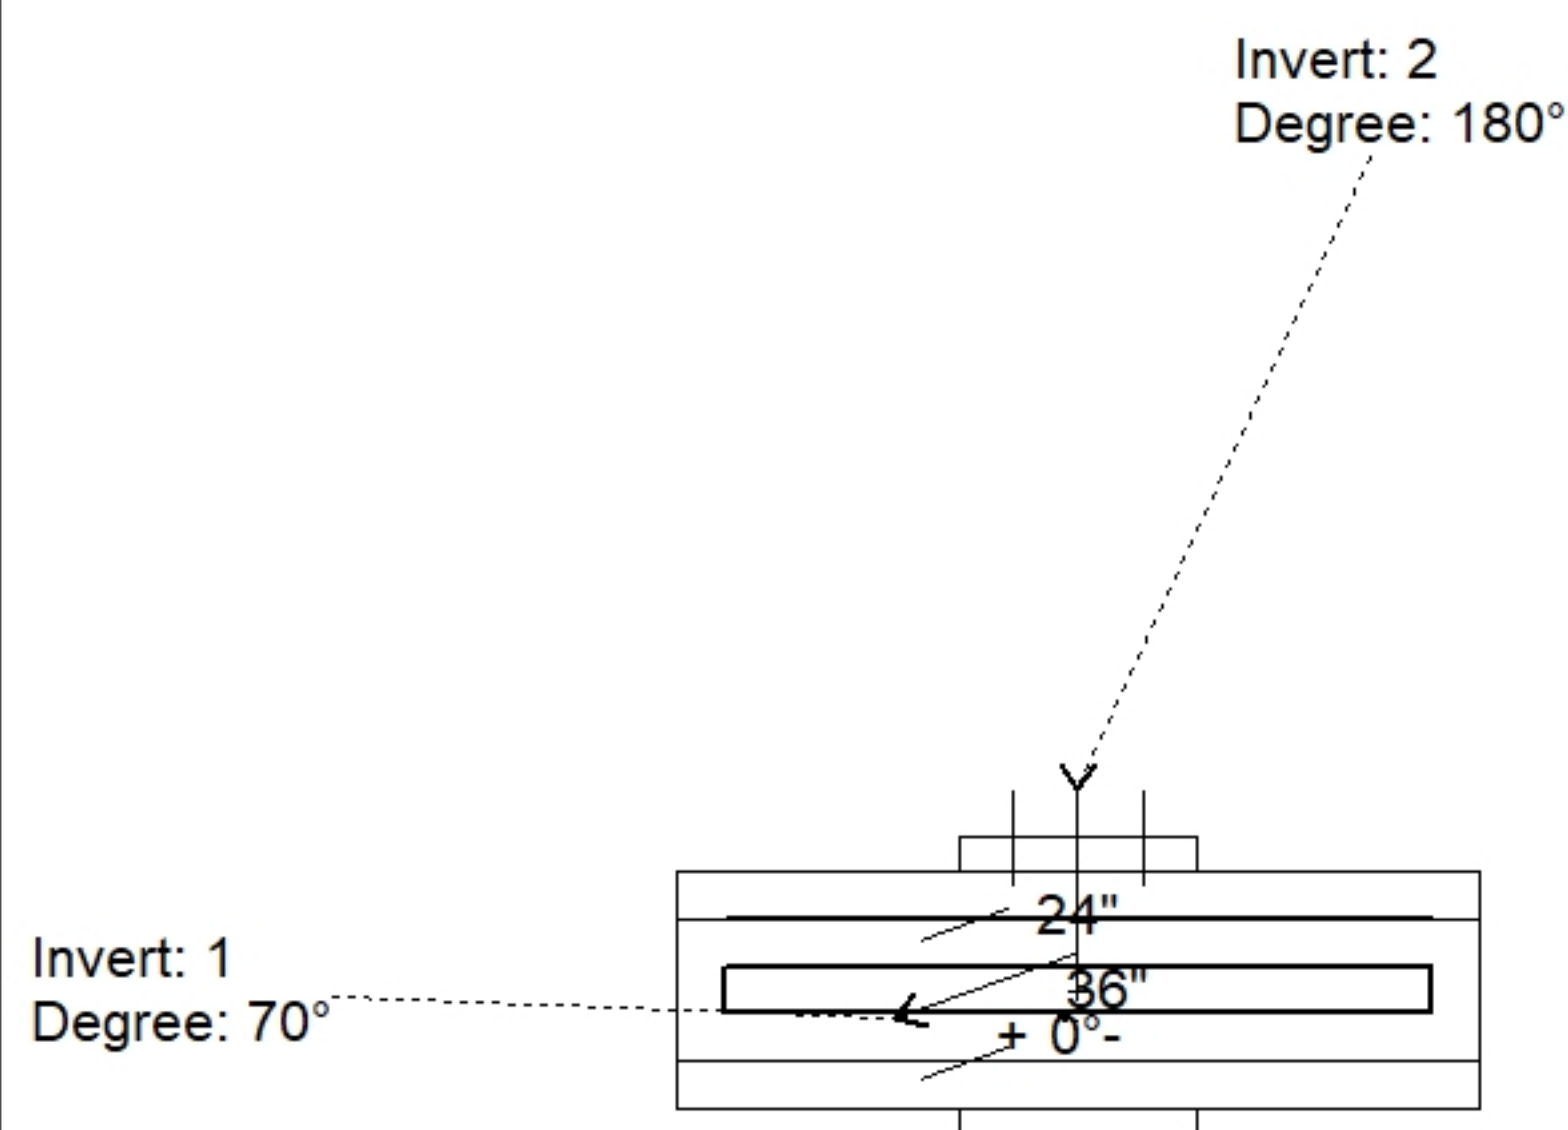

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	588.18'							
Reducer	585.067'							
Invert 1	582.9'	70°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	582.9'	180°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

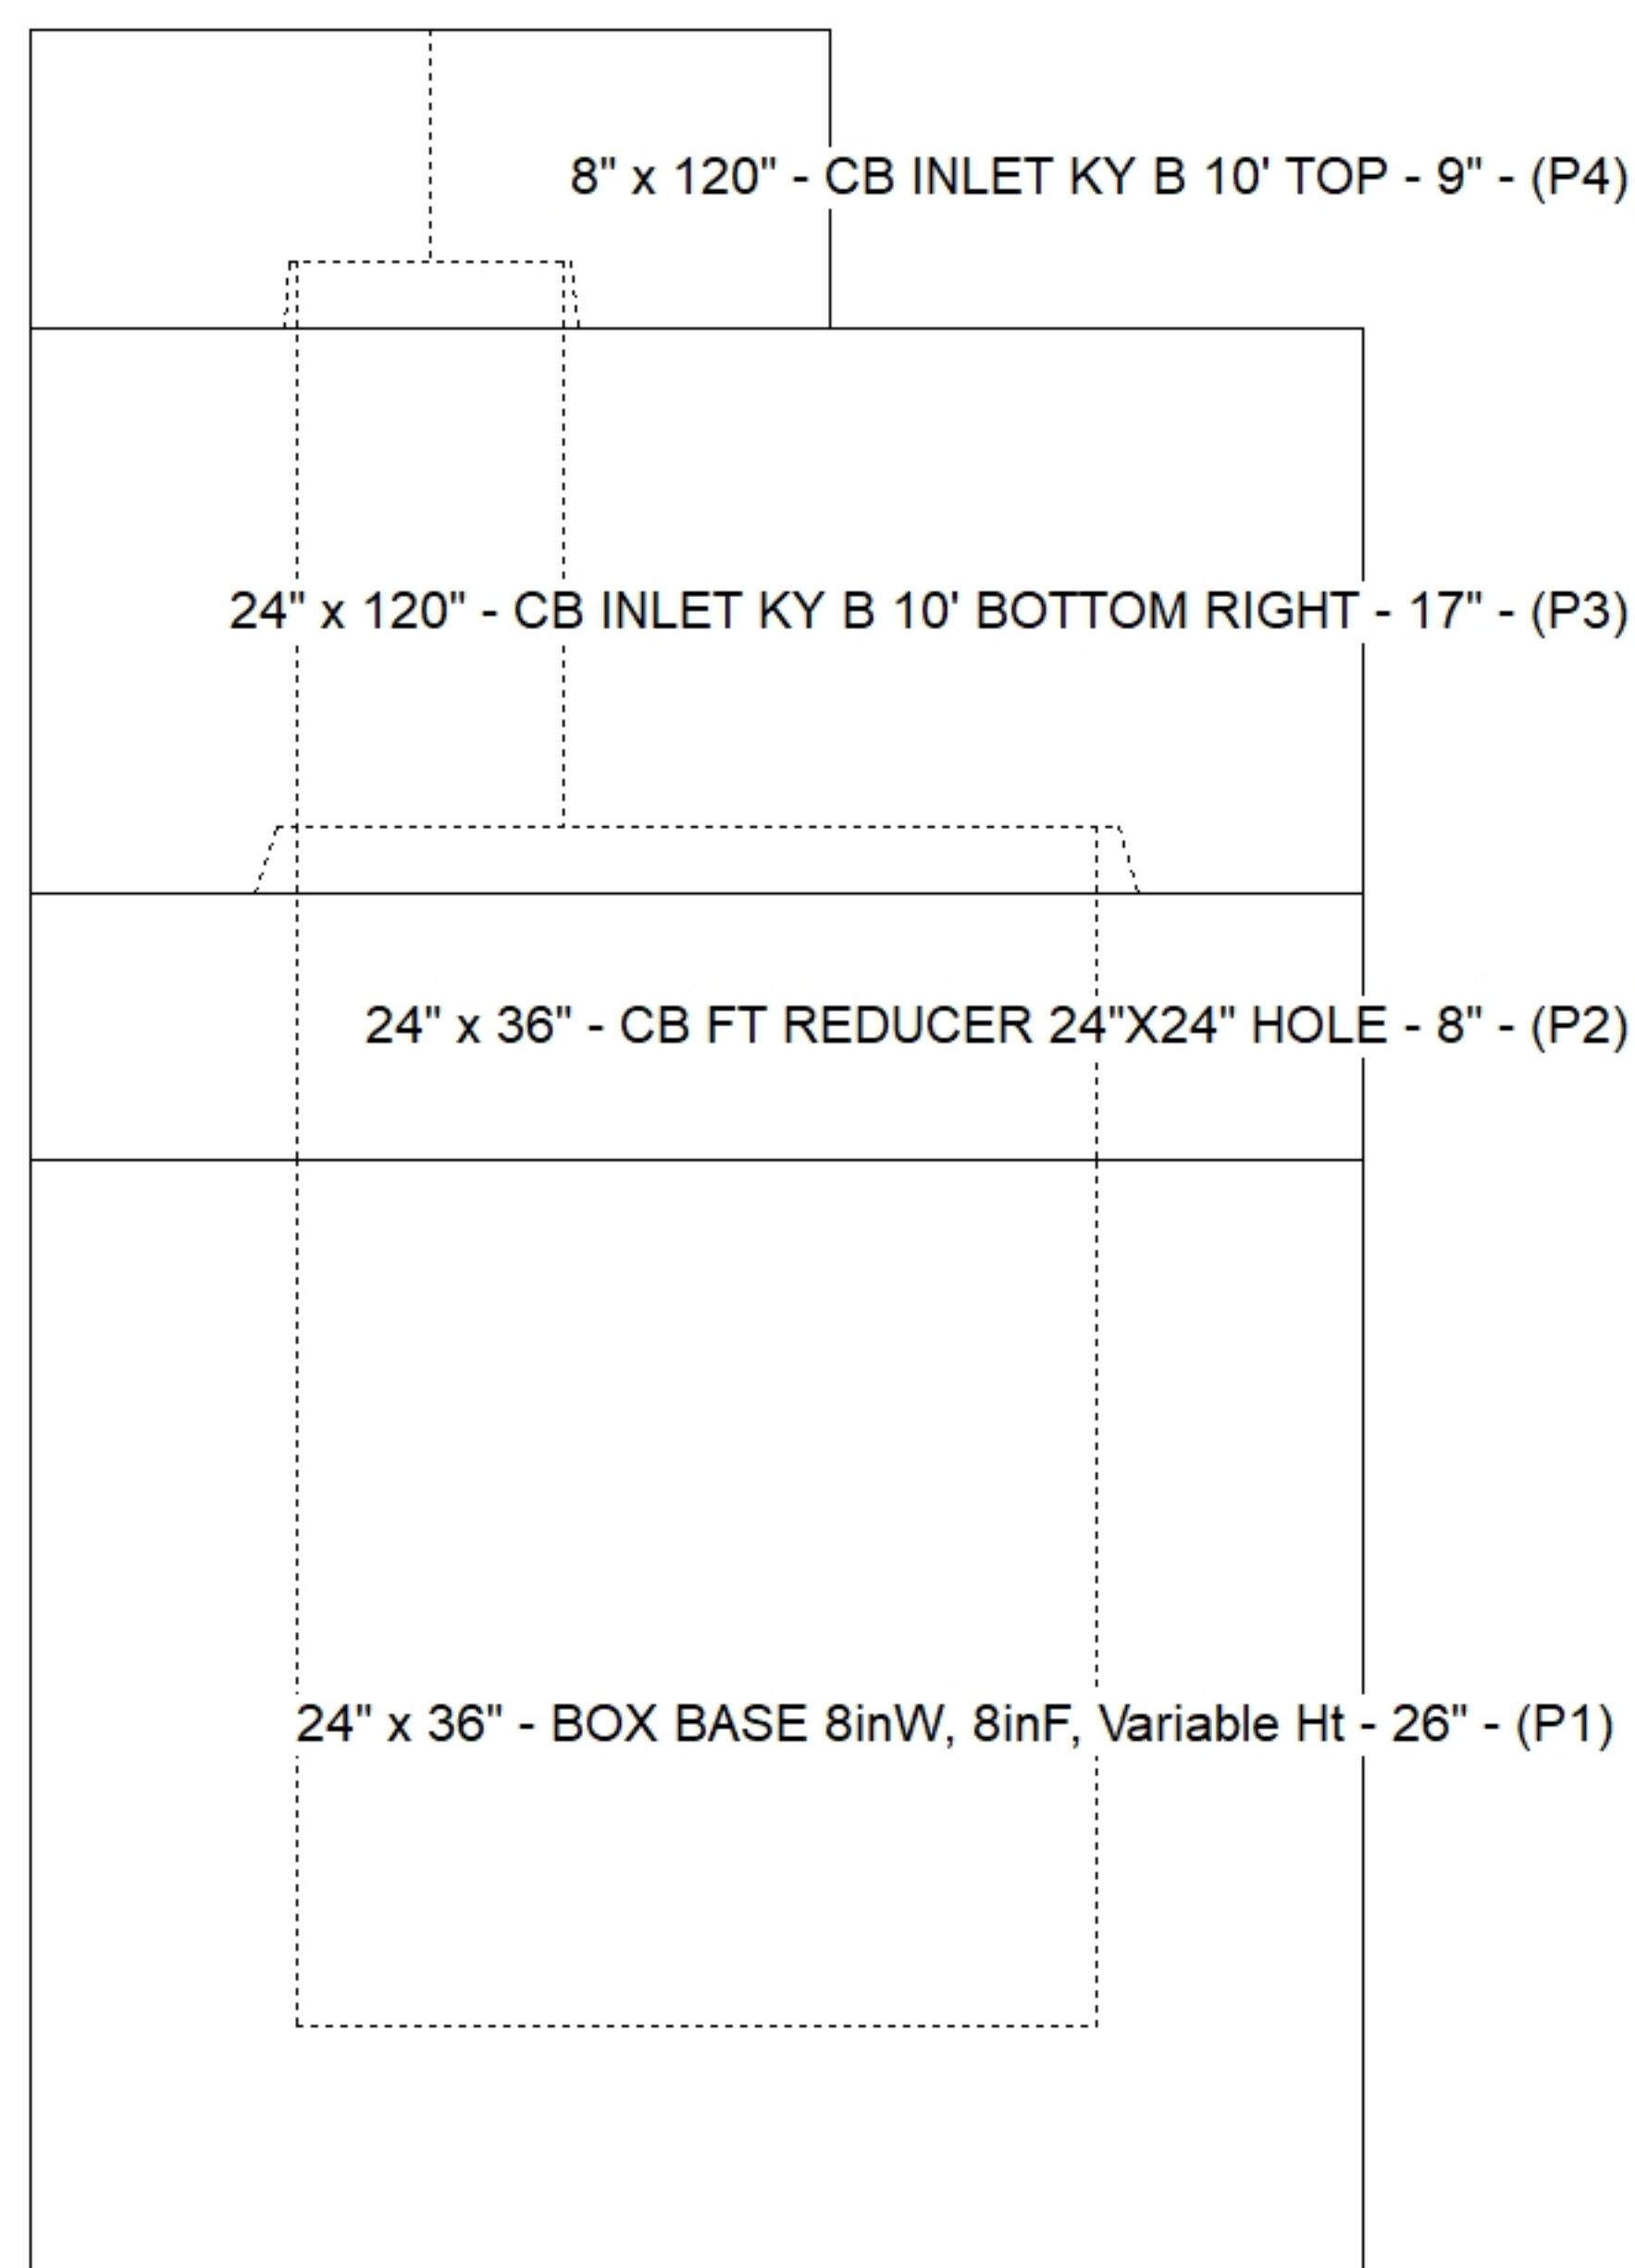

Default - Interior Dimensions

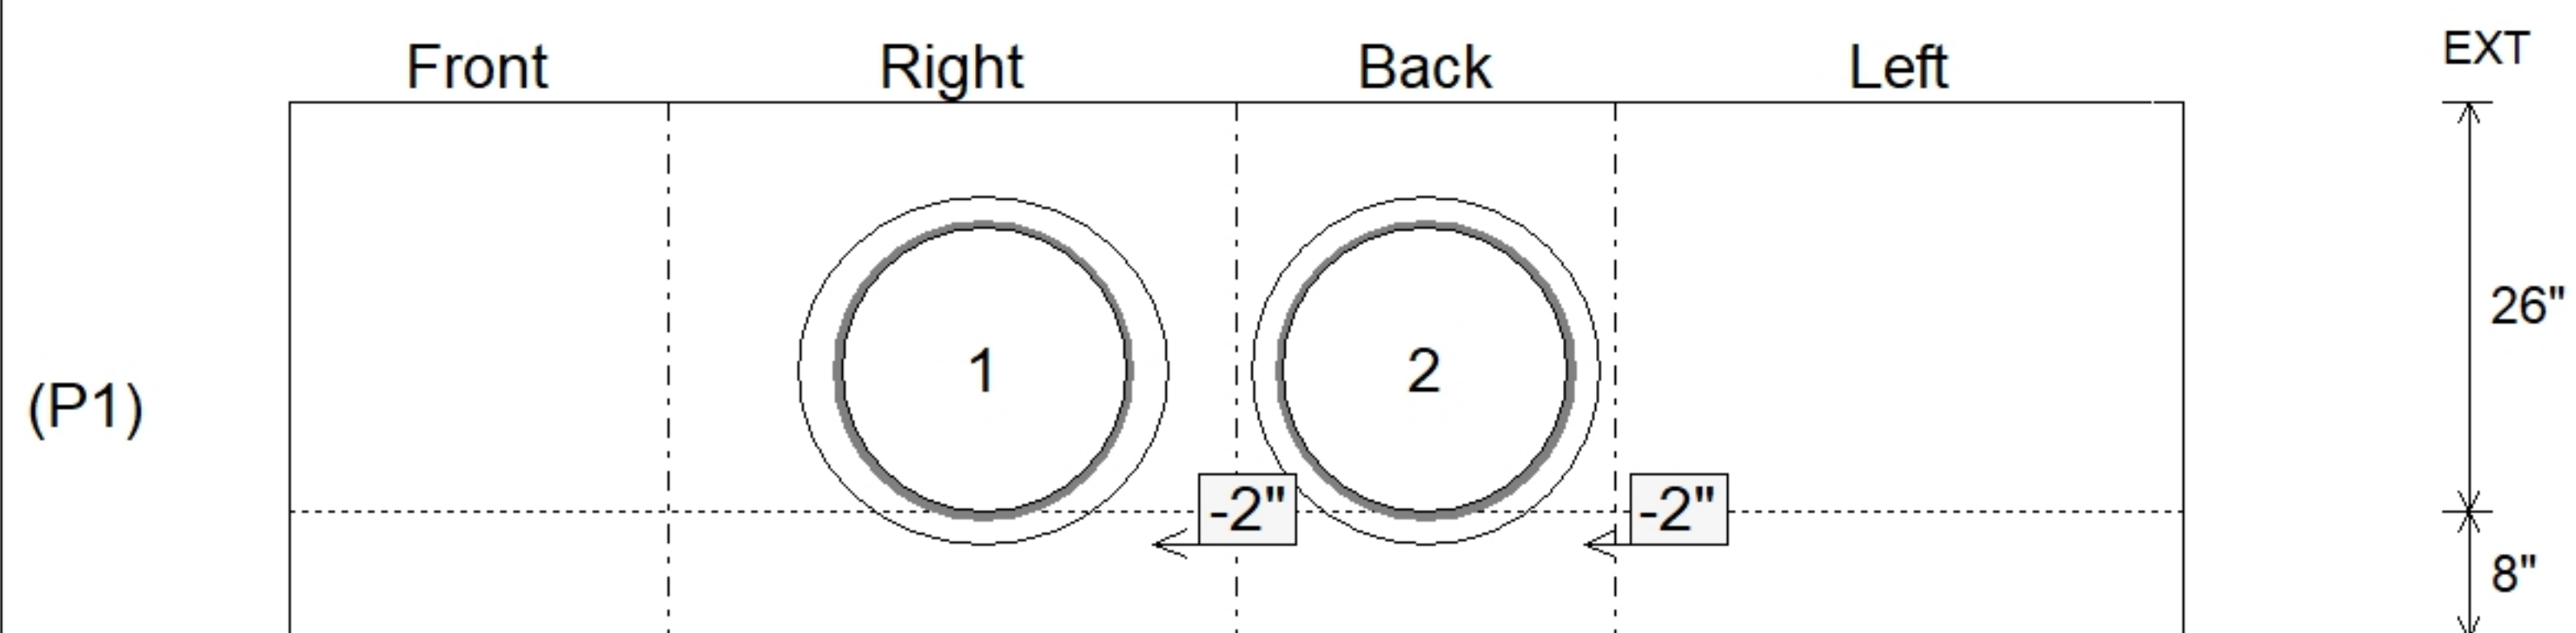

Submittal Drawing
8/10/2026 11:02:57 AM

SUBMITTAL
APPROVED BY:
