



Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:42 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 4006+00 MH-A											
P1 MH048BA30		MH BASE									
P3) 24" - CASTING HEIGHT - 4" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE - 30" 1) 48" - Conseal CS-102 1.00" 2) Hole - 22 5) MH Step ML-10-TDS-NCR - 10"						0 lb 2050 lb 3097 lb 0 lb 0 lb 0 lb ----- Structure Total: 5147 lb		Structure Notes: -KYTC STATE PROJECT 251007 -REINFORCING: PER ASTM C-478 SPECIFICATIONS. -TYPE 1 MANHOLE FRAME & COVER (BY OTHERS). -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.			
Rim: 586.09'		Rim to Invert: 5.2'		Slack: 0.4"		Sump: 2"		Step Position: 180			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	580.89'	0°	0"	18" CMP	19"	Hole 22	22"	22.854"	0"	0"	
Invert 2	580.89'	270°	136.659"	18" CMP	19"	Hole 22	22"	22.854"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

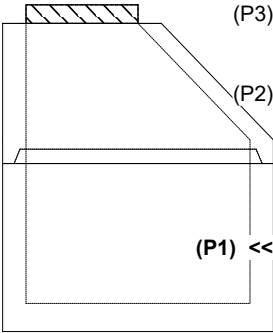


(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

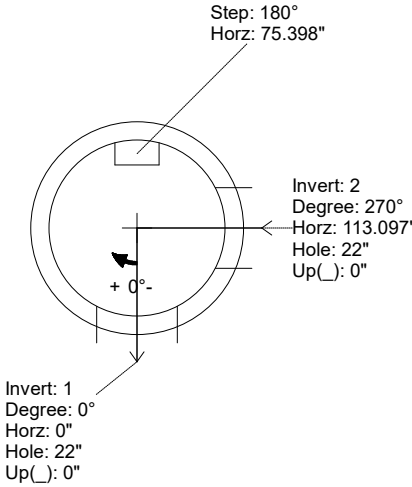

UPSIDE-DOWN VIEW (int. dimensions)

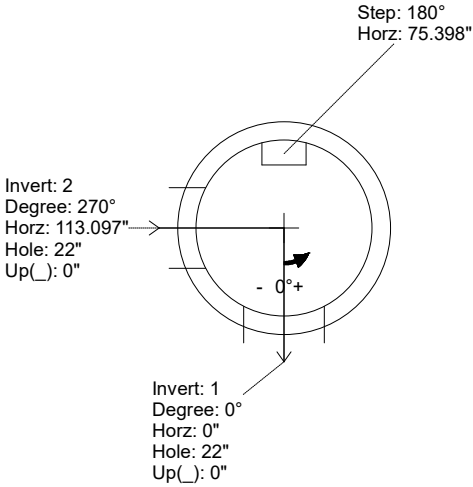

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3097 lb Volume (Net): 0.79cu.yd
----------------------------------	---------------------------------	--	--	--
