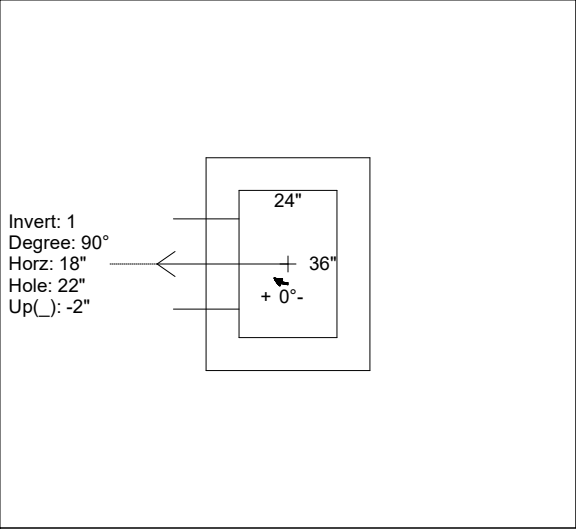
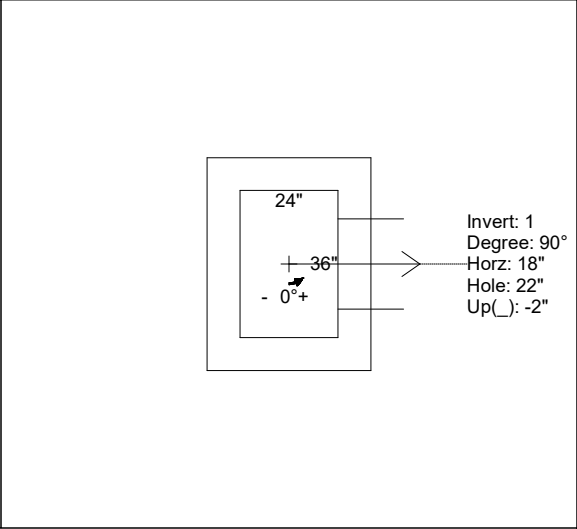
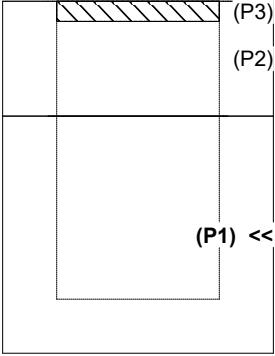
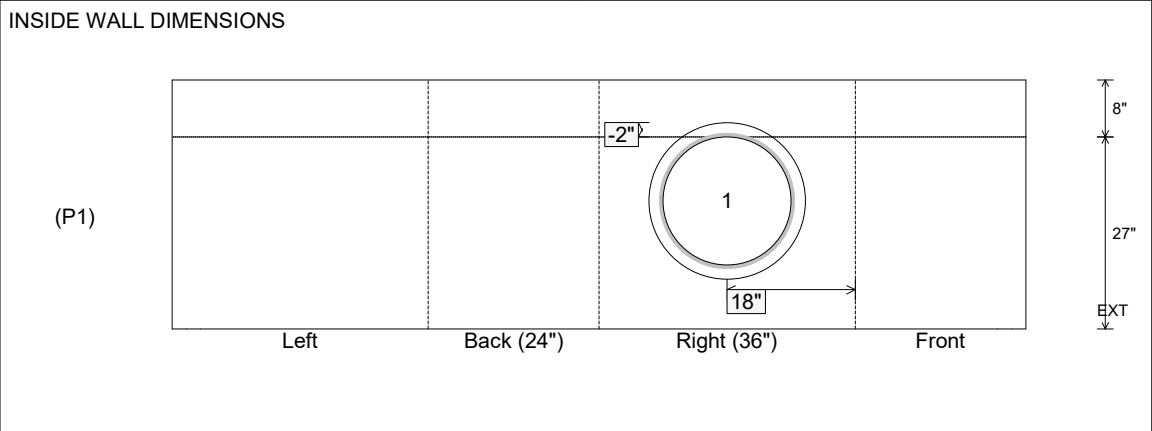


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:55 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 4010+04 LT CBBI-MOD B1											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CASTING (cast in) - 3" P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 27" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22					0 lb 4000 lb 3896 lb 0 lb 0 lb ----- 0 lb Structure Total: 7896 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 582.92'		Rim to Invert: 4'		Slack: 4"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	578.92'	90°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
   INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 27" Height (Ext): 35"		Weight (Net): 3896 lb Volume (Net): 1cu.yd		
