

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:28:51 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 4010+54 LT CBBI-MOD A1

P2 CMBBIT9-A1SG


CB MED BAR BOX INLET 9A1 SAG

- P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9A1 SAG - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 29"
1) 24" x 36" - Con seal CS-102 1.00"
2) Hole - 22

0 lb
4000 lb
3845 lb
0 lb
0 lb

Structure Total: 7845 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CASTING FRAMES & GRATES BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

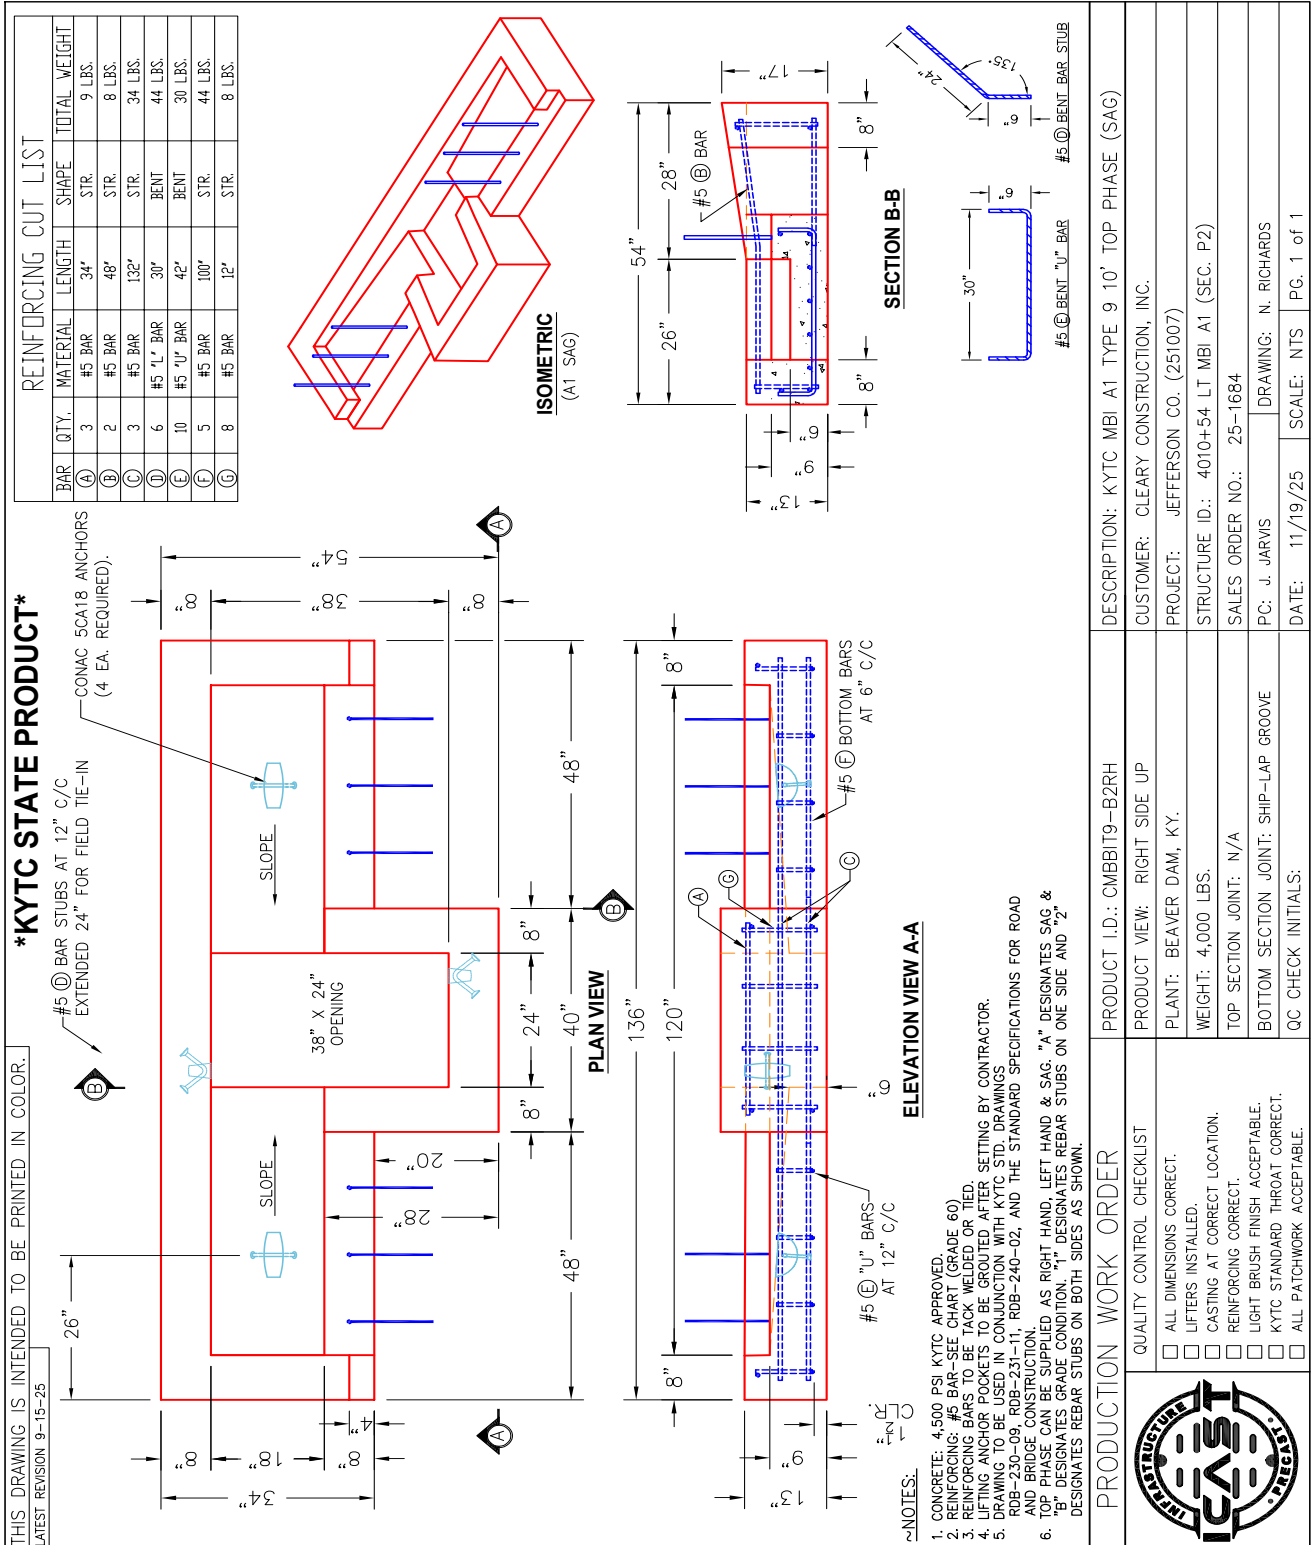

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 17"

Weight (Net): 4000 lb
Volume (Net): 0cu.yd
