




Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/6/2026 2:45:51 PM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 4014+56 LT CBBI-MOD B1											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CASTING (cast in) - 3" P2) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 25" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 4000 lb 3776 lb 0 lb 0 lb ----- 7776 lb Structure Total:		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 587.11' Rim to Invert: 3.9' Slack: 4.8" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	583.21'	90°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

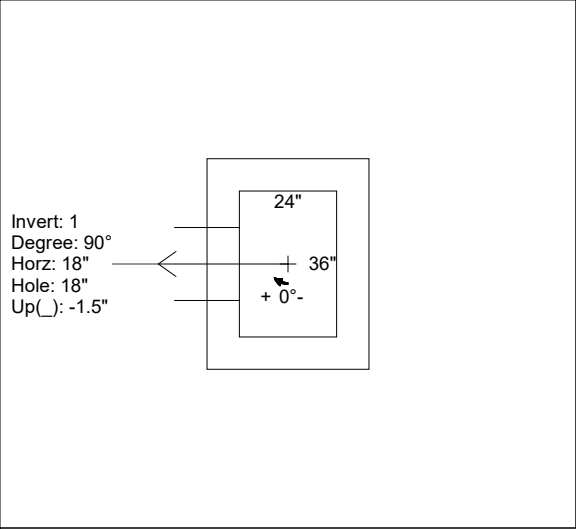

RIGHT-SIDE UP VIEW (int. dimensions)

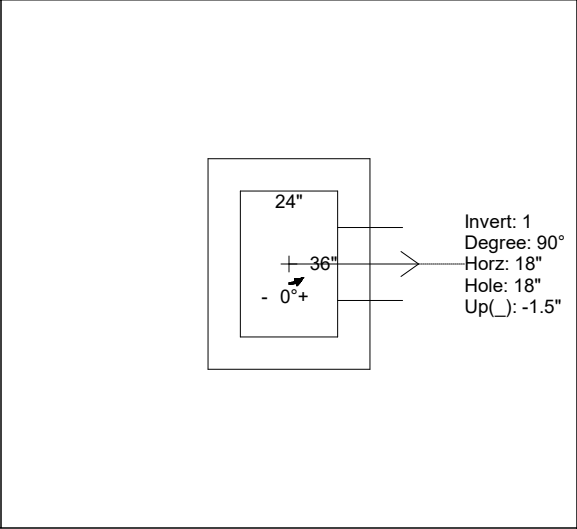

UPSIDE-DOWN VIEW (int. dimensions)

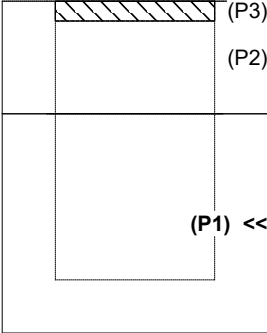


(P3)
(P2)
(P1) <<

INVERT: 1
Degree: 90°
Horz: 18"
Hole: 18"
Up(_): -1.5"

INVERT: 1
Degree: 90°
Horz: 18"
Hole: 18"
Up(_): -1.5"

INSIDE WALL DIMENSIONS

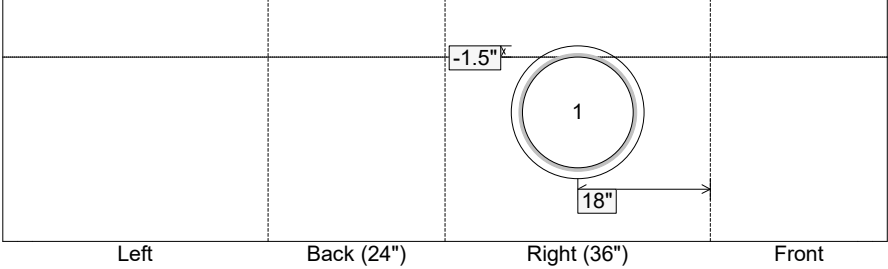

(P1)

Left Back (24") Right (36") Front

18"

25"

8"

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 25" Height (Ext): 33"	Weight (Net): 3776 lb Volume (Net): 0.96cu.yd
----------------------------------	-------------------------------	--	--	--
