

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:28:48 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 5014+69 LT DBI-10 MOD


P2 BX024030-08LD08-16x28

BX FLAT LID 8inW w/16"x28" HOLE

P3) 16" x 28" - CASTING HEIGHT - 5"
P2) 24" x 30" - BX FLAT LID 8inW w/16"x28" HOLE - 8"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 35"
1) 24" x 30" - Conseal CS-102 1.00"
1) Hole - 22
1) Hole - 18

Structure Total: 5033 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-DBI FRAME & GRATE (BY OTHERS).
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

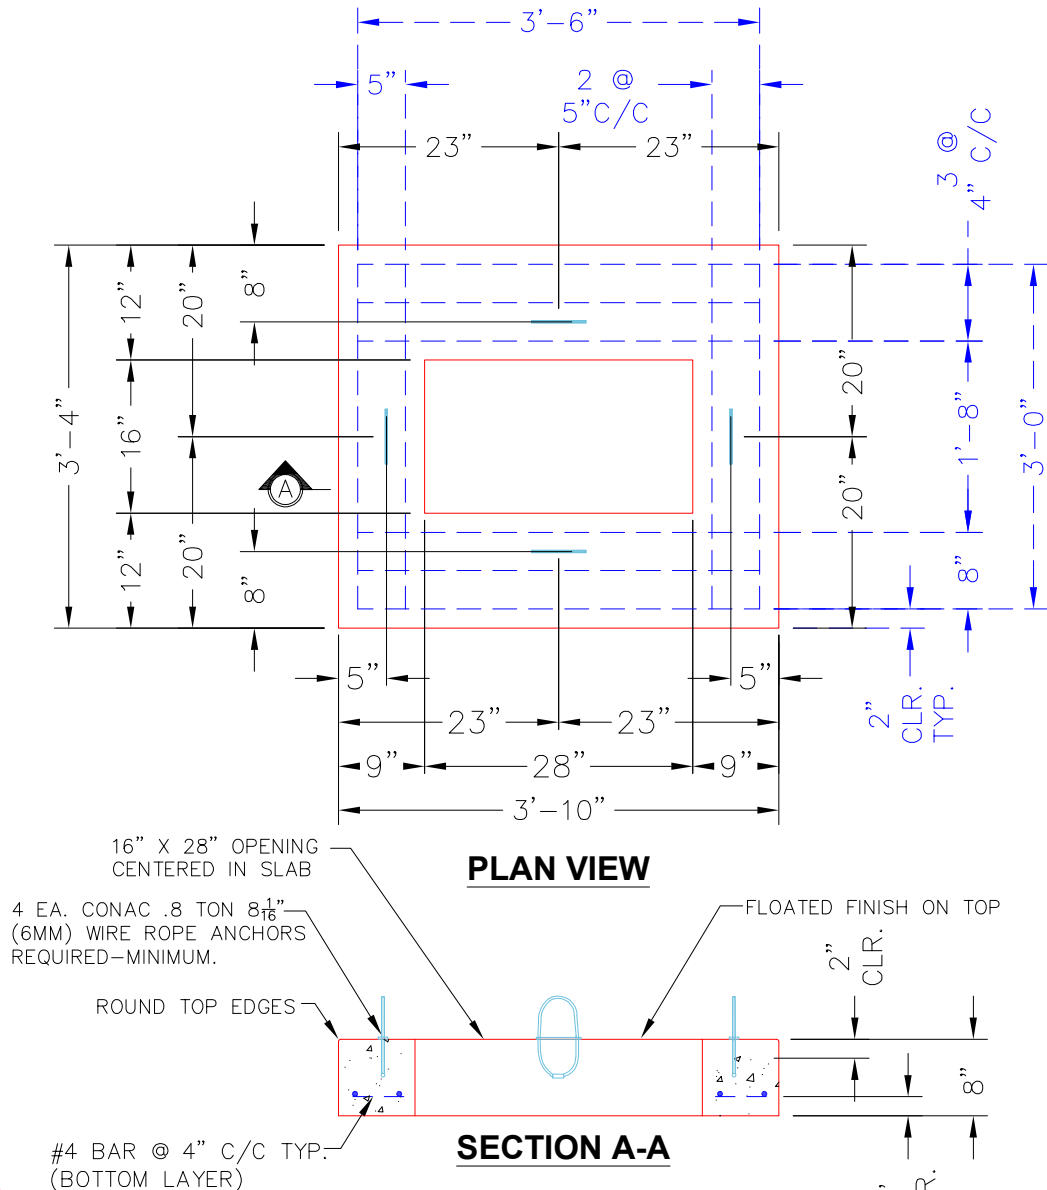

NOTES:

-CONCRETE: 4500 PSI @ 28 DAYS.
-MANUFACTURED TO ASTM C-913 SPECIFICATIONS.
-REINFORCING: #4 BAR AS SHOWN-GRADE 60.
-4 EA. CONAC WIRE LOOP LIFTS REQUIRED (MIN.)

#4 BAR CUT LIST
6 EA. @ 42" LG.
4 EA. @ 36" LG.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 934 lb
Volume (Net): 0.24cu.yd
