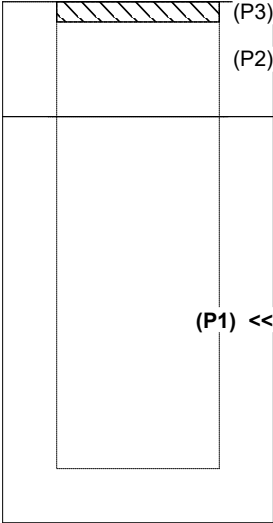
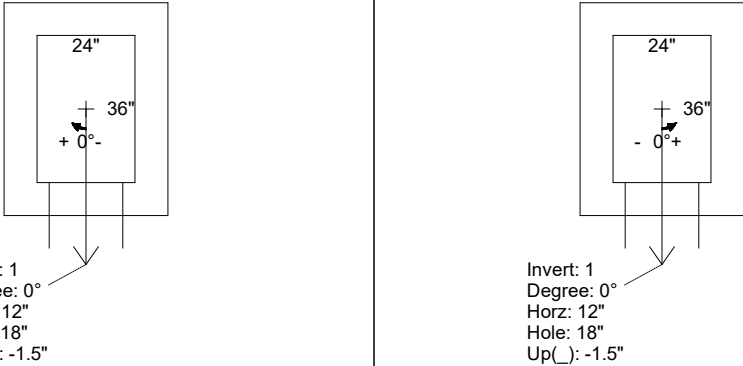
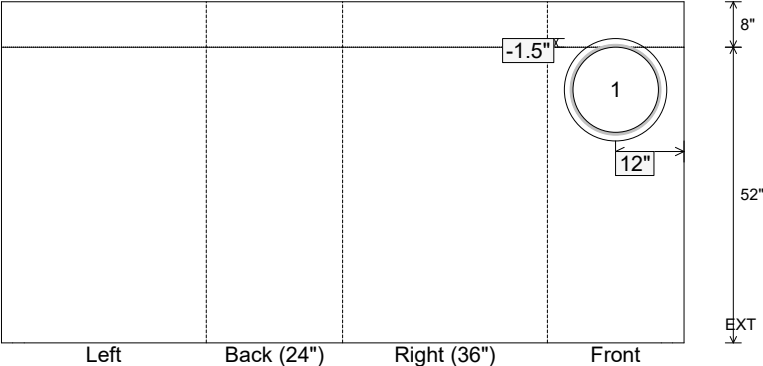


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:27 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 5077+33 RT CBBI-MOD B1											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CASTING (cast in) - 3" P2) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 52" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18						0 lb 4000 lb 6531 lb 0 lb 0 lb ----- Structure Total: 10531 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.			
Rim: 578.69' Rim to Invert: 6.1' Slack: 4.2" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	572.59'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)						UPSIDE-DOWN VIEW (int. dimenions)					
											
INSIDE WALL DIMENSIONS											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 52" Height (Ext): 60"		Weight (Net): 6531 lb Volume (Net): 1.67cu.yd		
