

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:28:42 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 5077+33 RT CBBI-MOD B1

P2 CMBBIT9-B1RH


CB MED BAR BOX INLET 9B1 RH

- P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 52"
1) 24" x 36" - Con seal CS-102 1.00"
1) Hole - 18

0 lb
4000 lb
6531 lb
0 lb
0 lb

Structure Total: 10531 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CASTING FRAMES & GRATES BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

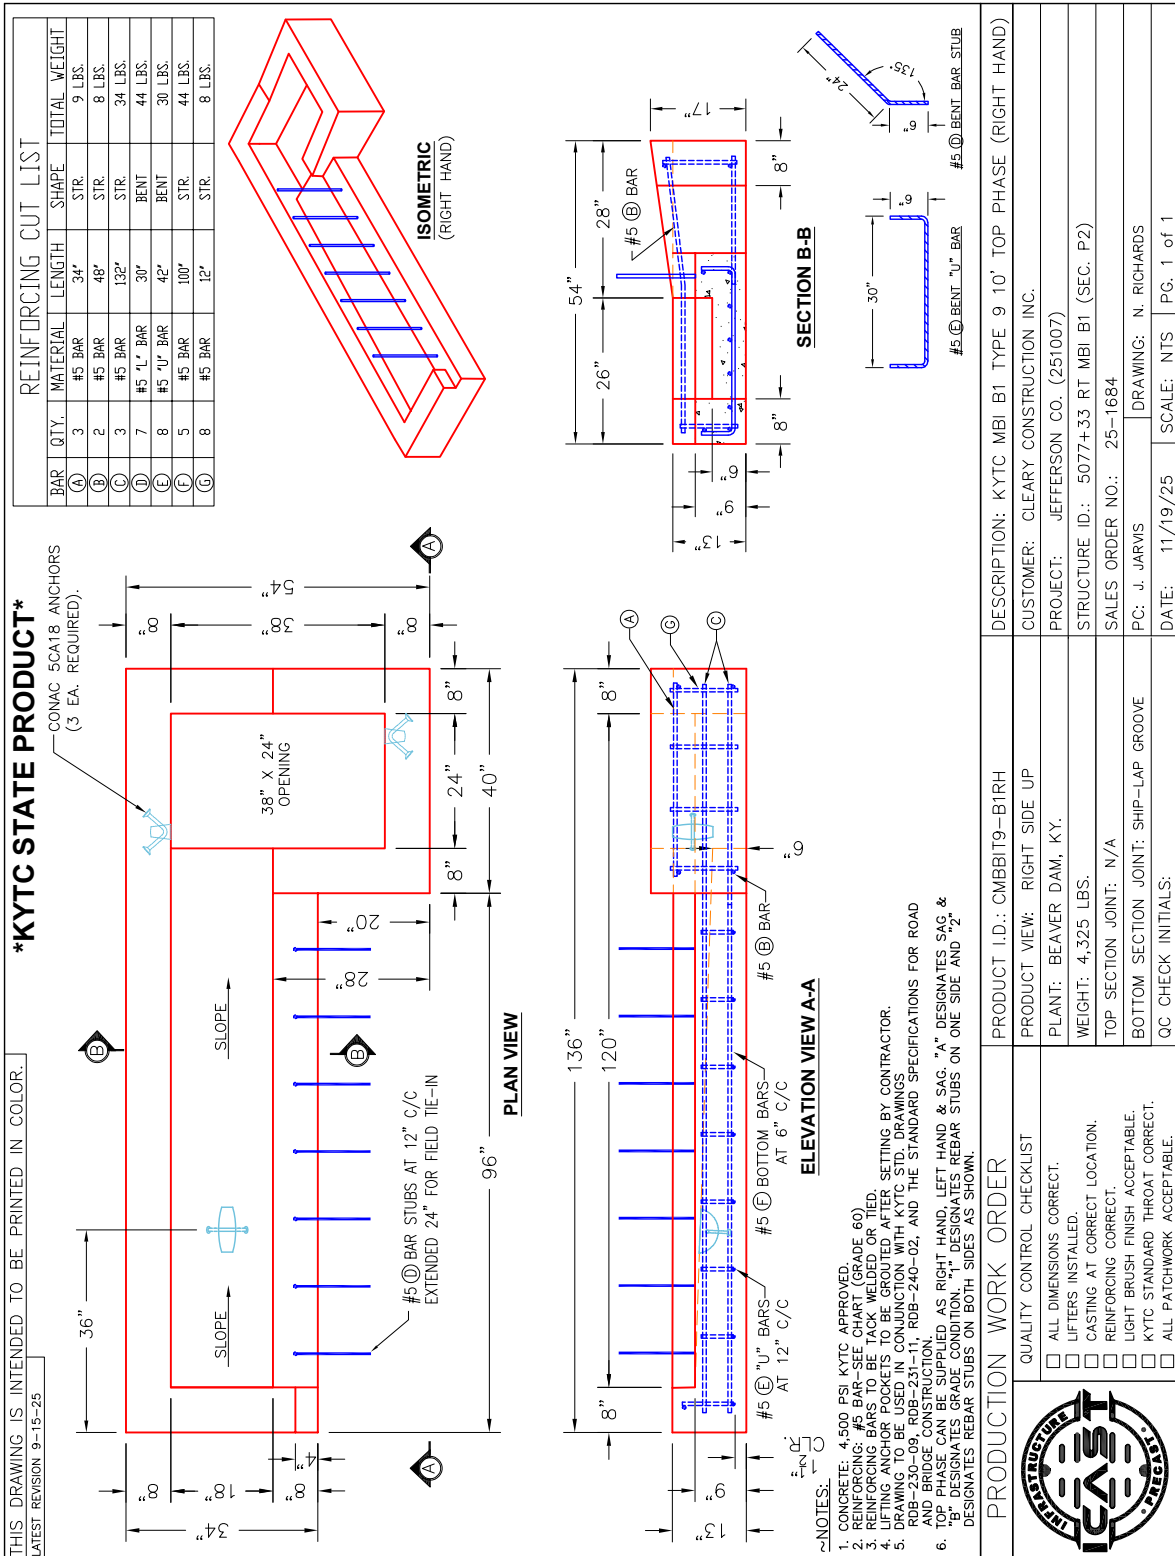

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 17"

Weight (Net): 4000 lb
Volume (Net): 0cu.yd
