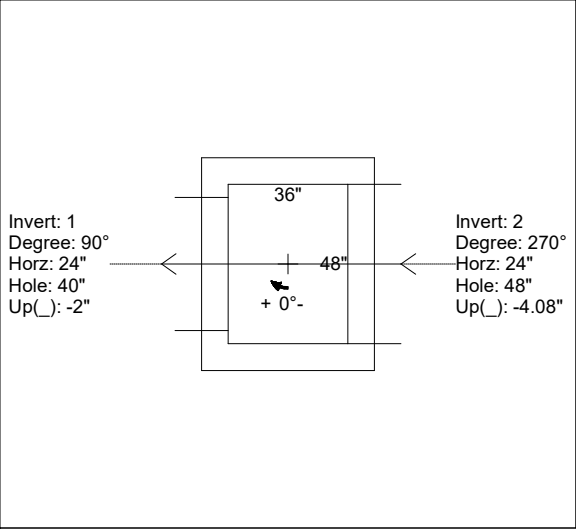
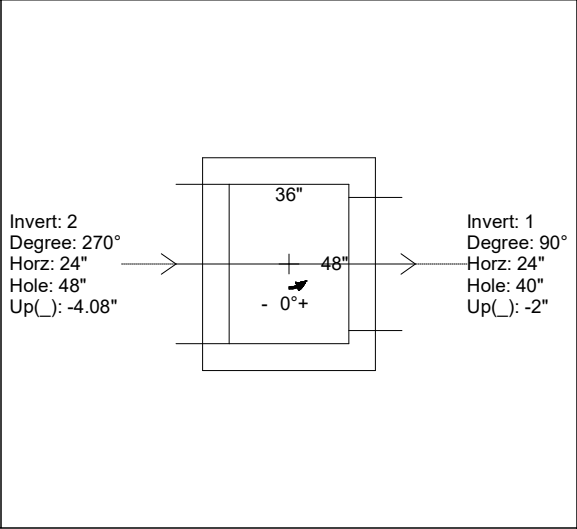
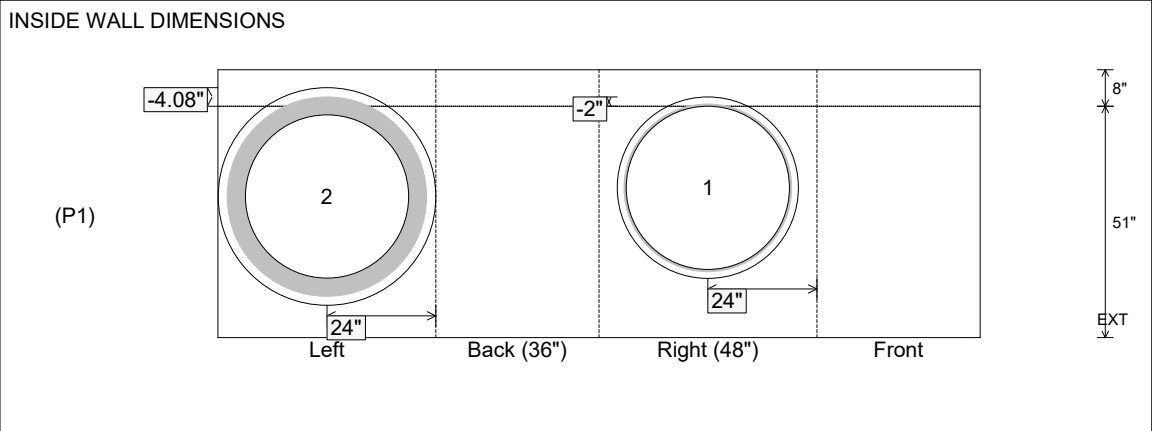


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:25 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 5081+13 LT CBBI-MOD B1											
P1		BX3648-08BAVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17" P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 51" 1) 36" x 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 40 1) Hole - 48					4000 lb 1654 lb 7327 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Structure Total:					12981 lb						
Rim: 580.21' Rim to Invert: 6.7' Slack: 4.4" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	573.51'	90°	32"	36" CMP	37"	Hole 40	40"	40"	-2"	0"	
Invert 2	573.67'	270°	32"	36" RCP B WALL	44"	Hole 48	48"	48"	-4.08"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
 Invert: 1 Degree: 90° Horz: 24" Hole: 40" Up(): -2" Invert: 2 Degree: 270° Horz: 24" Hole: 48" Up(): -4.08"  Invert: 2 Degree: 270° Horz: 24" Hole: 48" Up(): -4.08" Invert: 1 Degree: 90° Horz: 24" Hole: 40" Up(): -2"											
INSIDE WALL DIMENSIONS											
 (P1) Left Back (36") Right (48") Front EXT											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 51" Height (Ext): 59"		Weight (Net): 7327 lb Volume (Net): 1.87cu.yd		
