

Contractor: Cleary Construction, Inc.

PC: T. Ryan

TECH: J. Coppage

Plant: Beaver Dam, KY



Structure ID: 5083+65 LT CBBI-MOD B1

Spec: KYTC
Type: MBI TYPE 9
Size: 24" x 36"

Rim: 581.17'
Invert: 574.17'
Rim to Invert: 7'

Sump: 0"
Floor (Top): 574.17'
Floor Height: 8"


Floor (Bot): 573.503'
Overall Height: 7.333'
Slack: 4"

Structure Notes: .
 -KYTC STATE PROJECT 251007
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
 -CASTING FRAMES & GRATES BY OTHERS.
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
 -KYTC CERTIFICATIONS REQUIRED.


STRUCTURE SUMMARY:

P4) 24" x 120" - CASTING (cast in) - 3"	0 lb
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"	4000 lb
P2) 24" x 36" - BOX RISER 8inW, Variable Ht - 33"	3367 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"	4202 lb
2) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 22	0 lb


Structure Total:	11569 lb

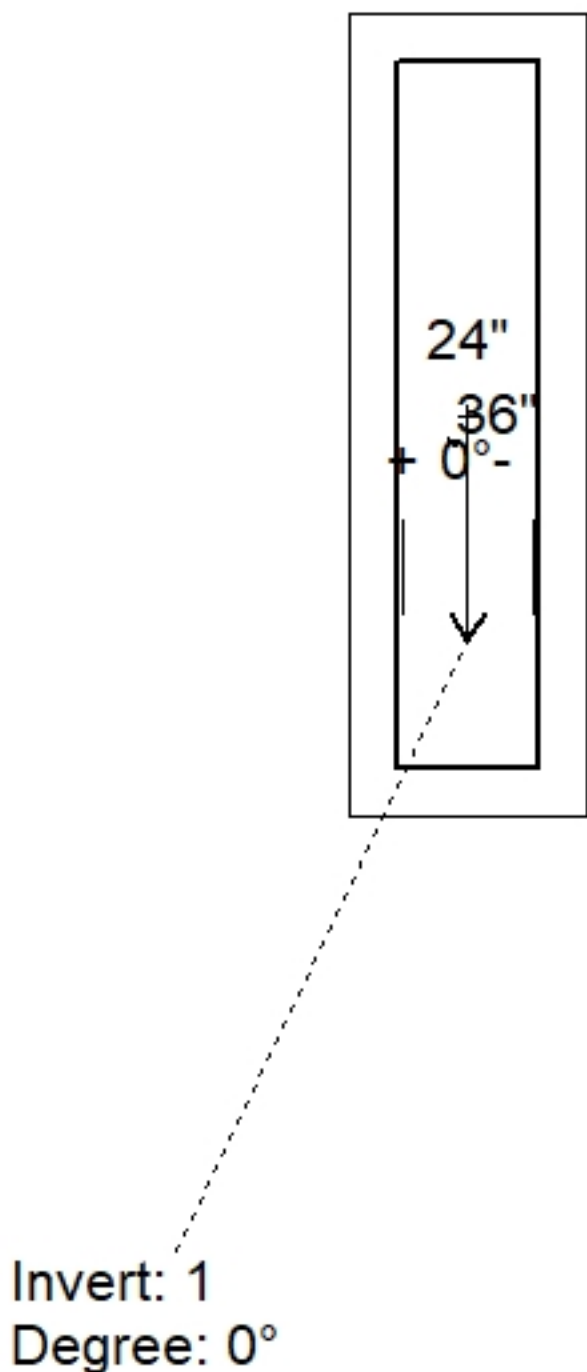

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	581.17'							
Reducer								
Invert 1	574.17'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

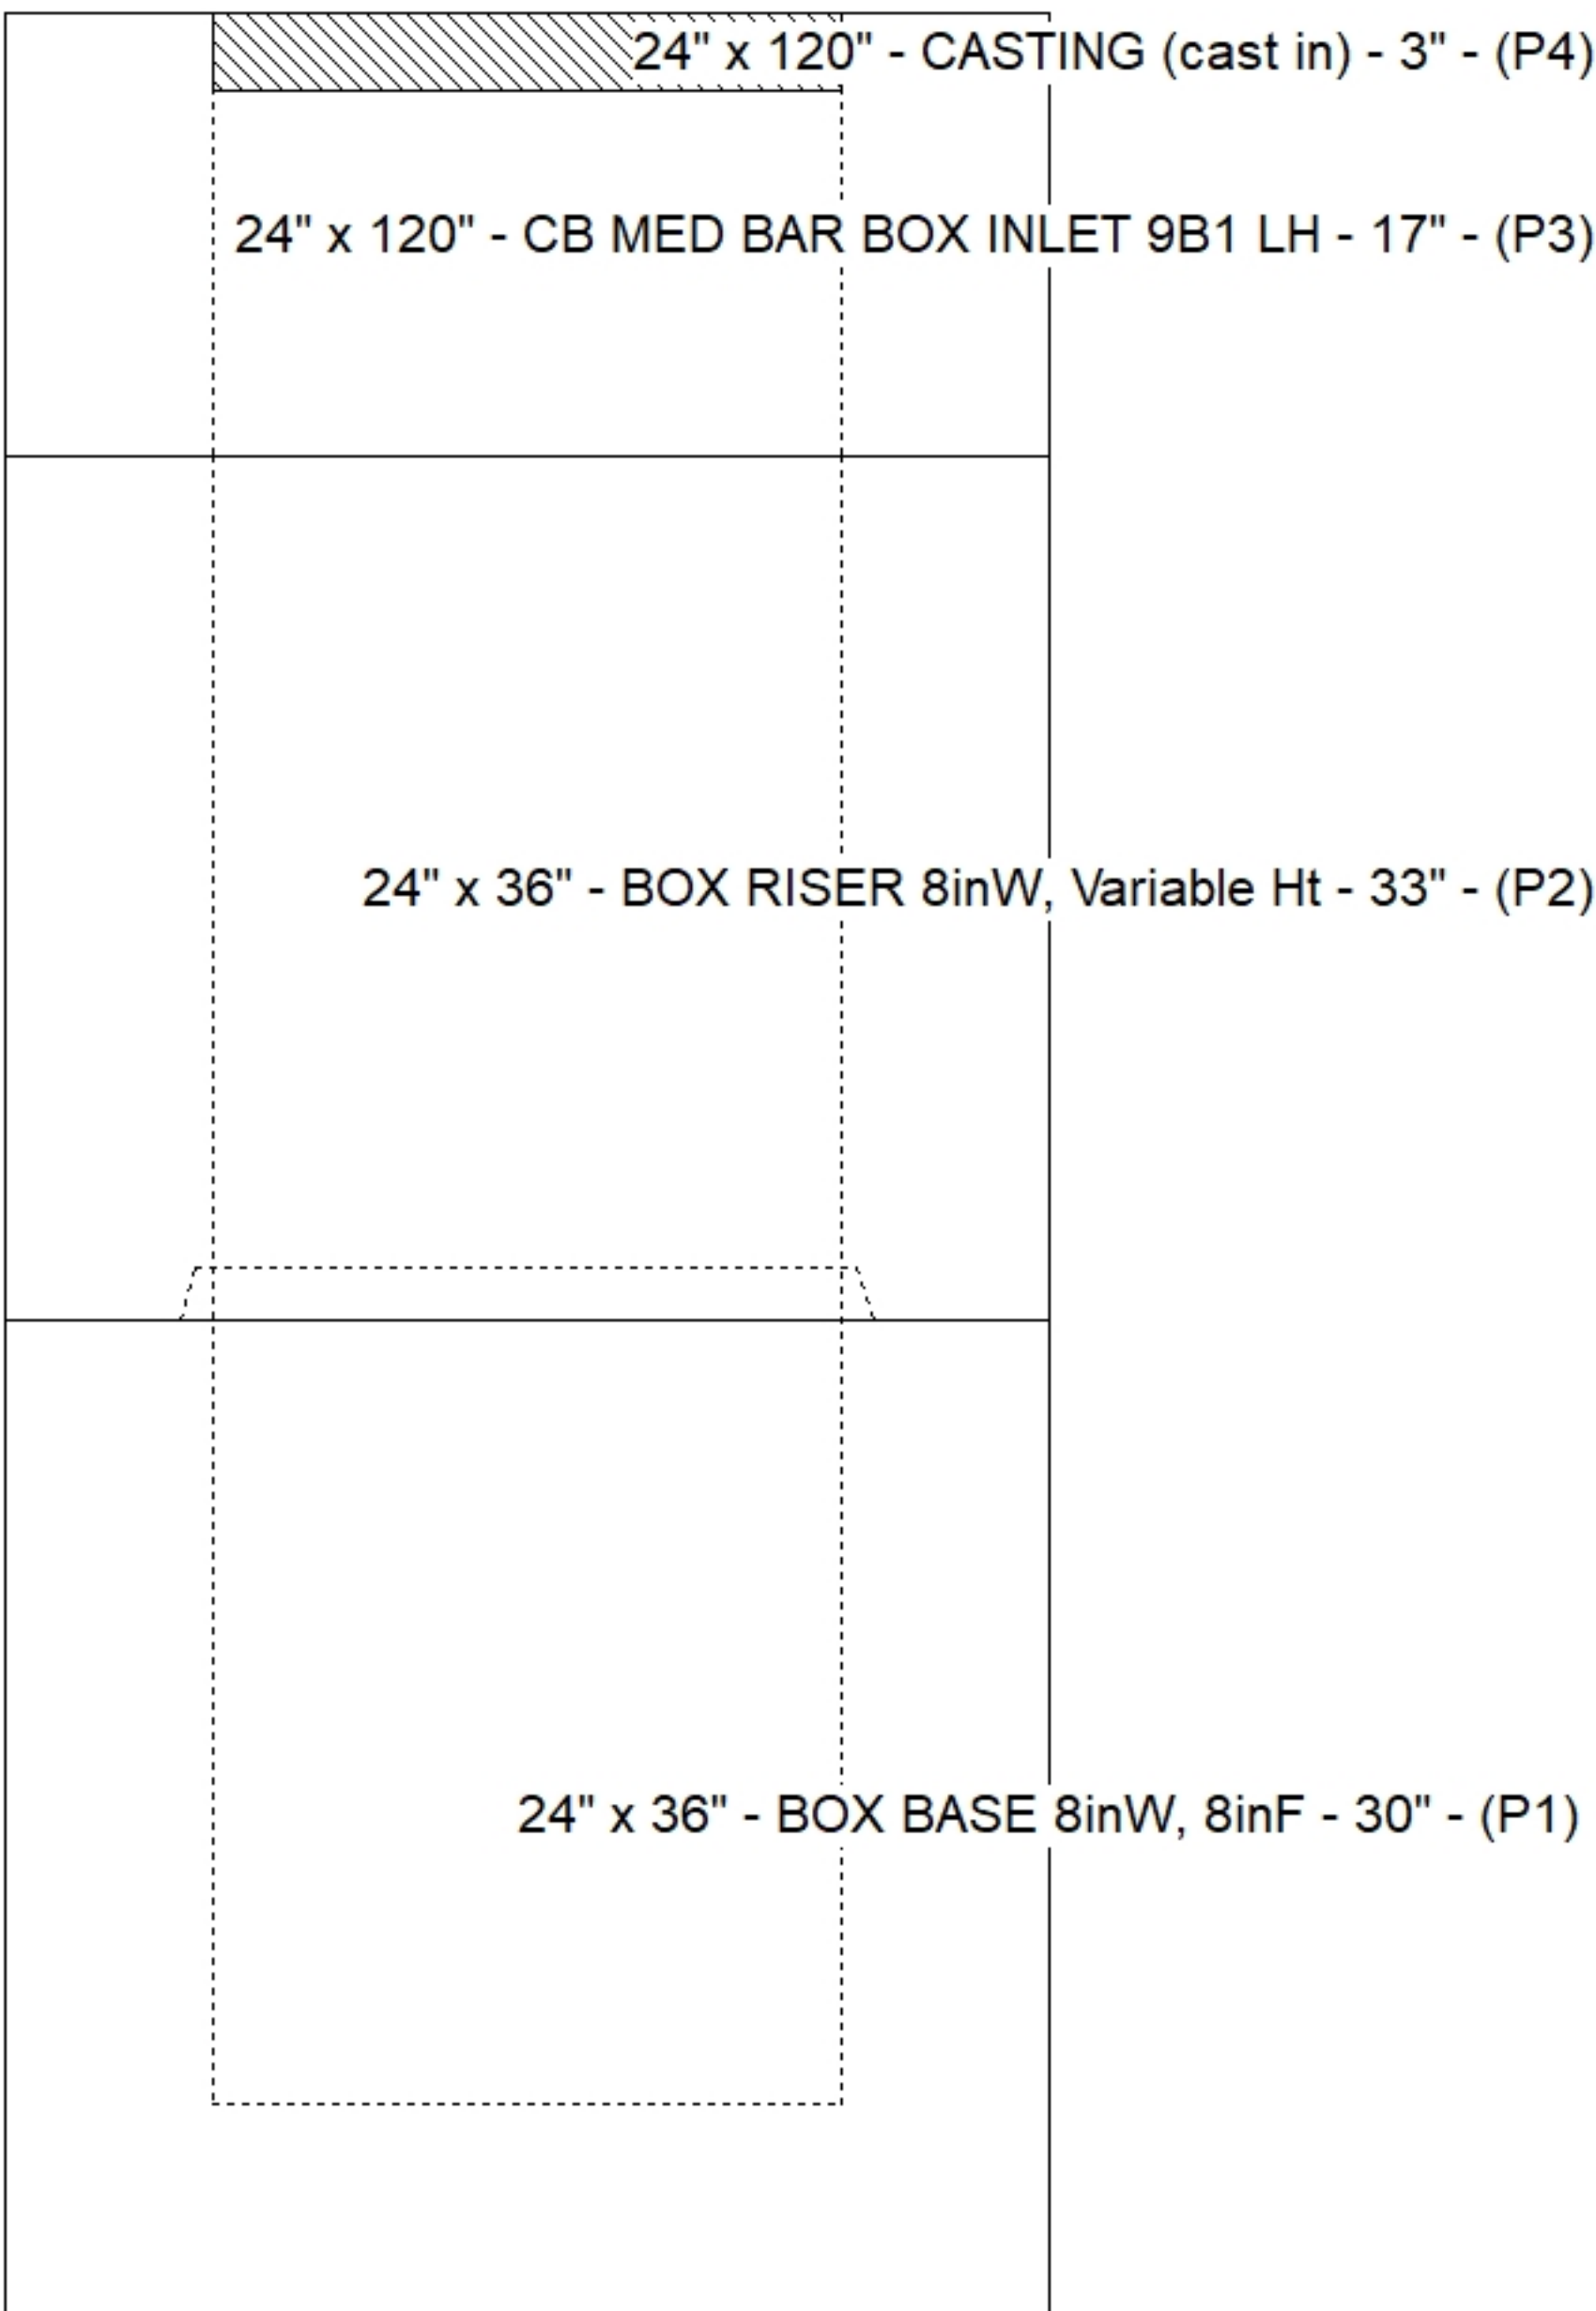

Default - Interior Dimensions

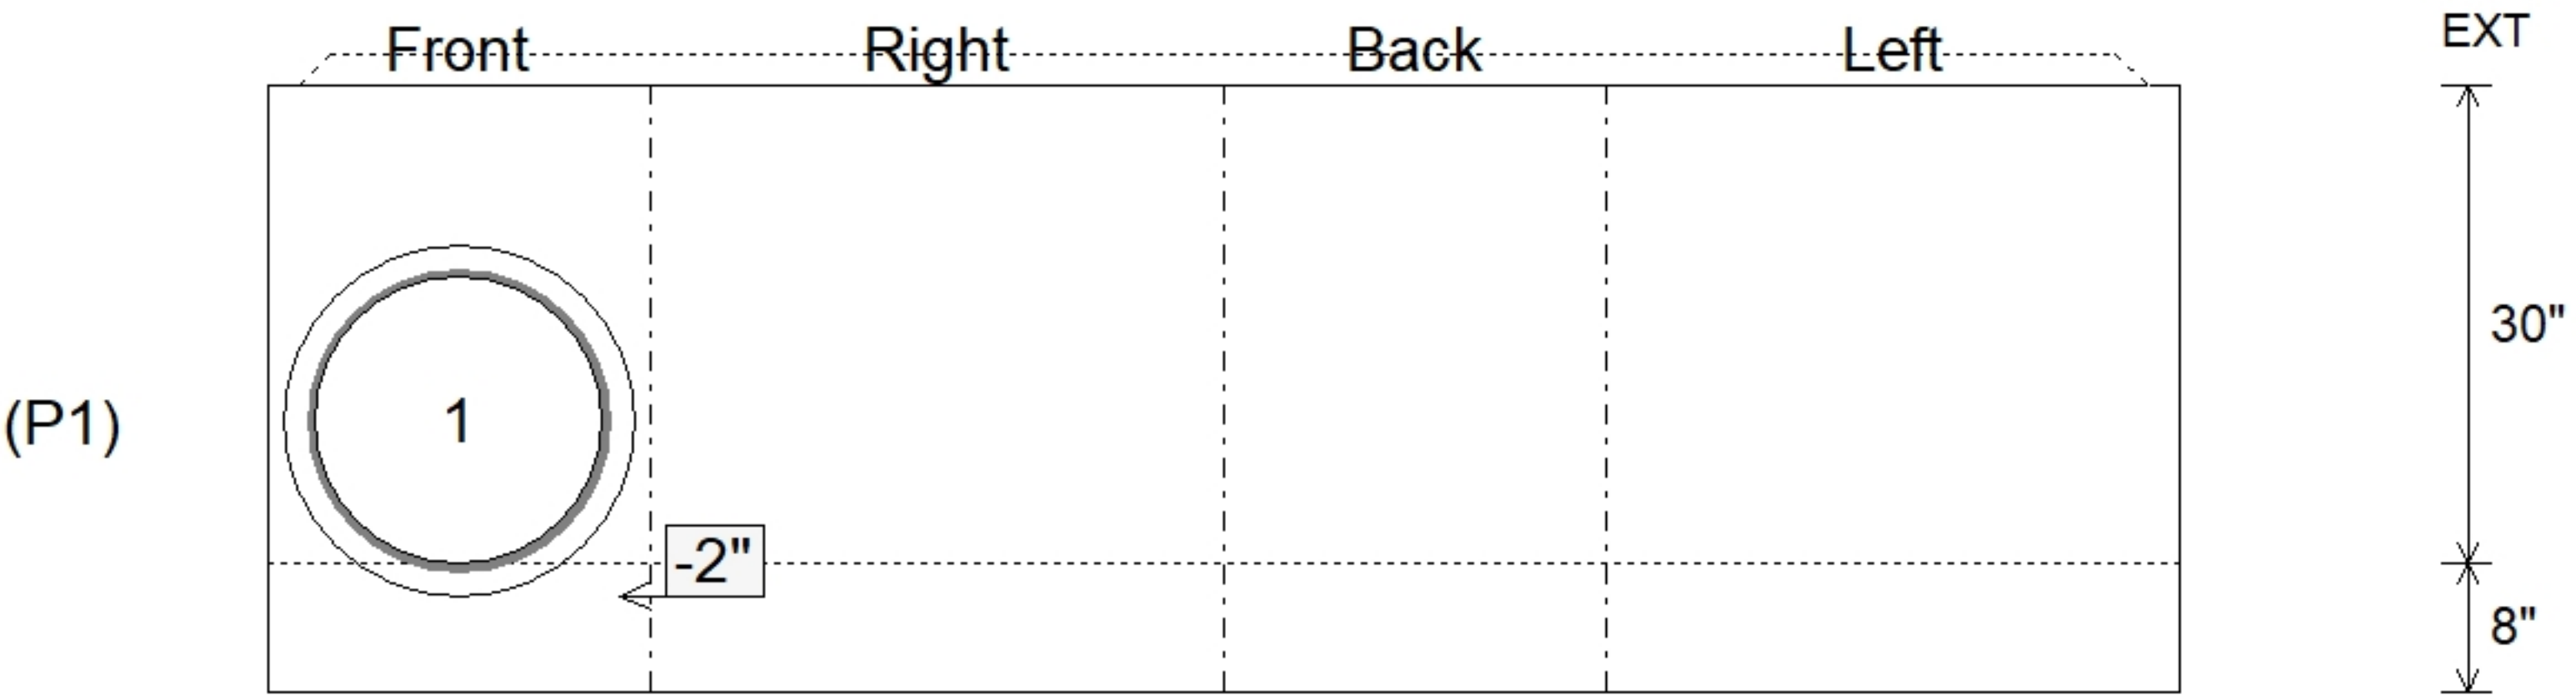

Submittal Drawing
8/10/2026 11:02:44 AM

SUBMITTAL
APPROVED BY:
