

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)

Job Location: I-264 Louisville, Ky.

Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY

8/4/2026 11:26:30 AM

Tech: J. Coppage

PC: T. Ryan



Structure ID: 5084+83 RT CBBI-MOD B1

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht

P3) 24" x 120" - CASTING (cast in) - 3"

P2) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17"

P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"

1) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 18

0 lb

4000 lb

3878 lb

0 lb

0 lb

0 lb

Structure Total: 7878 lb

Structure Notes:

-KYTC STATE PROJECT 251007

-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)

-CASTING FRAMES & GRATES BY OTHERS.

-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).

-KYTC CERTIFICATIONS REQUIRED.

Rim: 581.84'

Rim to Invert: 3.9'


Slack: 3.8"

Sump: 0"


Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	577.94'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)




UPSIDE-DOWN VIEW (int. dimensions)



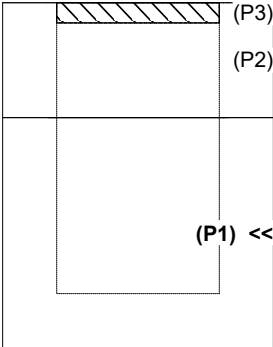

INSIDE WALL DIMENSIONS

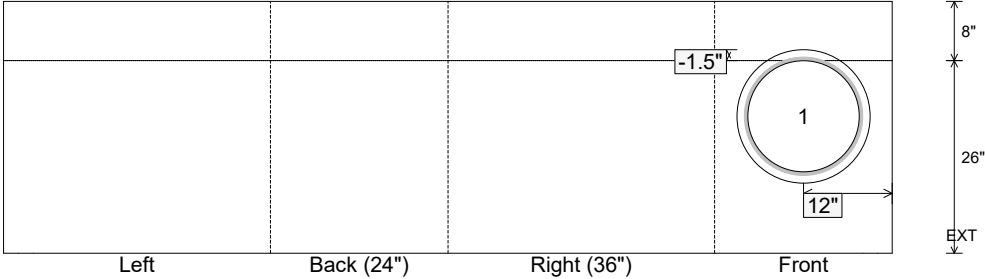

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 26"

Height (Ext): 34"

Weight (Net): 3878 lb

Volume (Net): 0.99cu.yd
