

Contractor: Cleary Construction, Inc.

PC: T. Ryan

TECH: J. Coppage

Plant: Beaver Dam, KY




Structure ID: 5084+83 RT CBBI-MOD B1			
Spec: KYTC	Rim: 581.84'	Sump: 0"	Floor (Bot): 577.273'
Type: MBI TYPE 9	Invert: 577.94'	Floor (Top): 577.94'	Overall Height: 4.25'
Size: 24" x 36"	Rim to Invert: 3.9'	Floor Height: 8"	Slack: 3.8"

Structure Notes:


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

STRUCTURE SUMMARY:	
P3) 24" x 120" - CASTING (cast in) - 3"	0 lb
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17"	4000 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"	3878 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb


Structure Total:	7878 lb

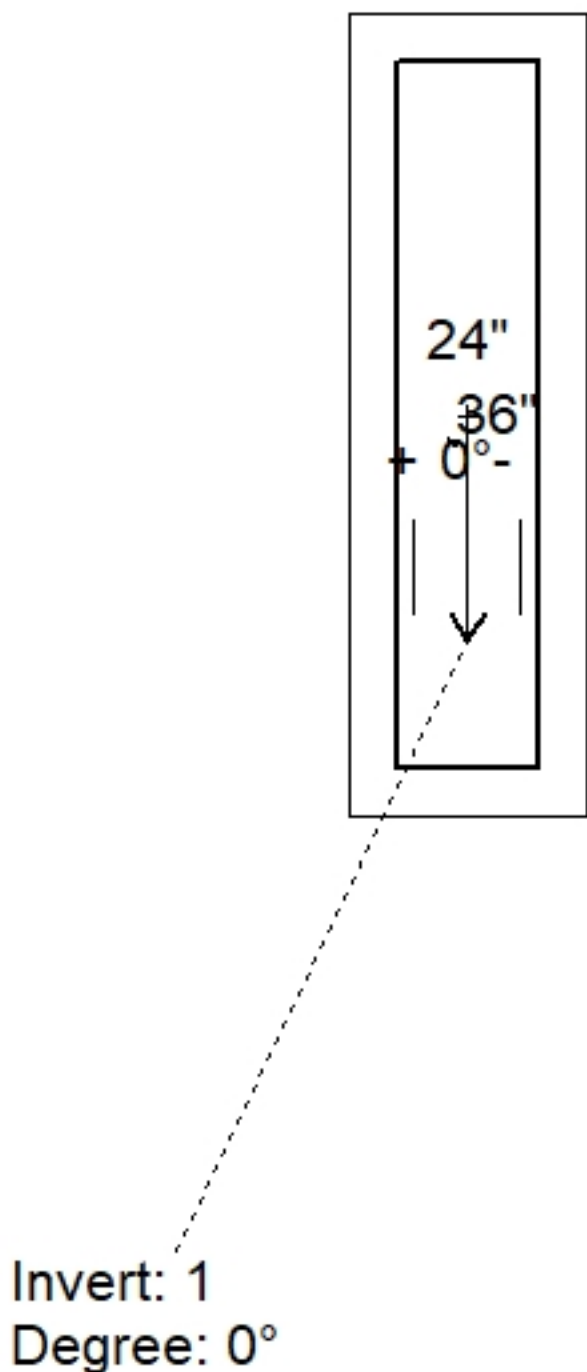

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	581.84'							
Reducer								
Invert 1	577.94'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

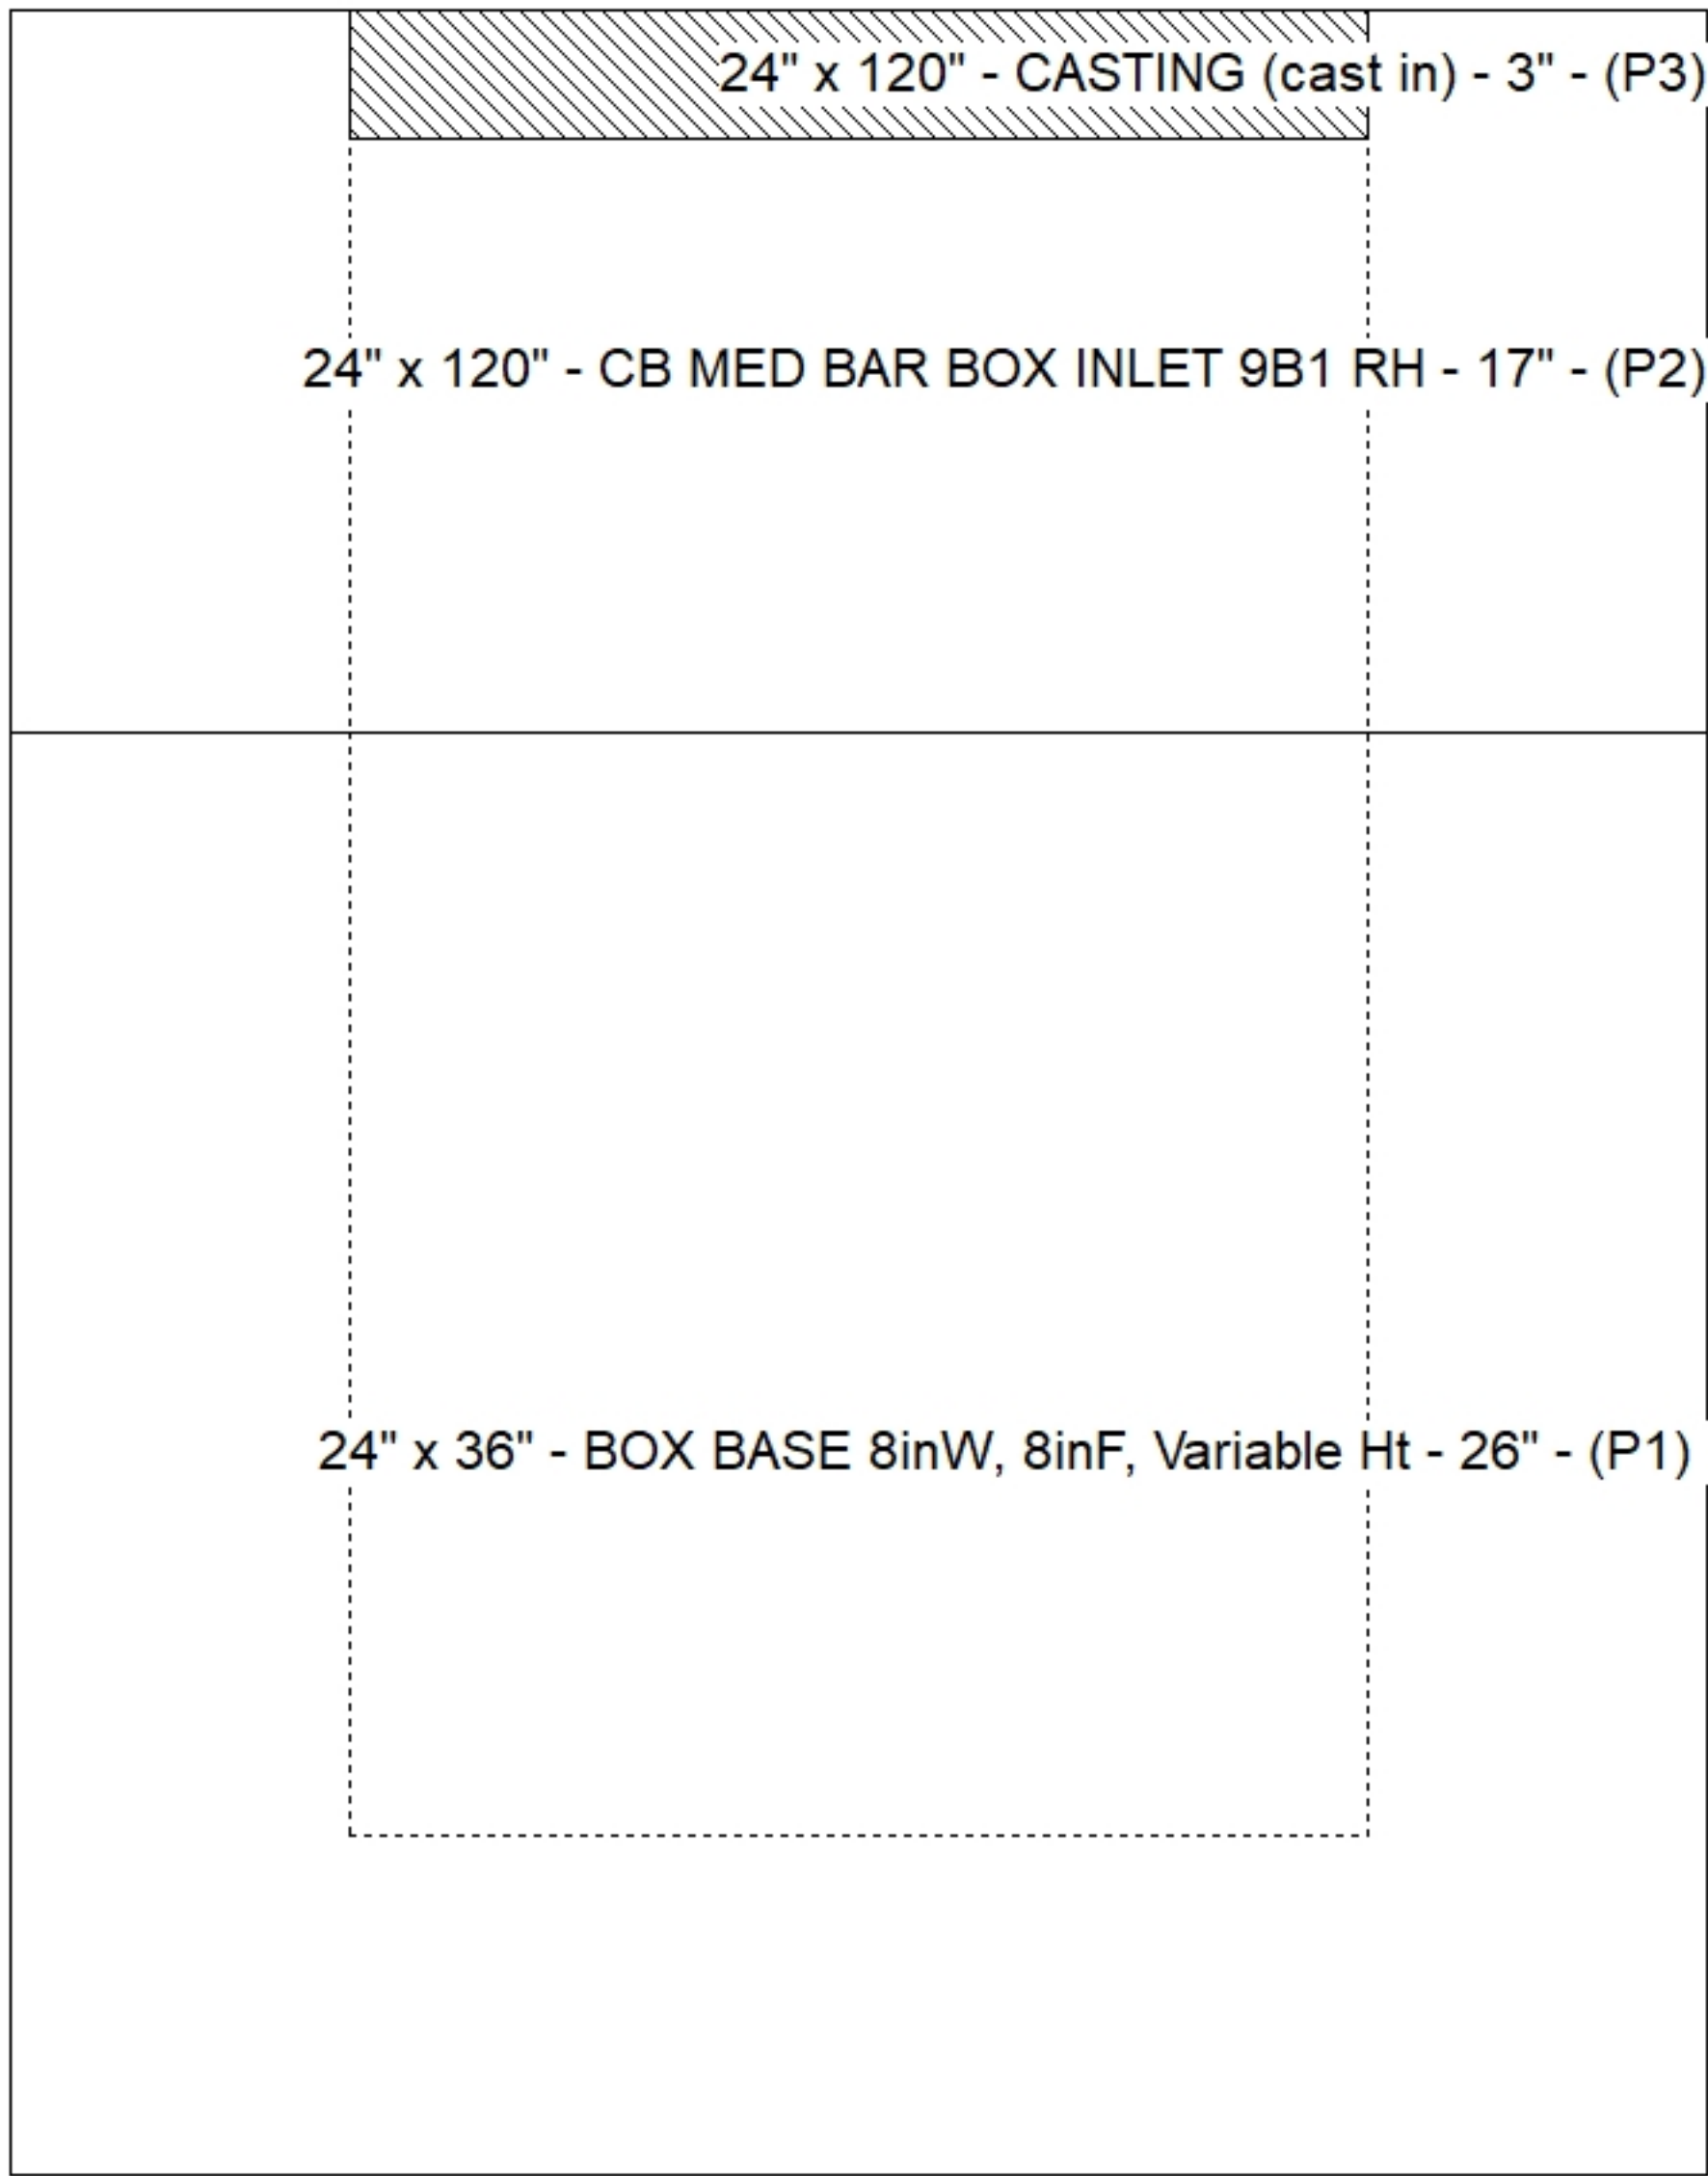

Default - Interior Dimensions

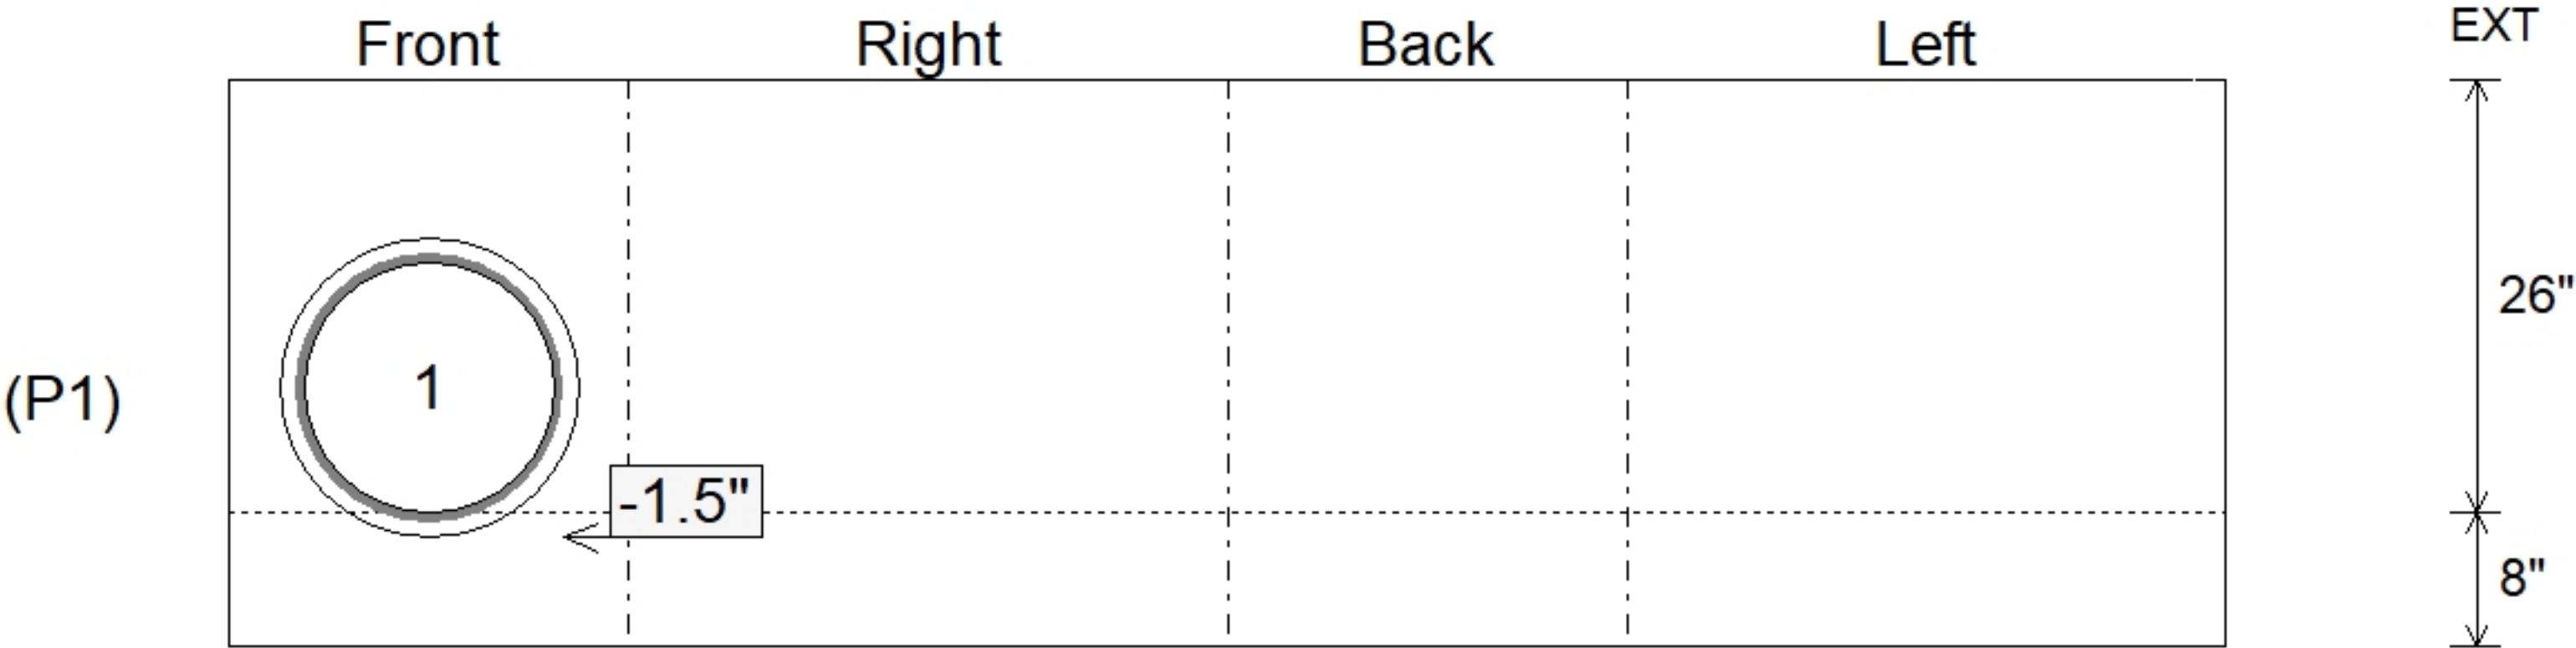

Submittal Drawing
8/10/2026 11:02:44 AM

SUBMITTAL
APPROVED BY:
