

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.	Plant: Beaver Dam, KY 8/4/2026 11:26:30 AM	Tech: J. Coppage PC: T. Ryan	
Structure ID: 5086+13 LT CBBI-MOD B1			
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht			

P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 39"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22

0 lb
4000 lb
4865 lb
0 lb
0 lb


Structure Total: 8865 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CASTING FRAMES & GRATES BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.


Rim: 582.09'		Rim to Invert: 5'	Slack: 4"	Sump: 0"	Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	577.09'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 2	577.09'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

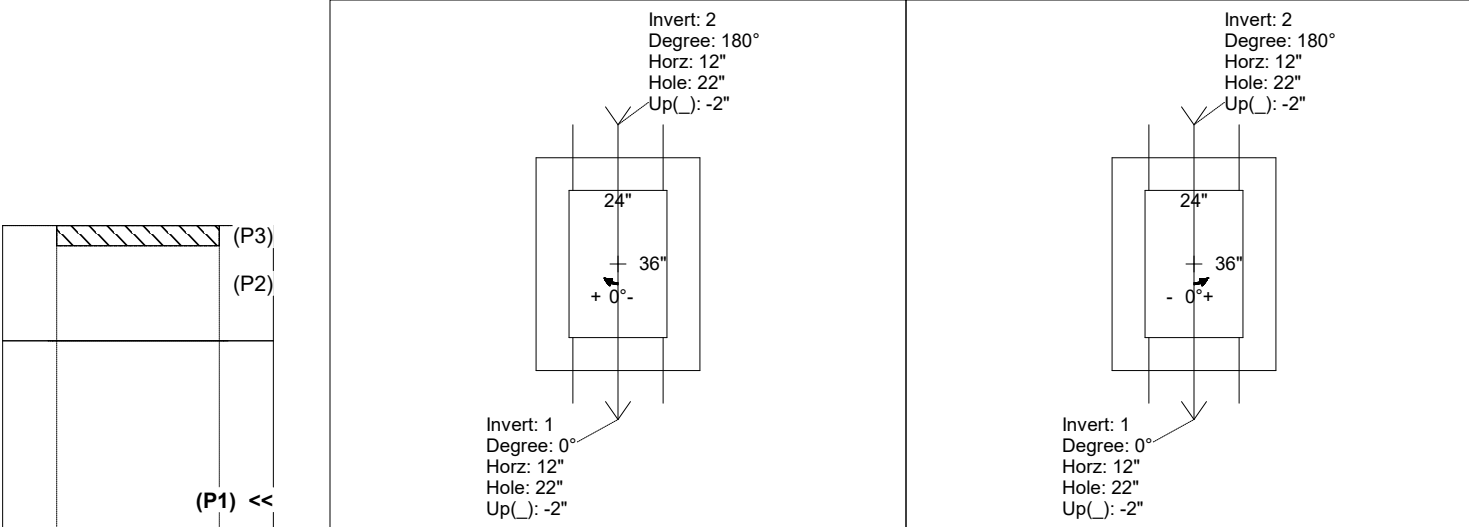

INSIDE WALL DIMENSIONS

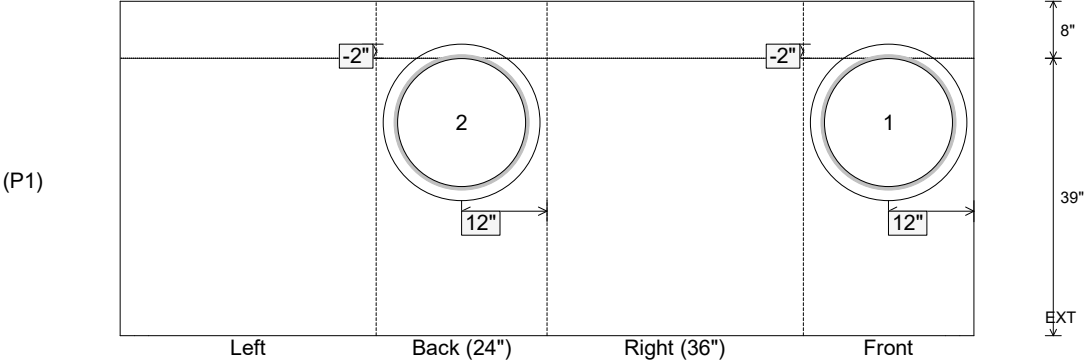

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 39" Height (Ext): 47"	Weight (Net): 4865 lb Volume (Net): 1.24cu.yd
----------------------------------	-------------------------------	--	--	--
