

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/10/2026 10:52:44 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 5090+98 LT CBBI-MOD B1

P3 BX048048-08TS024036

CB FT REDUCER 24"X36" HOLE-FT


- P5) 24" x 120" - CASTING (cast in) - 3"
P4) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P3) 48" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"
P2) 48" x 48" - BOX RISER 8inW, Variable Ht - 18"
P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 46"
2) 48" x 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 40
1) Hole - 28

0 lb
4000 lb
2170 lb
2707 lb
7512 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 16388 lb

Structure Notes:

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

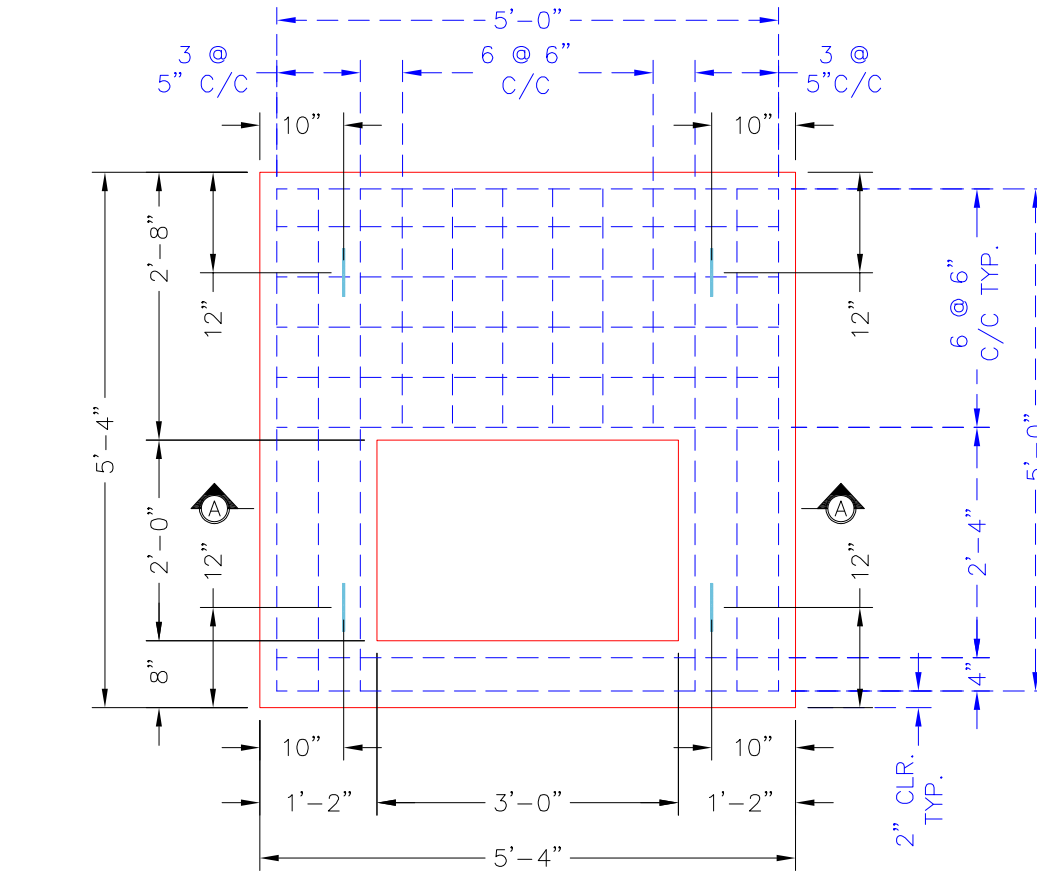

PLAN VIEW

4 EA. CONAC .8 TON 8 1/8" (6MM) WIRE ROPE ANCHORS REQUIRED-MINIMUM.

ROUND TOP EDGES

#5 BAR @ 5" C/C TYP. (TOP & BOTTOM)

SECTION A-A

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURED TO KYTC & ASTM C-913 SPECIFICATIONS.
- REINFORCING: #5 BAR AS SHOWN-GRADE 60. (TOP & BOTTOM LAYER)
- 4 EA. CONAC WIRE LOOP LIFTS REQUIRED (MIN.)

24" X 36" OPENING
OFFSET IN SLAB

2" CLR.

2" CLR.
8"

#5 BAR CUT LIST
28 EA. @ 60" LG.
12 EA. @ 28" LG.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 2170 lb
Volume (Net): 0.55cu.yd
