


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
 Job Location: I-264 Louisville, Ky.
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
 8/6/2026 2:12:00 PM

Tech: J. Coppage
 PC: T. Ryan



Structure ID: 5090+98 RT CBBI-MOD B1

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

- P4) 24" x 120" - CASTING (cast in) - 3"
 P3) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17"
 P2) 36" x 36" - CB FT REDUCER 24"X36" HOLE-FT - 8"
 P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 36"
 1) 36" x 36" - Conseal CS-102 1.00"
 1) 24" x 36" - Conseal CS-102 1.00"
 1) Hole - 34
 1) Hole - 28

Structure Notes:
 -KYTC STATE PROJECT 251007
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
 -CASTING FRAMES & GRATES BY OTHERS.
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
 -KYTC CERTIFICATIONS REQUIRED.



Structure Total: 10281 lb

Rim: 584.26' Rim to Invert: 5' Slack: 0" Sump: 1" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	579.26'	0°	26"	24" RCP B WALL	30"	Hole 34	34"	34"	-4"	0"
Invert 2	579.26'	180°	26"	24" CMP	25"	Hole 28	28"	28"	-1"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

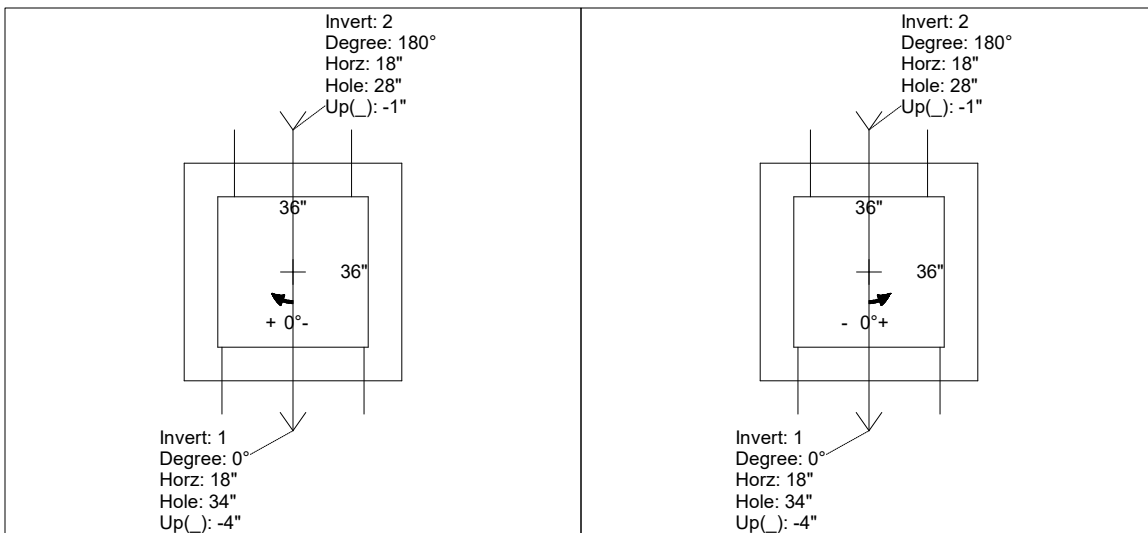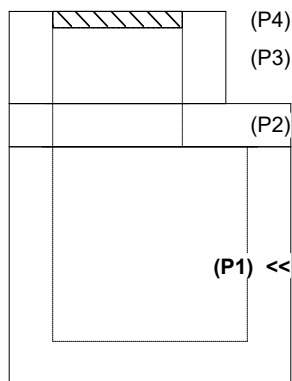

INSIDE WALL DIMENSIONS

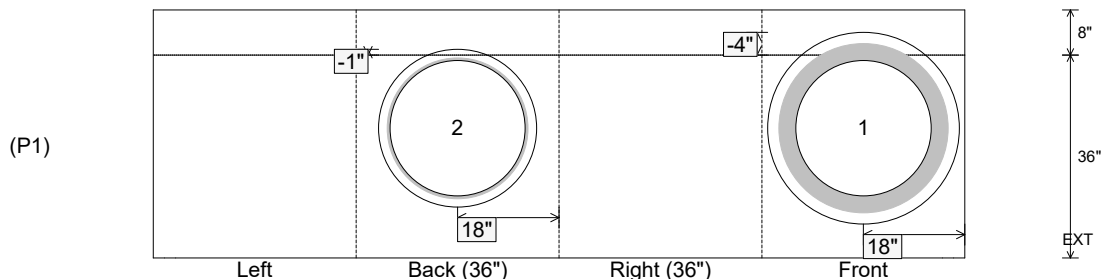

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 36"
 Height (Ext): 44"

Weight (Net): 5046 lb
 Volume (Net): 1.29cu.yd
