



Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:39 AM		Tech: J. Coppage PC: T. Ryan					
Structure ID: 5094+97 RT CBBI-MOD B1												
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht								
P3) 24" x 120" - CASTING (cast in) - 3" P2) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 4000 lb 3878 lb 0 lb 0 lb ----- Structure Total: 7878 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.					
Rim: 586.01'					Rim to Invert: 3.9'		Slack: 3.8"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1	582.11'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"		
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

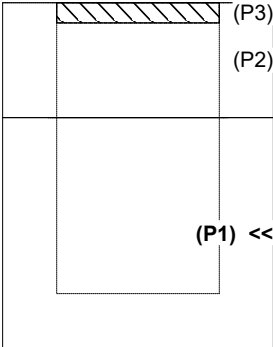


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimenions)



INSIDE WALL DIMENSIONS

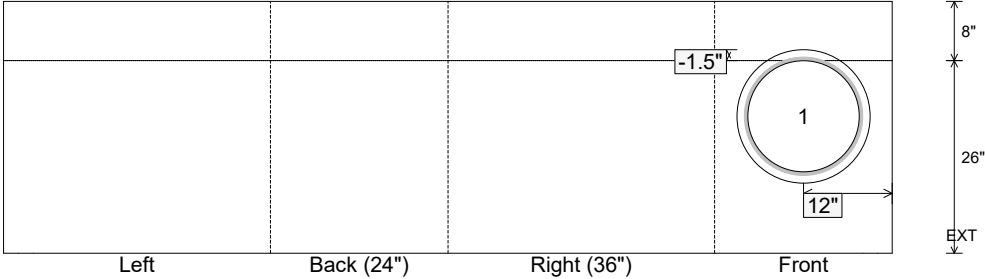

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 26"
Height (Ext): 34"

Weight (Net): 3878 lb
Volume (Net): 0.99cu.yd
