

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:28:46 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 5095+00 LT JB-A

P2 BX3648_08LD08

CB FLAT TOP 8"W SOLID


P2) 36" x 48" - CB FLAT TOP 8"W SOLID - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF - 42"
1) 36" x 48" - Conseal CS-102 1.00"
2) Hole - 40
1) Hole - 22

Structure Total:

2234 lb
5931 lb
0 lb
0 lb
0 lb
8165 lb

Structure Notes:

-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

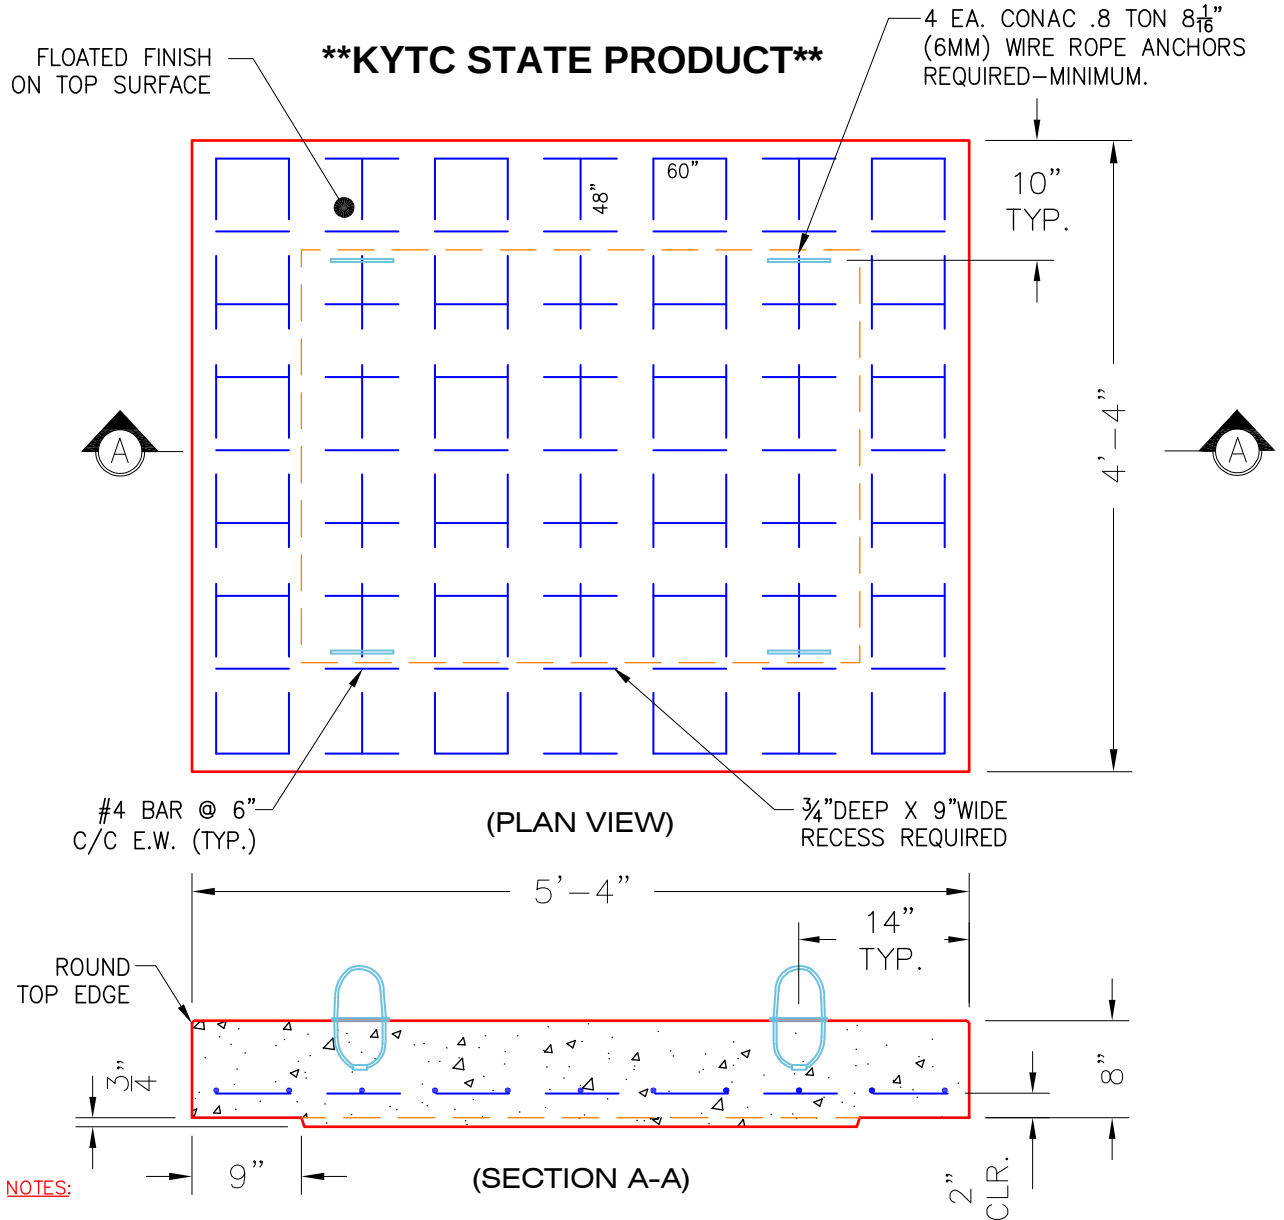

NOTES:

-CONCRETE: 4500 PSI @ 28 DAYS.
-MANUFACTURE TO KYTC SPECIFICATIONS.
-REINFORCING: #4 BAR @ 6" C/C E.W.—GRADE 60.
(BOTTOM LAYER ONLY)
-4 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

#4 BAR CUT LIST

9 EA. @ 60"
11 EA. @ 48"

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 2234 lb
Volume (Net): 0.57cu.yd
