


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
 Job Location: I-264 Louisville, Ky.
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
 8/6/2026 2:25:42 PM

Tech: J. Coppage
 PC: T. Ryan



Structure ID: 5096+43 LT CBBI-MOD B1

P1 BX3648-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

- P4) 24" x 120" - CASTING (cast in) - 3"
 P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
 P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"
 P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 41"
 1) 36" x 48" - Conseal CS-102 1.00"
 1) 24" x 36" - Conseal CS-102 1.00"
 1) DOGHOUSE INVRTD - 40"x43"
 1) Hole - 34"

Structure Notes:
 -KYTC STATE PROJECT 251007
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
 -CASTING FRAMES & GRATES BY OTHERS.
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
 -KYTC CERTIFICATIONS REQUIRED.


Structure Total: 11744 lb

Rim: 586.09' Rim to Invert: 5.5' Slack: 0" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	580.59'	90°	32"	36" CMP	37"	DOGHOUSE INVRTD 40"x43"	40" x 43"	40"	-2"	0"
Invert 2	580.59'	270°	32"	30" CMP	31"	Hole 34	34"	34"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

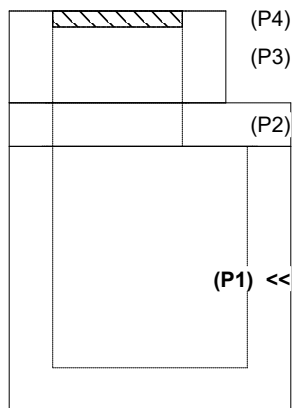


Invert: 1
 Degree: 90°
 Horz: 24"
 Hole: 40" x 43"
 Up(): -2"



Invert: 2
 Degree: 270°
 Horz: 24"
 Hole: 34"
 Up(): -2"


Invert: 2
 Degree: 270°
 Horz: 24"
 Hole: 34"
 Up(): -2"



Invert: 1
 Degree: 90°
 Horz: 24"
 Hole: 40" x 43"
 Up(): -2"

INSIDE WALL DIMENSIONS

(P1)

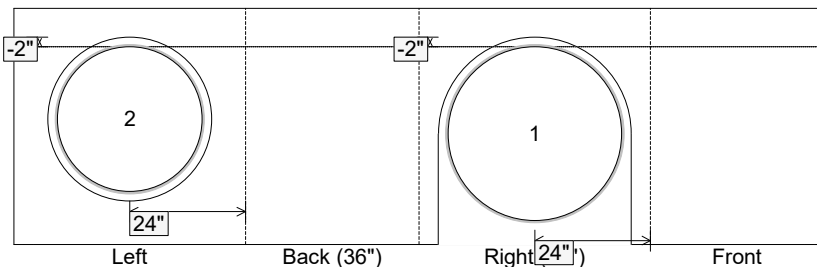

8"
 41"
 EXT

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 41"
 Height (Ext): 49"

Weight (Net): 6090 lb
 Volume (Net): 1.56cu.yd
