

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)  
Job Location: I-264 Louisville, Ky.  
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY  
8/6/2026 2:27:22 PM

Tech: J. Coppage  
PC: T. Ryan



## Structure ID: 5096+43 LT CBBI-MOD B1


**P2 BX036048-08TS024036**

**CB FT REDUCER 24"X36" HOLE-FT**


- P4) 24" x 120" - CASTING (cast in) - 3"  
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"  
P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"  
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 41"  
1) 36" x 48" - Conseal CS-102 1.00"  
1) 24" x 36" - Conseal CS-102 1.00"  
1) DOGHOUSE INVRTD - 40"x40"  
1) Hole - 34

0 lb  
4000 lb  
1654 lb  
6090 lb  
0 lb  
0 lb  
0 lb  
0 lb  
Structure Total: 11744 lb

**Structure Notes:**  
-KYTC STATE PROJECT 251007  
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)  
-CASTING FRAMES & GRATES BY OTHERS.  
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).  
-KYTC CERTIFICATIONS REQUIRED.

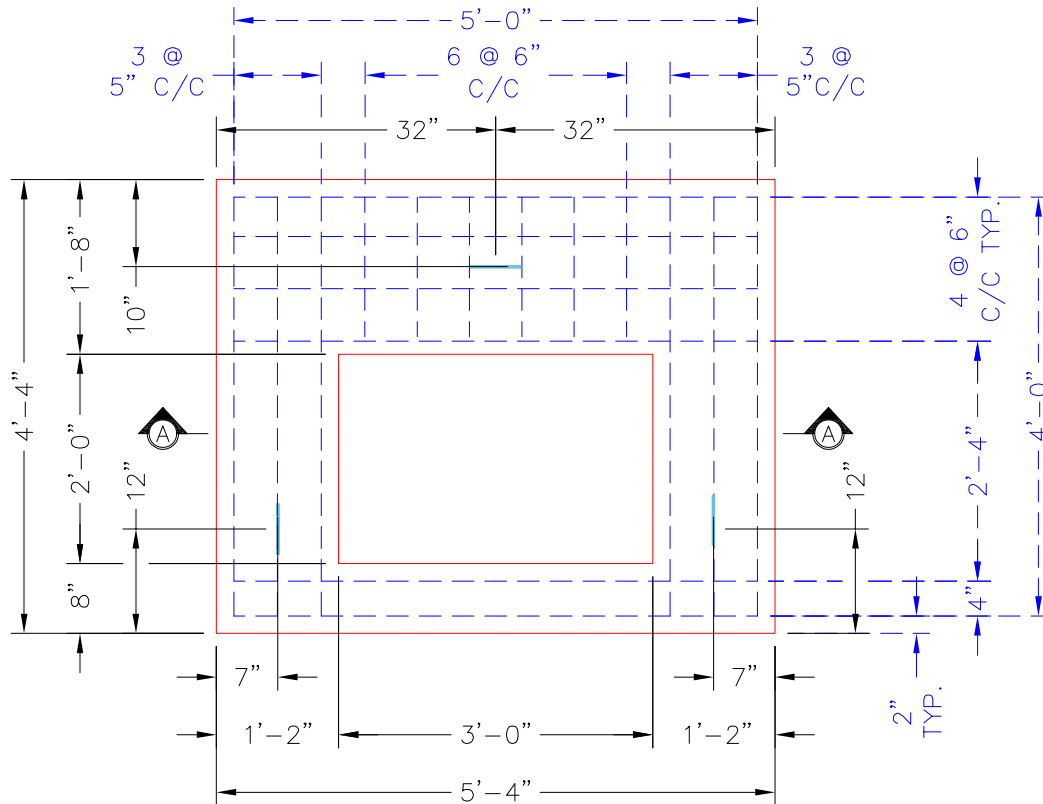

**PLAN VIEW**

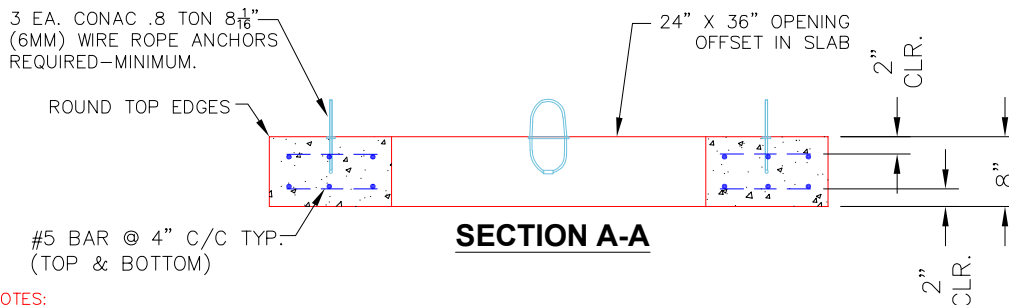

**SECTION A-A**

**NOTES:**

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURED TO KYTC & ASTM C-913 SPECIFICATIONS.
- REINFORCING: #5 BAR AS SHOWN-GRADE 60.  
(TOP & BOTTOM LAYER)
- 3 EA. CONAC WIRE LOOP LIFTS REQUIRED (MIN.)

**#5 BAR CUT LIST**

- 12 EA. @ 60" LG.
- 12 EA. @ 48" LG.
- 12 EA. @ 16" LG.

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1654 lb  
Volume (Net): 0.42cu.yd
