

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/6/2026 2:31:12 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 5097+50 LT CBBI-MOD B1


P3 CMBBIT9-B1LH

CB MED BAR BOX INLET 9B1 LH

- P4) 24" x 120" - CASTING (cast in) - 3"
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 41"
1) 36" x 48" - Conseal CS-102 1.00"
2) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 34
1) Hole - 22

- 0 lb Structure Notes:
4000 lb -KYTC STATE PROJECT 251007
1654 lb -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
6265 lb -CASTING FRAMES & GRATES BY OTHERS.
0 lb -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
0 lb -KYTC CERTIFICATIONS REQUIRED.
0 lb

Structure Total: 11919 lb

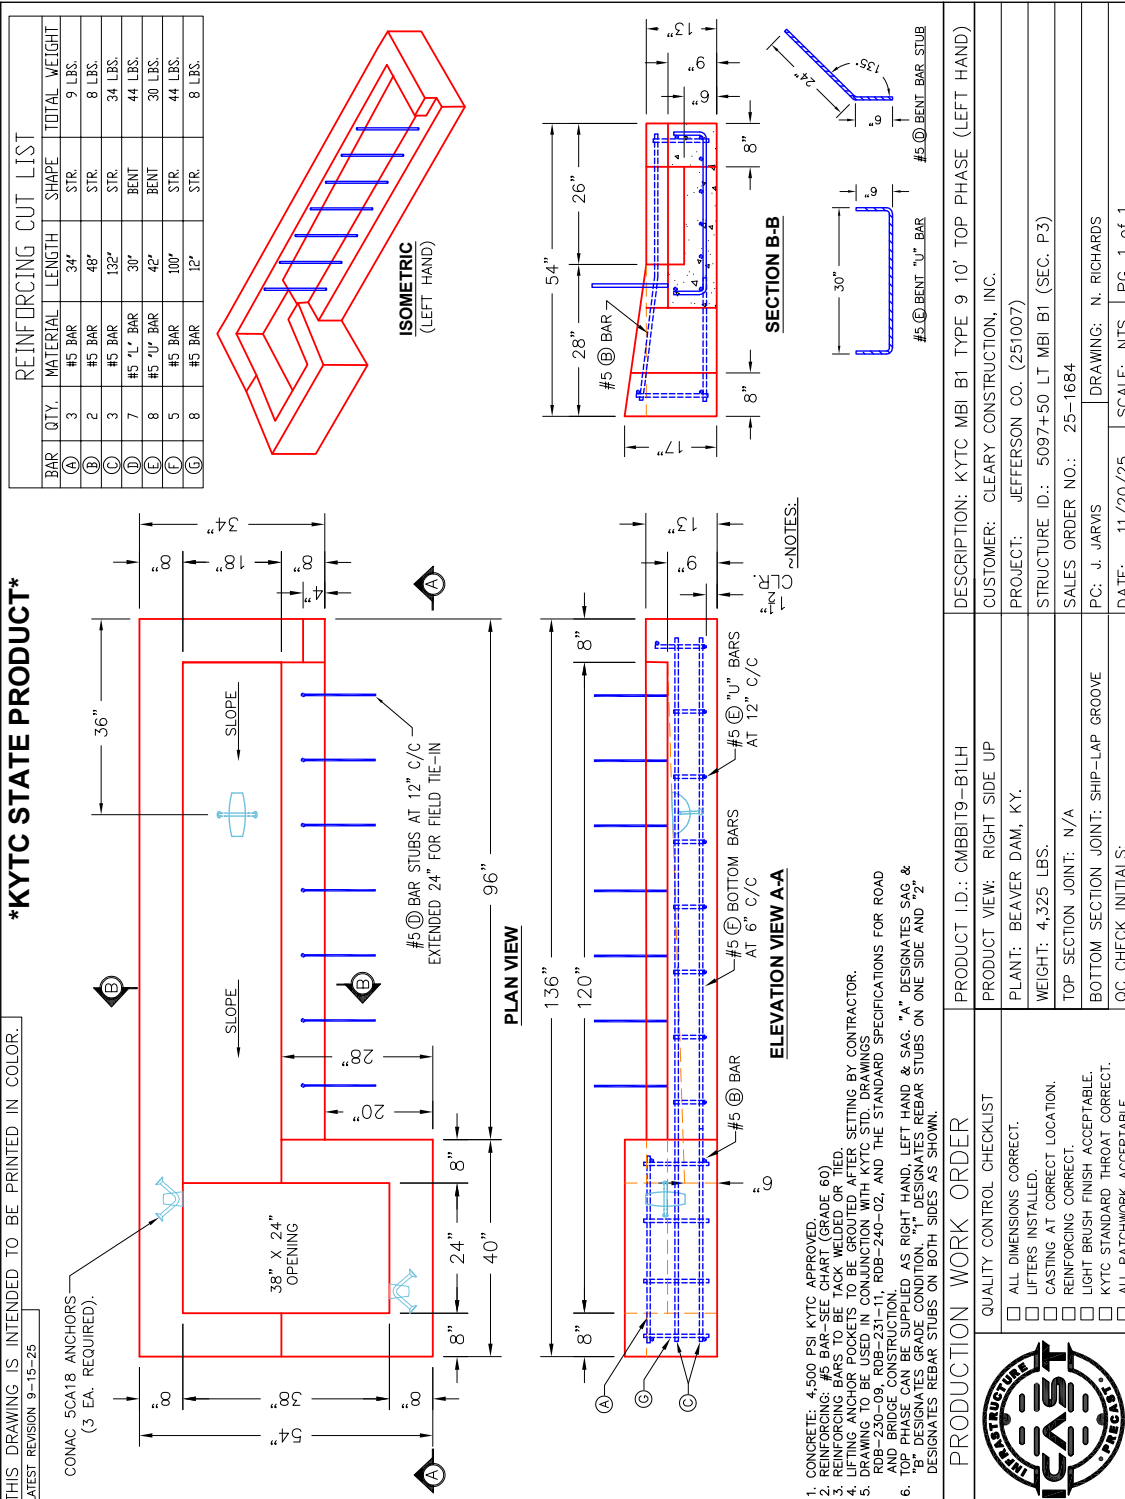

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 17"	Weight (Net): 4000 lb Volume (Net): 0cu.yd
----------------------------------	--------------------------------	--------------------	-------------------	---
