

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)  
Job Location: I-264 Louisville, Ky.  
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY  
8/4/2026 11:28:49 AM

Tech: J. Coppage  
PC: T. Ryan



## Structure ID: 5101+20 LT CBBI-MOD B1


### P2 CMBBIT9-B1LH

### CB MED BAR BOX INLET 9B1 LH

- P3) 24" x 120" - CASTING (cast in) - 3"  
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"  
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"  
1) 24" x 36" - Con seal CS-102 1.00"  
1) Hole - 18

0 lb  
4000 lb  
4287 lb  
0 lb  
0 lb  
Structure Total: 8287 lb

**Structure Notes:**  
-KYTC STATE PROJECT 251007  
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)  
-CASTING FRAMES & GRATES BY OTHERS.  
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).  
-KYTC CERTIFICATIONS REQUIRED.

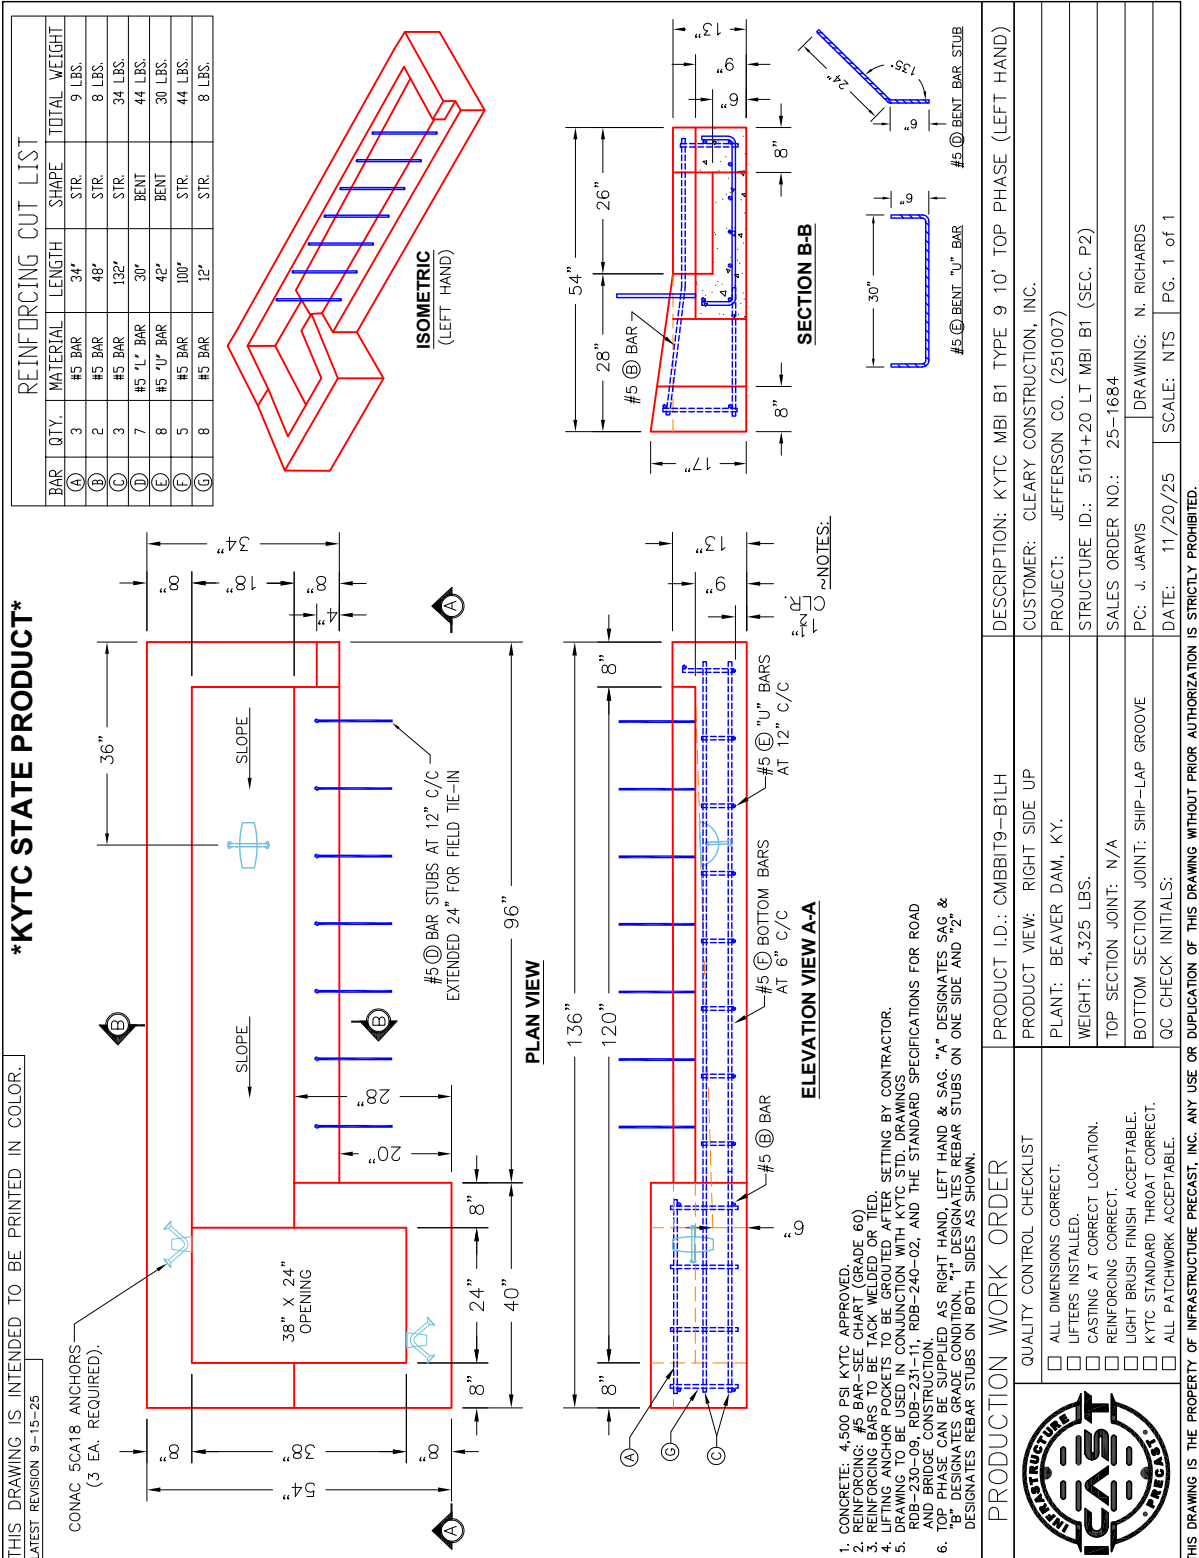

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 17"

Weight (Net): 4000 lb  
Volume (Net): 0cu.yd
