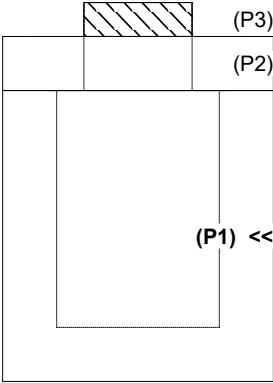
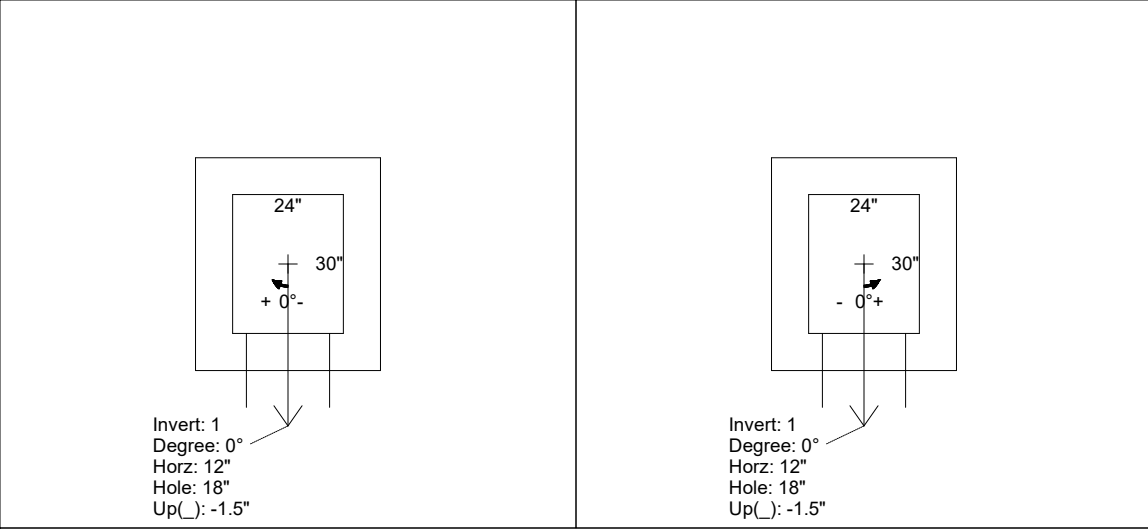
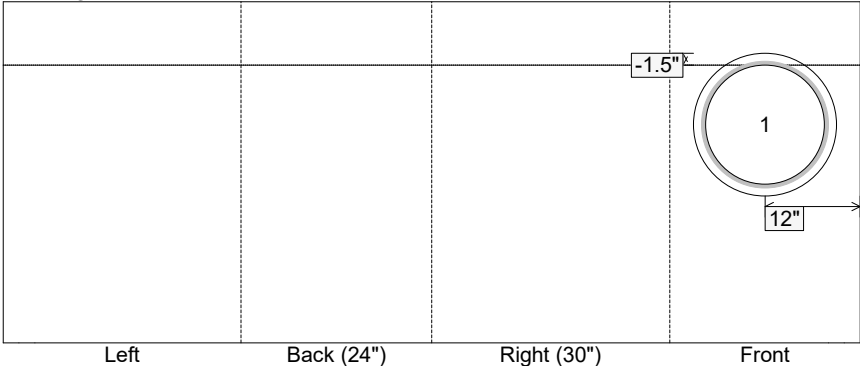



Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:45 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 5102+27 LT DBI-10 MOD											
P1		BX24300808VF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 16" x 28" - CASTING HEIGHT - 5" P2) 24" x 30" - BX FLAT LID 8inW w/16"x28" HOLE - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 35" 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 18"						0 lb 934 lb 4354 lb 0 lb 0 lb ----- 0 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -DBI FRAME & GRATE (BY OTHERS). -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.			
Structure Total: 5288 lb											
Rim: 588.96' Rim to Invert: 4' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	584.96'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 35" Height (Ext): 43"		Weight (Net): 4354 lb Volume (Net): 1.11cu.yd		
